


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
1		Reserve at Lakeland Square	619 days	Mon 5/6/19	Thu 9/16/21	Mon 5/6/19	NA	0%												
2		Owner-Contract	238 days	Tue 8/13/19	Thu 7/9/20	Tue 8/13/19	Thu 7/9/20	100%												
10		Seawood Builders	86 days	Mon 5/6/19	Mon 9/2/19	Mon 5/6/19	Mon 9/2/19	100%												
22		Contract - close HUD	230 days	Mon 8/26/19	Fri 7/10/20	Mon 8/26/19	Fri 7/10/20	100%												
26		Pre-Construction	251 days	Tue 8/6/19	Tue 7/21/20	Tue 8/6/19	NA	0%												
31		Pre-Construction Meeting HUD	1 day	Fri 7/10/20	Fri 7/10/20	Fri 7/10/20	Fri 7/10/20	100%		76										
35		Owner Tasking	332 days	Fri 11/15/19	Mon 2/22/21	NA	NA	0%												
62		Seawood Pre-Construction	1 day	Wed 7/22/20	Wed 7/22/20	NA	NA	0%												
75		Mobilization	35 days	Mon 7/13/20	Fri 8/28/20	NA	NA	0%												
76		Division-01	7 days	Mon 7/13/20	Tue 7/21/20	NA	NA	0%	34,31,32,33	77										
77		Office	7 days	Wed 7/22/20	Thu 7/30/20	NA	NA	0%	76	78										
78		Fencing- Office Compound	7 days	Fri 7/31/20	Mon 8/10/20	NA	NA	0%	77	79										
79		Lay Down Staging area Constructed	7 days	Tue 8/11/20	Wed 8/19/20	NA	NA	0%	78	80										
80		Temporary Utilities- Phone-IT to trailer	7 days	Thu 8/20/20	Fri 8/28/20	NA	NA	0%	79											
81		Procurement	65 days	Tue 7/21/20	Mon 10/19/20	NA	NA	0%												
129		Submittals	335 days	Mon 8/19/19	Fri 11/27/20	Mon 8/19/19	NA	0%												
564		Construction Schedule	301 days	Thu 7/23/20	Thu 9/16/21	NA	NA	0%												
565		Area - 01	264 days	Thu 7/23/20	Tue 7/27/21	NA	NA	0%												
566		Site Work - Site Utilities and MEP Underground	264 days	Thu 7/23/20	Tue 7/27/21	NA	NA	0%												
567		SWPP-	38 days	Thu 7/23/20	Mon 9/14/20	NA	NA	0%												
568		Control Boundary/Wetland- Benchmark	2 days	Thu 7/23/20	Fri 7/24/20	NA	NA	0%	66	569,1103FS+29 d										
569		Clear Silt Fence Line	10 days	Mon 7/27/20	Fri 8/7/20	NA	NA	0%	568	570										
570		SWPP/Roadway/Silt Fence/Boundary	4 days	Mon 8/10/20	Thu 8/13/20	NA	NA	0%	569	571										
571		Clear/Grub Site Area -01	8 days	Fri 8/14/20	Tue 8/25/20	NA	NA	0%	570	572,729										
572		Construction Fence	4 days	Wed 8/26/20	Mon 8/31/20	NA	NA	0%	571	573										
573		Construction Entrance/Road	5 days	Tue 9/1/20	Mon 9/7/20	NA	NA	0%	572	574										
574		Survey-Pond Boundary	5 days	Tue 9/8/20	Mon 9/14/20	NA	NA	0%	573	576										
575		Pond Construction -01	100 days	Tue 9/15/20	Mon 2/1/21	NA	NA	0%												
576		Excavate Pond- Build Berm - 01	10 days	Tue 9/15/20	Mon 9/28/20	NA	NA	0%	574	715,659FS+20 days,665,580,587										
577		Final Dress Slopes and bottom	4 days	Mon 1/25/21	Thu 1/28/21	NA	NA	0%	596,607,585	578										
578		Stabilize Pond-01	2 days	Fri 1/29/21	Mon 2/1/21	NA	NA	0%	577											
579		Retaining Wall -01	27 days	Tue 9/29/20	Wed 11/4/20	NA	NA	0%												
580		Excavate Retaining Wall Foundation -195/f	4 days	Tue 9/29/20	Fri 10/2/20	NA	NA	0%	576	581										
581		Set Rebar	4 days	Mon 10/5/20	Thu 10/8/20	NA	NA	0%	580	582										
582		Inspect Foundation	0 days	Thu 10/8/20	Thu 10/8/20	NA	NA	0%	581	583										
583		Cast Fooundation	3 days	Fri 10/9/20	Tue 10/13/20	NA	NA	0%	582	584										
584		Set CMU	14 days	Wed 10/14/20	Mon 11/2/20	NA	NA	0%	583	585										
585		Grout Bond Beam/Down Cells	2 days	Tue 11/3/20	Wed 11/4/20	NA	NA	0%	584	577,588,599										
586		Pond Construction -02	90 days	Tue 9/29/20	Mon 2/1/21	NA	NA	0%												
587		Excavate Pond- Build Berm - 02	15 days	Tue 9/29/20	Mon 10/19/20	NA	NA	0%	576	715,659FS+20 days,665,598,591										
588		Final Dress Slopes and bottom	4 days	Mon 1/25/21	Thu 1/28/21	NA	NA	0%	596,607,585	589										
589		Stabilize Pond-02	2 days	Fri 1/29/21	Mon 2/1/21	NA	NA	0%	588											
590		Retaining Wall -02	27 days	Tue 10/20/20	Wed 11/25/20	NA	NA	0%												

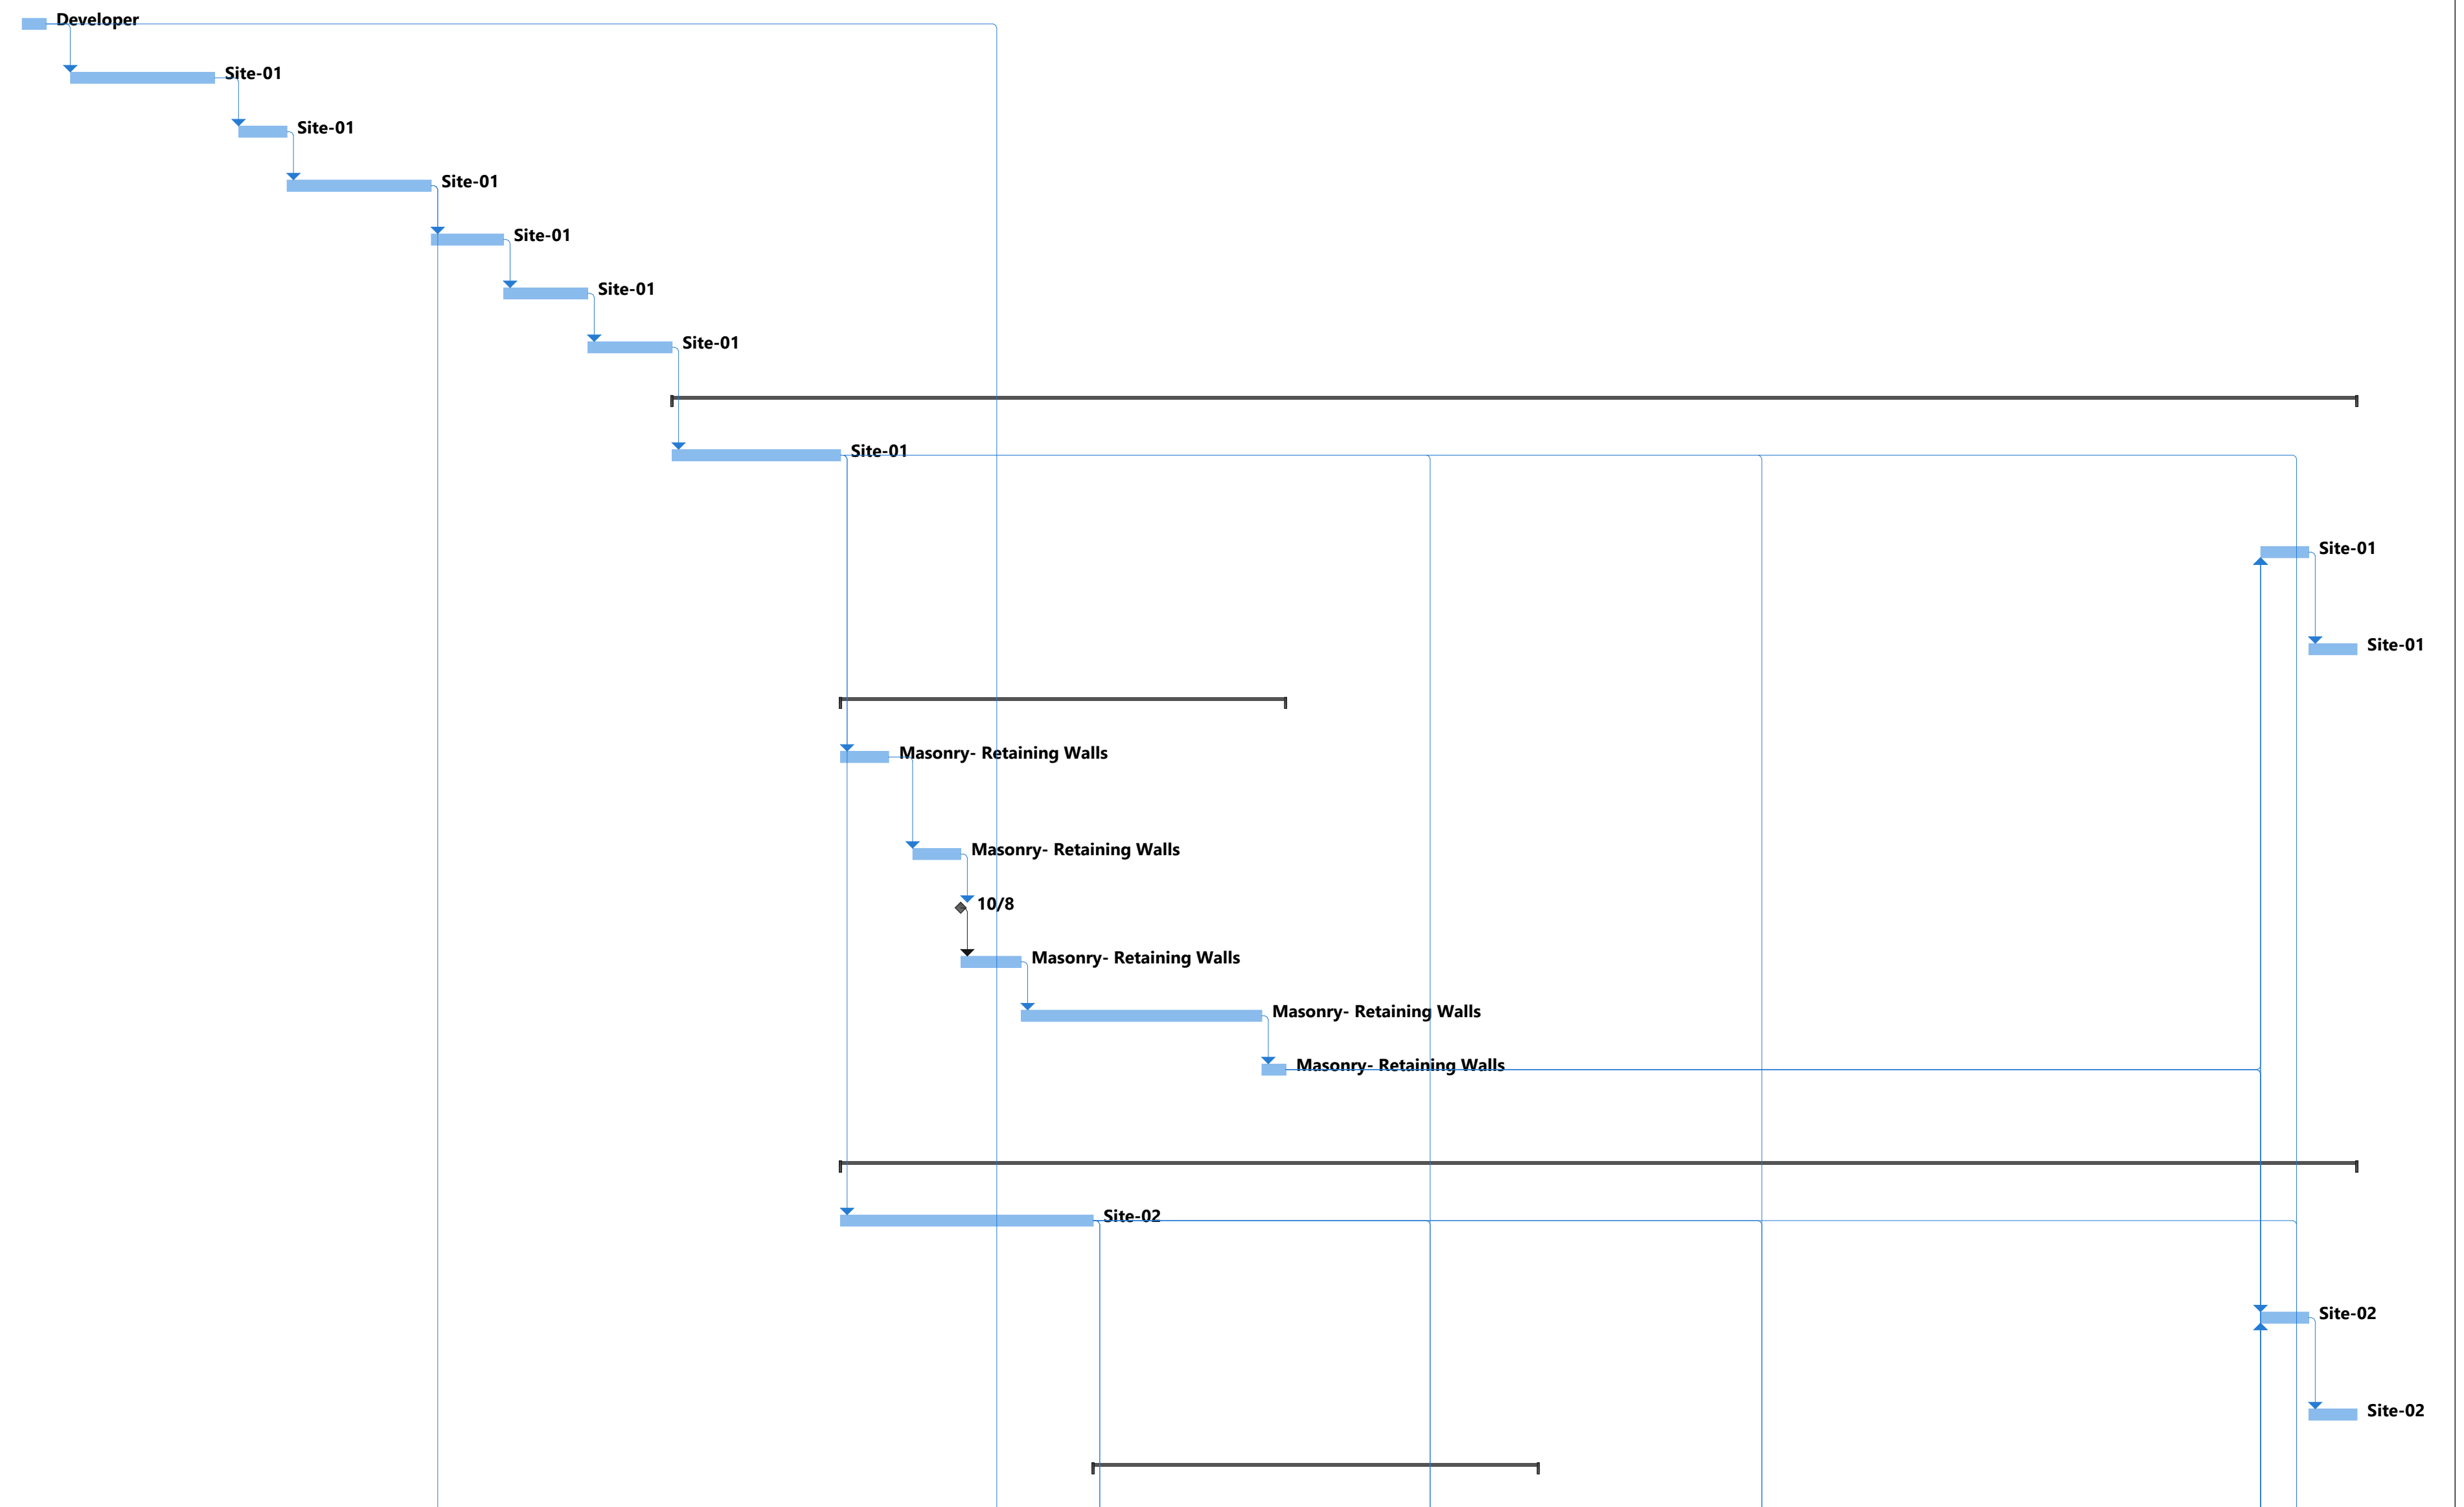


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
591		Excavate Retaining Wall Foundation -194/f	4 days	Tue 10/20/20	Fri 10/23/20	NA	NA	0%	587	592										
592		Set Rebar	4 days	Mon 10/26/20	Thu 10/29/20	NA	NA	0%	591	593										
593		Inspect Foundation	0 days	Thu 10/29/20	Thu 10/29/20	NA	NA	0%	592	594										
594		Cast Fooundation	3 days	Fri 10/30/20	Tue 11/3/20	NA	NA	0%	593	595										
595		Set CMU	14 days	Wed 11/4/20	Mon 11/23/20	NA	NA	0%	594	596,725										
596		Grout Bond Beam/Down Cells	2 days	Tue 11/24/20	Wed 11/25/20	NA	NA	0%	595	577,588,599										
597		Pond Construction -03	75 days	Tue 10/20/20	Mon 2/1/21	NA	NA	0%												
598		Excavate - Build Berm Pond - 03	20 days	Tue 10/20/20	Mon 11/16/20	NA	NA	0%	587	715,659FS+20 days,665,602,692										
599		Final Dress Slopes and bottom	4 days	Mon 1/25/21	Thu 1/28/21	NA	NA	0%	596,607,585	600										
600		Stabilize Pond-03	2 days	Fri 1/29/21	Mon 2/1/21	NA	NA	0%	599											
601		Retaining Wall -03	49 days	Tue 11/17/20	Fri 1/22/21	NA	NA	0%												
602		Excavate Retaining Wall Foundation -645/f	19 days	Tue 11/17/20	Fri 12/11/20	NA	NA	0%	598	603SS+4 days										
603		Set Rebar	15 days	Mon 11/23/20	Fri 12/11/20	NA	NA	0%	602SS+4 days	604SS+4 days										
604		Inspect Foundation	12 days	Fri 11/27/20	Mon 12/14/20	NA	NA	0%	603SS+4 days	605SS										
605		Cast Foundation	12 days	Fri 11/27/20	Mon 12/14/20	NA	NA	0%	604SS	606SS+3 days										
606		Set CMU	32 days	Wed 12/2/20	Thu 1/14/21	NA	NA	0%	605SS+3 days	607										
607		Grout Bond Beam/Down Cells	6 days	Fri 1/15/21	Fri 1/22/21	NA	NA	0%	606	577,588,599,692										
608		Griffin-Deexcel/Excel	108 days	Tue 7/28/20	Thu 12/24/20	NA	NA	0%												
609		Submittals	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%												
610		Polk County- ROW Permit	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82	624										
611		Polk County -DOT Maintenance of traffic Plan approved	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
612		Lane Closure Counts and Frequency	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
613		Proctor/Pit- @ Stabilizer LBR40 min.	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
614		Base Rock- Pit PDOT Certified	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
615		Asphalt Mix Design	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
616		Signage	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
617		Striping	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
618		Concrete Mix Designs	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
619		Curb VDOT Index	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
620		48 hour Lane Closure process established	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%												
621		Communication/Notification	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
622		Frequency-Timing	21 days	Tue 7/28/20	Tue 8/25/20	NA	NA	0%	82											
623		Construction-Off site	26 days	Wed 8/26/20	Wed 9/30/20	NA	NA	0%												
624		Lane Closure Notification East and West Lane at Median	2 days	Wed 8/26/20	Thu 8/27/20	NA	NA	0%	610	655,625,680										
625		MOT Set Western lane	1 day	Fri 8/28/20	Fri 8/28/20	NA	NA	0%	624	626										
626		MOT Set Eastern lane	1 day	Mon 8/31/20	Mon 8/31/20	NA	NA	0%	625	627										
627		Excavate Roadway Media	2 days	Tue 9/1/20	Wed 9/2/20	NA	NA	0%	626	628										
628		Tie-in Stabilizer	2 days	Thu 9/3/20	Fri 9/4/20	NA	NA	0%	627	629										
629		PDOT Inspect/ Soils test	1 day	Mon 9/7/20	Mon 9/7/20	NA	NA	0%	628	630,636										
630		Concrete Curb Install	1 day	Tue 9/8/20	Tue 9/8/20	NA	NA	0%	629	631										
631		Tie-In Base	1 day	Wed 9/9/20	Wed 9/9/20	NA	NA	0%	630	632										
632		Asphalt	1 day	Thu 9/10/20	Thu 9/10/20	NA	NA	0%	631	633,634										
633		Asphalt Cure	14 days	Fri 9/11/20	Wed 9/30/20	NA	NA	0%	632	651										


Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Split Milestone Summary Project Summary Inactive Task Manual Task Duration-only Manual Summary Rollup Manual Summary Start-only Finish-only External Tasks External Milestone Deadline Progress Manual Progress


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
634		Temp stripe	1 day	Fri 9/11/20	Fri 9/11/20	NA	NA	0%	632											
635		Deexcel/Excel Eastern Lane	32 days	Tue 9/8/20	Wed 10/21/20	NA	NA	0%												
636		Lane Closure Notification Eastern Lane	2 days	Tue 9/8/20	Wed 9/9/20	NA	NA	0%	629	638,637										
637		MOT Set	1 day	Thu 9/10/20	Thu 9/10/20	NA	NA	0%	636											
638		Excavate Roadway Media	2 days	Thu 9/10/20	Fri 9/11/20	NA	NA	0%	636	639										
639		Import/Place Backfill	2 days	Mon 9/14/20	Tue 9/15/20	NA	NA	0%	638	640,643										
640		Tie-in Stabilizer	2 days	Wed 9/16/20	Thu 9/17/20	NA	NA	0%	639	641										
641		PDOT Inspect/ Soils test	1 day	Fri 9/18/20	Fri 9/18/20	NA	NA	0%	640	642										
642		Concrete Curb Install	3 days	Mon 9/21/20	Wed 9/23/20	NA	NA	0%	641	646										
643		Form and Place Sidewalk to ADA	4 days	Wed 9/16/20	Mon 9/21/20	NA	NA	0%	639	644										
644		Install Bollards @Meter Assembly Pad	2 days	Tue 9/22/20	Wed 9/23/20	NA	NA	0%	643	645										
645		Form and Place Concrete Pad @Meter Assembly Sheet 12 details	2 days	Thu 9/24/20	Fri 9/25/20	NA	NA	0%	644											
646		Tie-In Base	2 days	Thu 9/24/20	Fri 9/25/20	NA	NA	0%	642	647										
647		Asphalt	1 day	Mon 9/28/20	Mon 9/28/20	NA	NA	0%	646	648,649,653										
648		Asphalt Cure	14 days	Tue 9/29/20	Fri 10/16/20	NA	NA	0%	647	651										
649		Temp stripe	1 day	Tue 9/29/20	Tue 9/29/20	NA	NA	0%	647	650										
650		Install Entry Signage	1 day	Wed 9/30/20	Wed 9/30/20	NA	NA	0%	649											
651		Final Striping Median Griffin	2 days	Mon 10/19/20	Tue 10/20/20	NA	NA	0%	633,648	652										
652		De-Mobilize MOT Off Site- Re-install MOT Entry	1 day	Wed 10/21/20	Wed 10/21/20	NA	NA	0%	651											
653		Re-Install Entry- Rubble/Rumble at Temp Entrance	2 days	Tue 9/29/20	Wed 9/30/20	NA	NA	0%	647											
654		Data/Telephone- Entry-Griffin	33 days	Tue 11/10/20	Thu 12/24/20	NA	NA	0%												
655		ATT/Cable Provider Extend Service Lateral Across Griffin	5 days	Tue 11/10/20	Mon 11/16/20	NA	NA	0%	624,48	656,49										
656		Extend Service lateral Into Site	14 days	Tue 11/17/20	Fri 12/4/20	NA	NA	0%	655	657										
657		Extend Site conduit to each Bldg.	14 days	Mon 12/7/20	Thu 12/24/20	NA	NA	0%	656											
658		Retaining Wall	78 days	Mon 12/14/20	Thu 4/1/21	NA	NA	0%												
659		Retaining Wall Foundation Complete- See Note Cut Details Sheet 20	0 days	Mon 12/14/20	Mon 12/14/20	NA	NA	0%	46,576FS+20 days,587FS+20 days,598FS+20 days	660										
660		Station 13+58 to Sta. 22+71 -CMU	14 days	Tue 12/15/20	Fri 1/1/21	NA	NA	0%	659	661,674,675										
661		Station 22+71 to 23+00 begin roadway (Segmented Modular with fence (Pool)	30 days	Mon 1/4/21	Fri 2/12/21	NA	NA	0%	660	662,676										
662		Station 22+62 both sides Roadway to Station 25 End Ret Roadway- CMU	30 days	Mon 2/15/21	Fri 3/26/21	NA	NA	0%	661	663,677										
663		Install Guard Railing Roadway	4 days	Mon 3/29/21	Thu 4/1/21	NA	NA	0%	662											
664		Site Earthwork	98 days	Tue 11/17/20	Thu 4/1/21	NA	NA	0%												
665		Import Clubhouse- Through Bldg. Pad.	12 days	Tue 11/17/20	Wed 12/2/20	NA	NA	0%	576,587,598	666										
666		Import Apartment -01- Through Bldg. Pad	12 days	Thu 12/3/20	Fri 12/18/20	NA	NA	0%	665	667										
667		Bldg. Pad set -AP-01	2 days	Mon 12/21/20	Tue 12/22/20	NA	NA	0%	666	668,926										
668		Bldg. Pad Set CH-01	2 days	Wed 12/23/20	Thu 12/24/20	NA	NA	0%	667	669,817,873,670										
669		Relocate Pool Borrow	2 days	Fri 12/25/20	Mon 12/28/20	NA	NA	0%	668	671										
670		Build Parking through Retaining Walls to Stabilizer Parking	10 days	Fri 12/25/20	Thu 1/7/21	NA	NA	0%	668	671,753										
671		Build Roadway Through Stabilized Subgrade	10 days	Fri 1/8/21	Thu 1/21/21	NA	NA	0%	669,670	672										
672		Build Compactor Roadway Bldg. Pad through Stabilizer	5 days	Fri 1/22/21	Thu 1/28/21	NA	NA	0%	671	673										
673		Build Maintenance Bldg. Pad	2 days	Fri 1/29/21	Mon 2/1/21	NA	NA	0%	672	873										
674		Backfill- Retaining Walls-	64 days	Mon 1/4/21	Thu 4/1/21	NA	NA	0%	660											

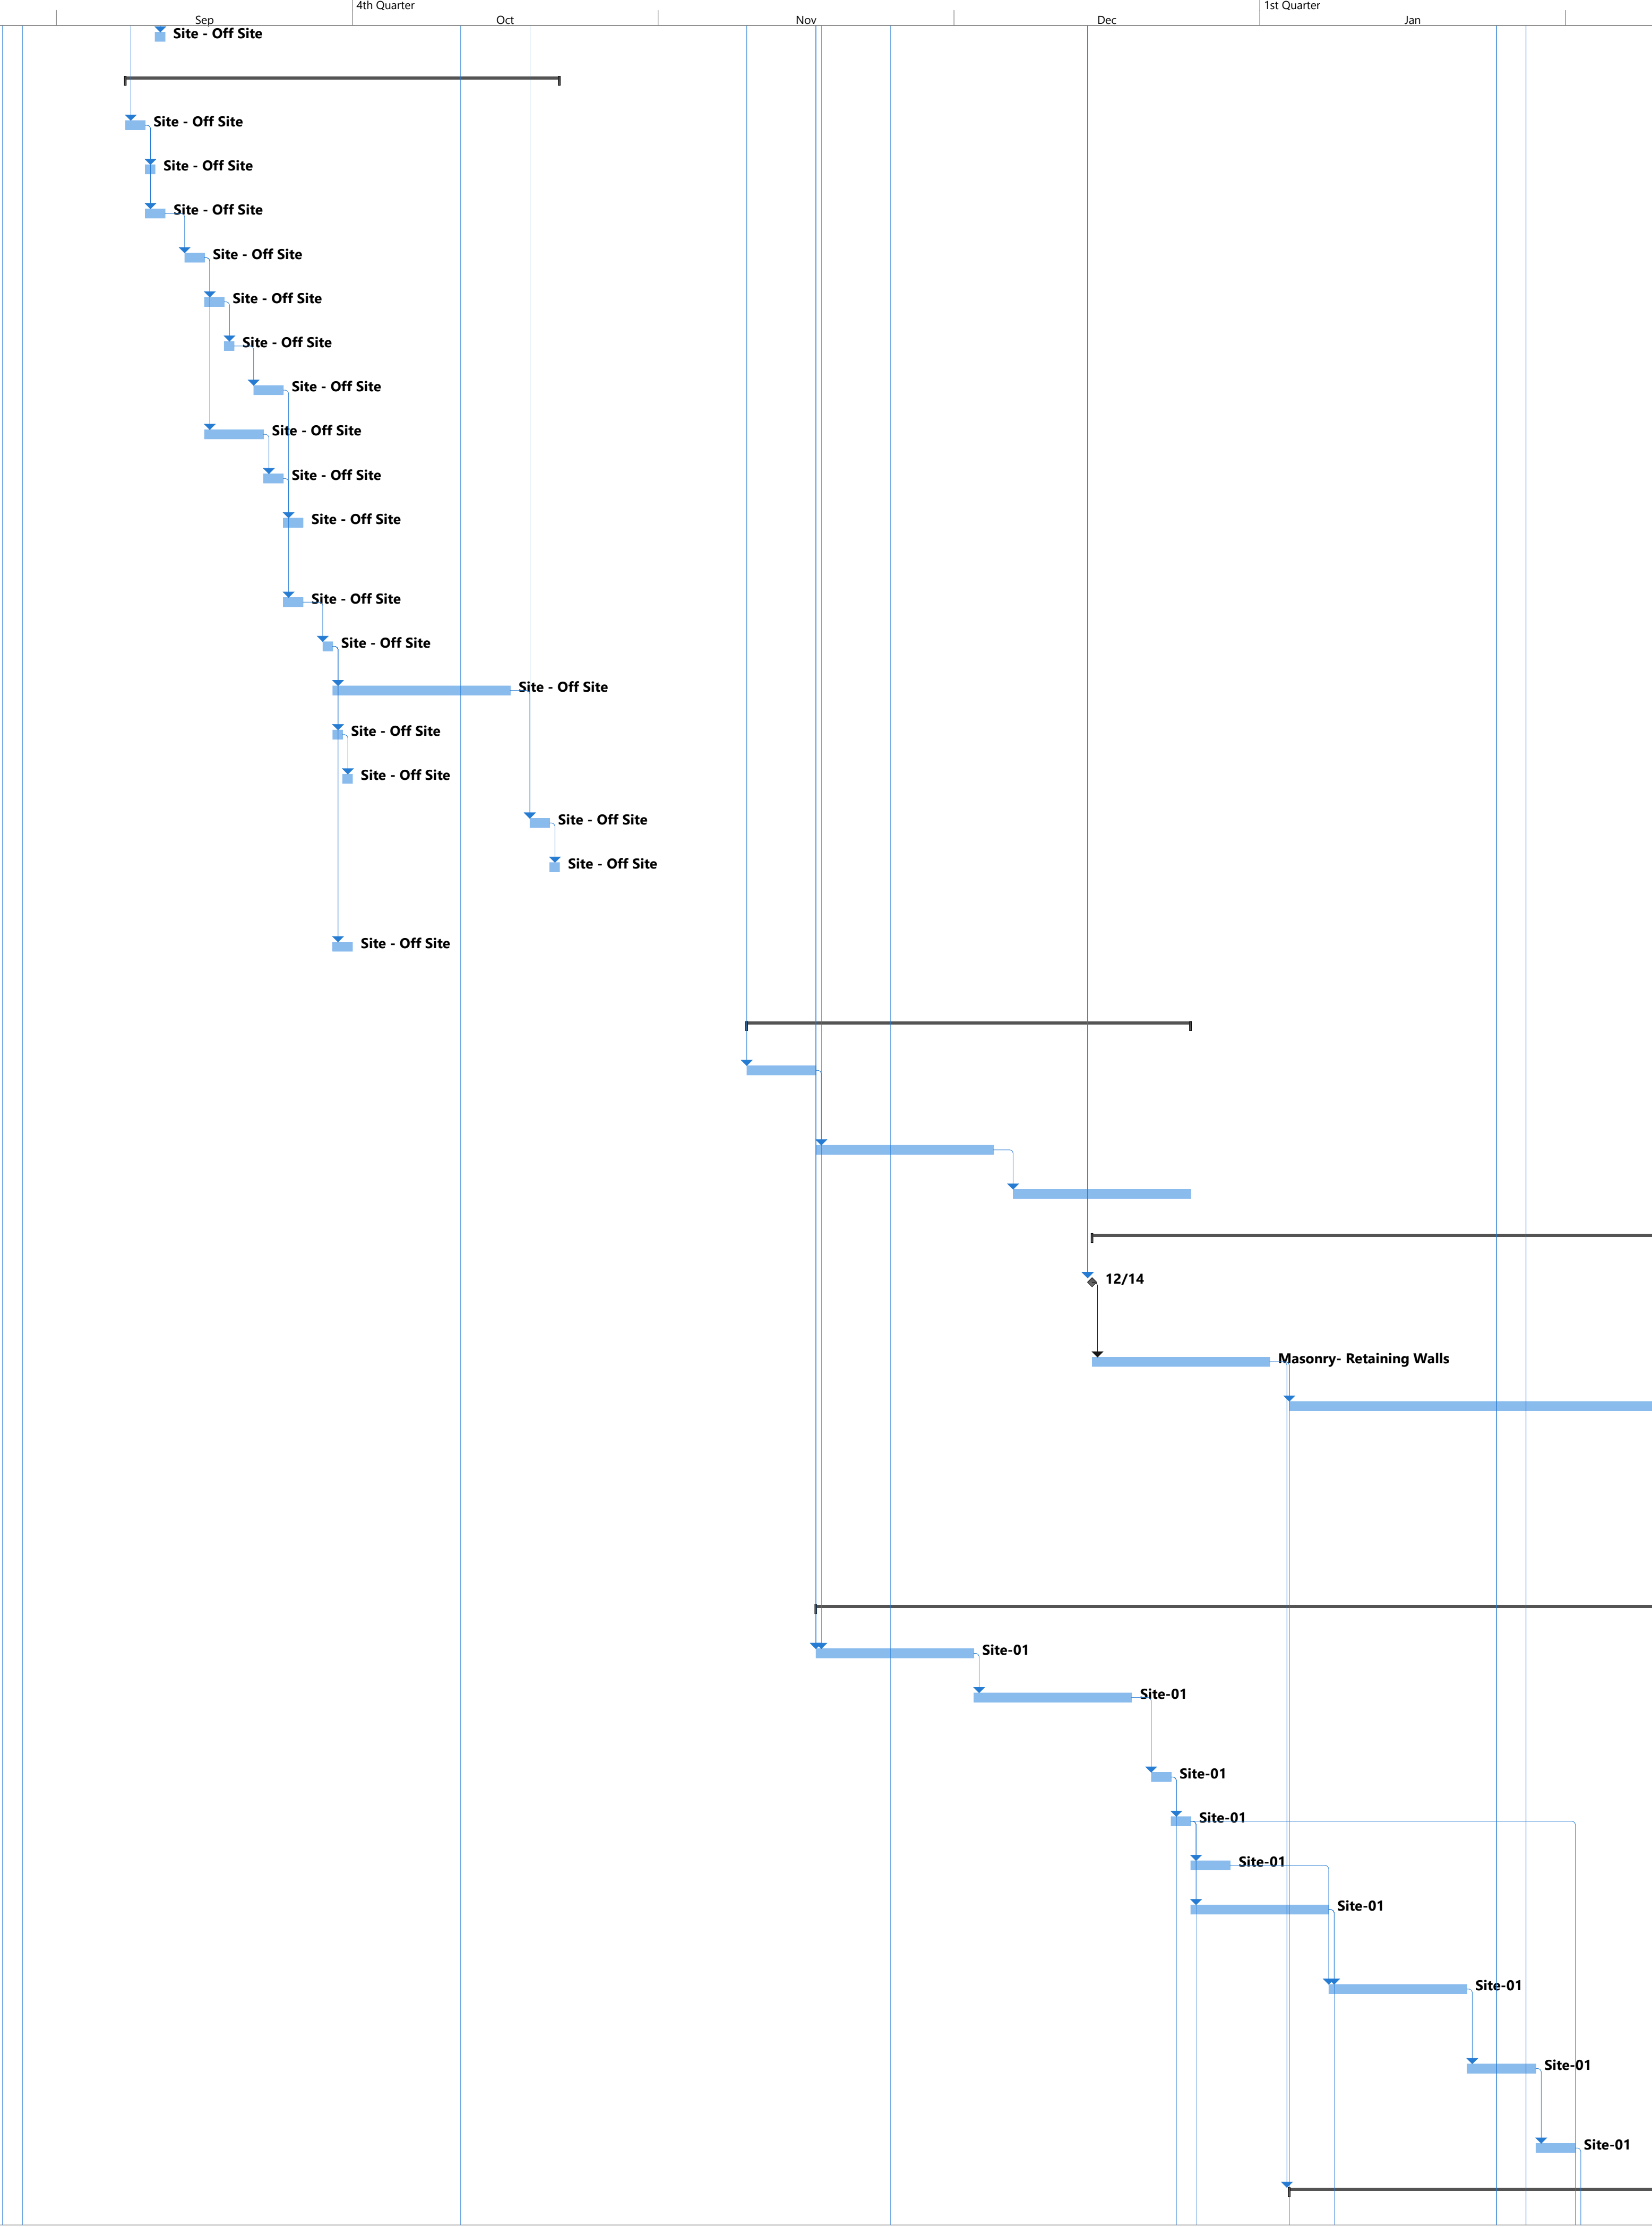


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter			
											Jul	Aug	Sep	Oct	Nov	Dec	Jan			
675		Station 13+58 to Sta. 22+71 -CMU	4 days	Mon 1/4/21	Thu 1/7/21	NA	NA	0%	660											
676		Station 22+71 to 23+00 begin roadway (Segmented Modular with fence (Pool))	4 days	Mon 2/15/21	Thu 2/18/21	NA	NA	0%	661											
677		Station 22+62 both sides Roadway to Station 25 End Ret Roadway- CMU	4 days	Mon 3/29/21	Thu 4/1/21	NA	NA	0%	662											
678		Site Utilities- Area-01	133 days	Wed 8/26/20	Fri 2/26/21	NA	NA	0%												
679		Off Site/Griffin	21 days	Fri 8/28/20	Fri 9/25/20	NA	NA	0%												
680		Set MOT Griffin at Jack Pit	1 day	Fri 8/28/20	Fri 8/28/20	NA	NA	0%	624	681										
681		Jack and Bore Griffin	3 days	Mon 8/31/20	Wed 9/2/20	NA	NA	0%	680	682SS+1 day										
682		Tap w/ Restraint and Valve East Side	2 days	Tue 9/1/20	Wed 9/2/20	NA	NA	0%	681SS+1 day	684,683										
683		Test Service/Pressure/Leaks	0 days	Wed 9/2/20	Wed 9/2/20	NA	NA	0%	682											
684		Extend 8" with restraints	6 days	Thu 9/3/20	Thu 9/10/20	NA	NA	0%	682	685,686										
685		Test Service/Pressure/Leaks	6 days	Fri 9/11/20	Fri 9/18/20	NA	NA	0%	684											
686		Inspect/Backfill	7 days	Fri 9/11/20	Mon 9/21/20	NA	NA	0%	684	687										
687		Split 8" at Meter assembly to Fire/Water	2 days	Tue 9/22/20	Wed 9/23/20	NA	NA	0%	686	688										
688		Set BFP Fire / Water	2 days	Thu 9/24/20	Fri 9/25/20	NA	NA	0%	687	689										
689		Extend Water/Fire into Site	0 days	Fri 9/25/20	Fri 9/25/20	NA	NA	0%	688	710,711										
690		On Site-Area-01 Utility	133 days	Wed 8/26/20	Fri 2/26/21	NA	NA	0%												
691		Lift station -02	13 days	Mon 1/25/21	Wed 2/10/21	NA	NA	0%												
692		Excavation- Set Dewatering to Pond 02	3 days	Mon 1/25/21	Wed 1/27/21	NA	NA	0%	598,607	693,715										
693		Set Pre-Cast	1 day	Thu 1/28/21	Thu 1/28/21	NA	NA	0%	692	694										
694		Backfill- 12" Lifts	1 day	Fri 1/29/21	Fri 1/29/21	NA	NA	0%	693	695										
695		Test Lifts	1 day	Mon 2/1/21	Mon 2/1/21	NA	NA	0%	694	696										
696		Tie-in FM Invert	1 day	Tue 2/2/21	Tue 2/2/21	NA	NA	0%	695	697,702										
697		Tie-in SS Gravity- Clubhouse at wye- Establish Elevation- CH	1 day	Wed 2/3/21	Wed 2/3/21	NA	NA	0%	696	698,708										
698		Tie-in SS Gravity @ Wye- Establish Elevation - Ap-01	1 day	Thu 2/4/21	Thu 2/4/21	NA	NA	0%	697	699,707										
699		Set Pumps	2 days	Fri 2/5/21	Mon 2/8/21	NA	NA	0%	698	700										
700		Set Control Panels	2 days	Tue 2/9/21	Wed 2/10/21	NA	NA	0%	699											
701		Force main to SHM-01	16 days	Wed 2/3/21	Wed 2/24/21	NA	NA	0%												
702		Extend FM to MH-SMH-01- 900 I/f	13 days	Wed 2/3/21	Fri 2/19/21	NA	NA	0%	696	703,705										
703		Check Elevation-Conflict/Crossing	1 day	Mon 2/22/21	Mon 2/22/21	NA	NA	0%	702	704										
704		Set MH end of run- With Tie-in	2 days	Tue 2/23/21	Wed 2/24/21	NA	NA	0%	703											
705		Test Pressure-Leaks	0 days	Fri 2/19/21	Fri 2/19/21	NA	NA	0%	702											
706		Sanitary Gravity	5 days	Thu 2/4/21	Wed 2/10/21	NA	NA	0%												
707		SS Gravity-Ap-01	4 days	Fri 2/5/21	Wed 2/10/21	NA	NA	0%	698											
708		SS Gravity- AP-CH	2 days	Thu 2/4/21	Fri 2/5/21	NA	NA	0%	697											
709		Water & Fire Main	2 days	Mon 9/28/20	Tue 9/29/20	NA	NA	0%												
710		Extend Water to Clubhouse-5' out	2 days	Mon 9/28/20	Tue 9/29/20	NA	NA	0%	689											
711		Extend Fire with FDC- Hydrant to CH	2 days	Mon 9/28/20	Tue 9/29/20	NA	NA	0%	689	712										
712		Test Pressure-Leaks	0 days	Tue 9/29/20	Tue 9/29/20	NA	NA	0%	711											
713		Storm Sewer	133 days	Wed 8/26/20	Fri 2/26/21	NA	NA	0%												
714		Survey- Control elevations Set	2 days	Thu 1/28/21	Fri 1/29/21	NA	NA	0%	715SS	716										

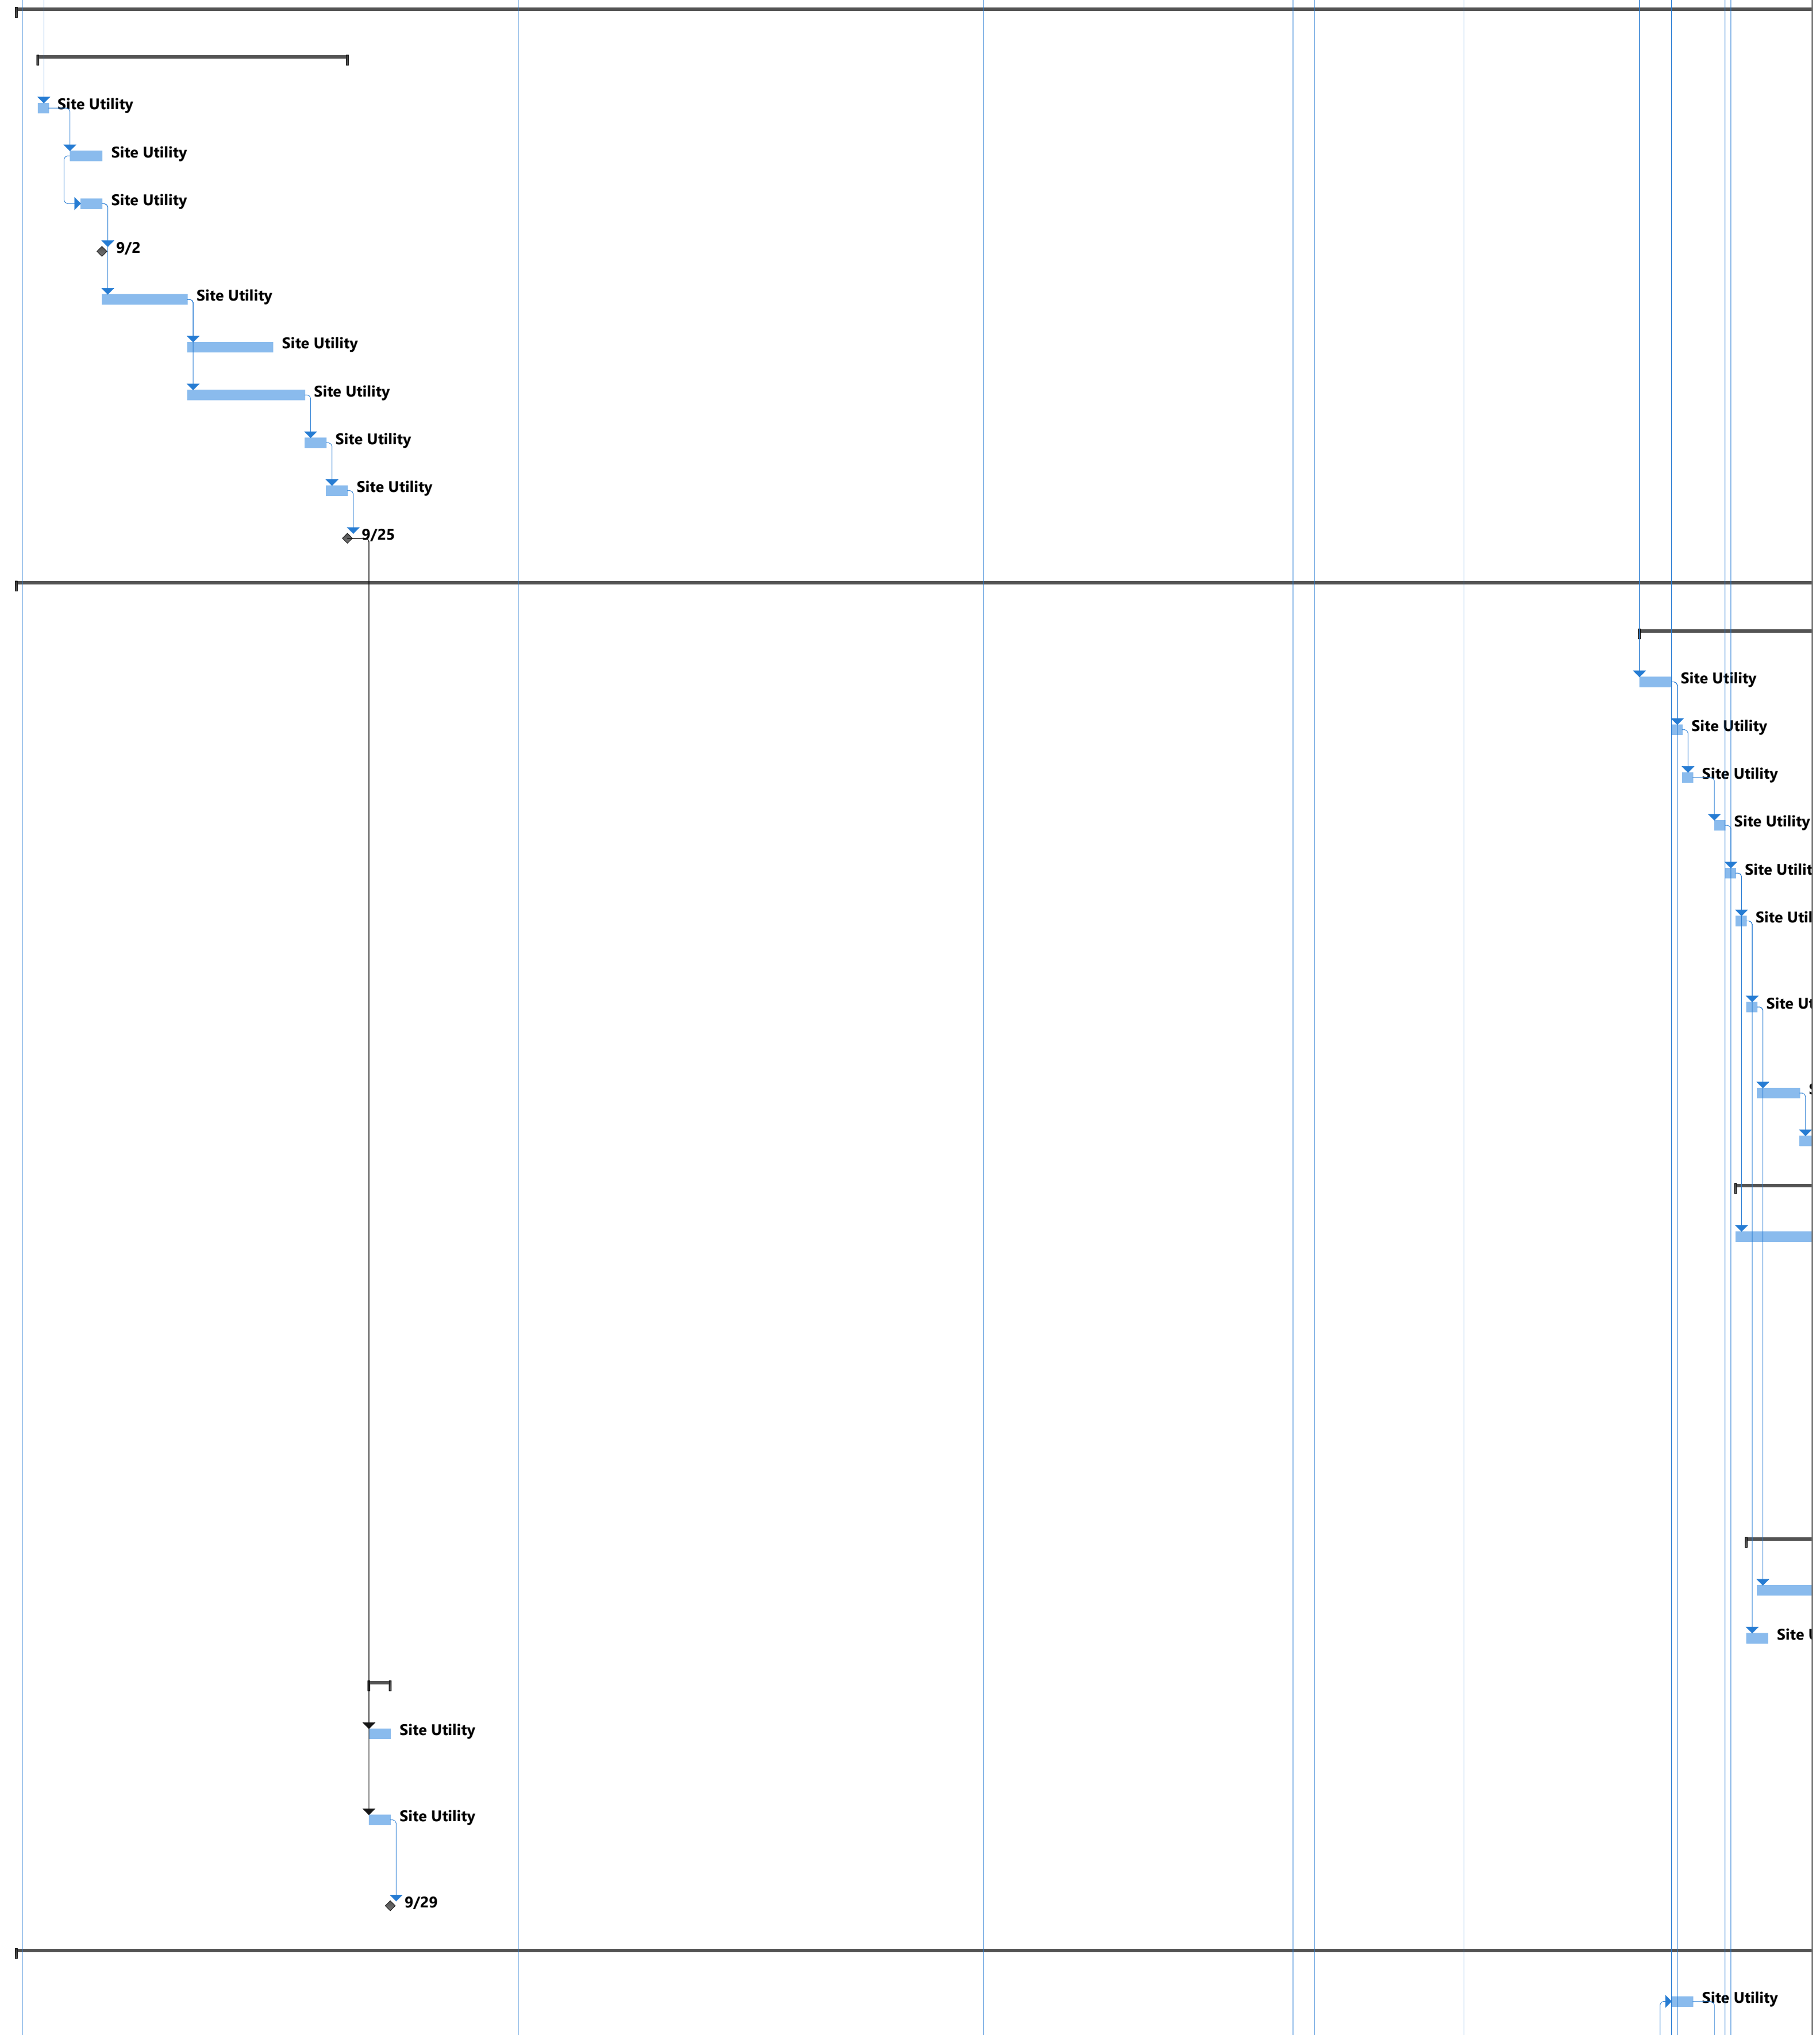


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
715		CS-1- through Pond-01 Mitered End- (Discharge Wetland) See SWPP	3 days	Thu 1/28/21	Mon 2/1/21	NA	NA	0%	576,587,598,692	71455										
716		DBI-18A- With mitered End Pond-01	2 days	Mon 2/1/21	Tue 2/2/21	NA	NA	0%	714	717										
717		DBI-18-AP-01	3 days	Wed 2/3/21	Fri 2/5/21	NA	NA	0%	716	718										
718		DMH-17B-AP-01	3 days	Mon 2/8/21	Wed 2/10/21	NA	NA	0%	717	720,719										
719		Survey Control- Verify Elevation Placed	2 days	Thu 2/11/21	Fri 2/12/21	NA	NA	0%	718											
720		DBI-17	3 days	Thu 2/11/21	Mon 2/15/21	NA	NA	0%	718	721										
721		DBI-17A	3 days	Tue 2/16/21	Thu 2/18/21	NA	NA	0%	720	722										
722		FES-1-1	2 days	Fri 2/19/21	Mon 2/22/21	NA	NA	0%	721	723										
723		FES 1-4	2 days	Tue 2/23/21	Wed 2/24/21	NA	NA	0%	722	724										
724		FES-1-5	2 days	Thu 2/25/21	Fri 2/26/21	NA	NA	0%	723											
725		FES 16- Mitered End to Pond -02	2 days	Tue 11/24/20	Wed 11/25/20	NA	NA	0%	595	726										
726		FES 16A- Mitered End to Pond -02	2 days	Thu 11/26/20	Fri 11/27/20	NA	NA	0%	725	727										
727		Survey Control- Verify Elevation Placed- FES 16- Pond J2	2 days	Mon 11/30/20	Tue 12/1/20	NA	NA	0%	726											
728		Headwall	39 days	Wed 8/26/20	Mon 10/19/20	NA	NA	0%												
729		Temp Dike Head Side	3 days	Wed 8/26/20	Fri 8/28/20	NA	NA	0%	571	730										
730		Excavate elevate. +/- 190	2 days	Mon 8/31/20	Tue 9/1/20	NA	NA	0%	729	731										
731		Dewater	2 days	Wed 9/2/20	Thu 9/3/20	NA	NA	0%	730	733,732										
732		Set GEO Fabric -See sheet 21 CC-10	1 day	Fri 9/4/20	Fri 9/4/20	NA	NA	0%	731											
733		Form Foundation return Slab-	2 days	Fri 9/4/20	Mon 9/7/20	NA	NA	0%	731	734										
734		Bar-	1 day	Tue 9/8/20	Tue 9/8/20	NA	NA	0%	733	735										
735		Inspect	1 day	Wed 9/9/20	Wed 9/9/20	NA	NA	0%	734	736										
736		Cast Slab	1 day	Thu 9/10/20	Thu 9/10/20	NA	NA	0%	735	737										
737		Place 12" #57 stone bed	1 day	Fri 9/11/20	Fri 9/11/20	NA	NA	0%	736	738										
738		Set Double Barrell 60"	2 days	Mon 9/14/20	Tue 9/15/20	NA	NA	0%	737	739										
739		Form Headwall Face	5 days	Wed 9/16/20	Tue 9/22/20	NA	NA	0%	738	740										
740		Bar-	2 days	Wed 9/23/20	Thu 9/24/20	NA	NA	0%	739	741										
741		Inspect	1 day	Fri 9/25/20	Fri 9/25/20	NA	NA	0%	740	742										
742		Cast	1 day	Mon 9/28/20	Mon 9/28/20	NA	NA	0%	741	743										
743		Form Wingwall Left to Right	3 days	Tue 9/29/20	Thu 10/1/20	NA	NA	0%	742	744										
744		Bar-	2 days	Fri 10/2/20	Mon 10/5/20	NA	NA	0%	743	745										
745		Inspect	1 day	Tue 10/6/20	Tue 10/6/20	NA	NA	0%	744	746										
746		Cast	1 day	Wed 10/7/20	Wed 10/7/20	NA	NA	0%	745	747										
747		Backfill D-60" 12" Lift	2 days	Thu 10/8/20	Fri 10/9/20	NA	NA	0%	746	748,1103										
748		Remove de-watering	1 day	Mon 10/12/20	Mon 10/12/20	NA	NA	0%	747	749,1117										
749		Place RIP Rap each end	2 days	Tue 10/13/20	Wed 10/14/20	NA	NA	0%	748	750,765										
750		Set Rail- Guard Type	3 days	Thu 10/15/20	Mon 10/19/20	NA	NA	0%	749											
751		Roadway Paving	60 days	Fri 1/8/21	Thu 4/1/21	NA	NA	0%												
752		Roadway and Parking Area-01	60 days	Fri 1/8/21	Thu 4/1/21	NA	NA	0%												
753		Subgrade\Lime rock - Parking Lots	14 days	Fri 1/8/21	Wed 1/27/21	NA	NA	0%	670	754,803,794										
754		Install Curbing	4 days	Thu 1/28/21	Tue 2/2/21	NA	NA	0%	753	75555+1 day,756										
755		Sidewalks	15 days	Fri 1/29/21	Thu 2/18/21	NA	NA	0%	75455+1 day	799										
756		Stabilize Subgrade at Entrance and Install P	10 days	Wed 2/3/21	Tue 2/16/21	NA	NA	0%	754	757										
757		Base with tack	12 days	Wed 2/17/21	Thu 3/4/21	NA	NA	0%	756	758										
758		Asphalt Placement	7 days	Fri 3/5/21	Mon 3/15/21	NA	NA	0%	757	75955+14 days,75										

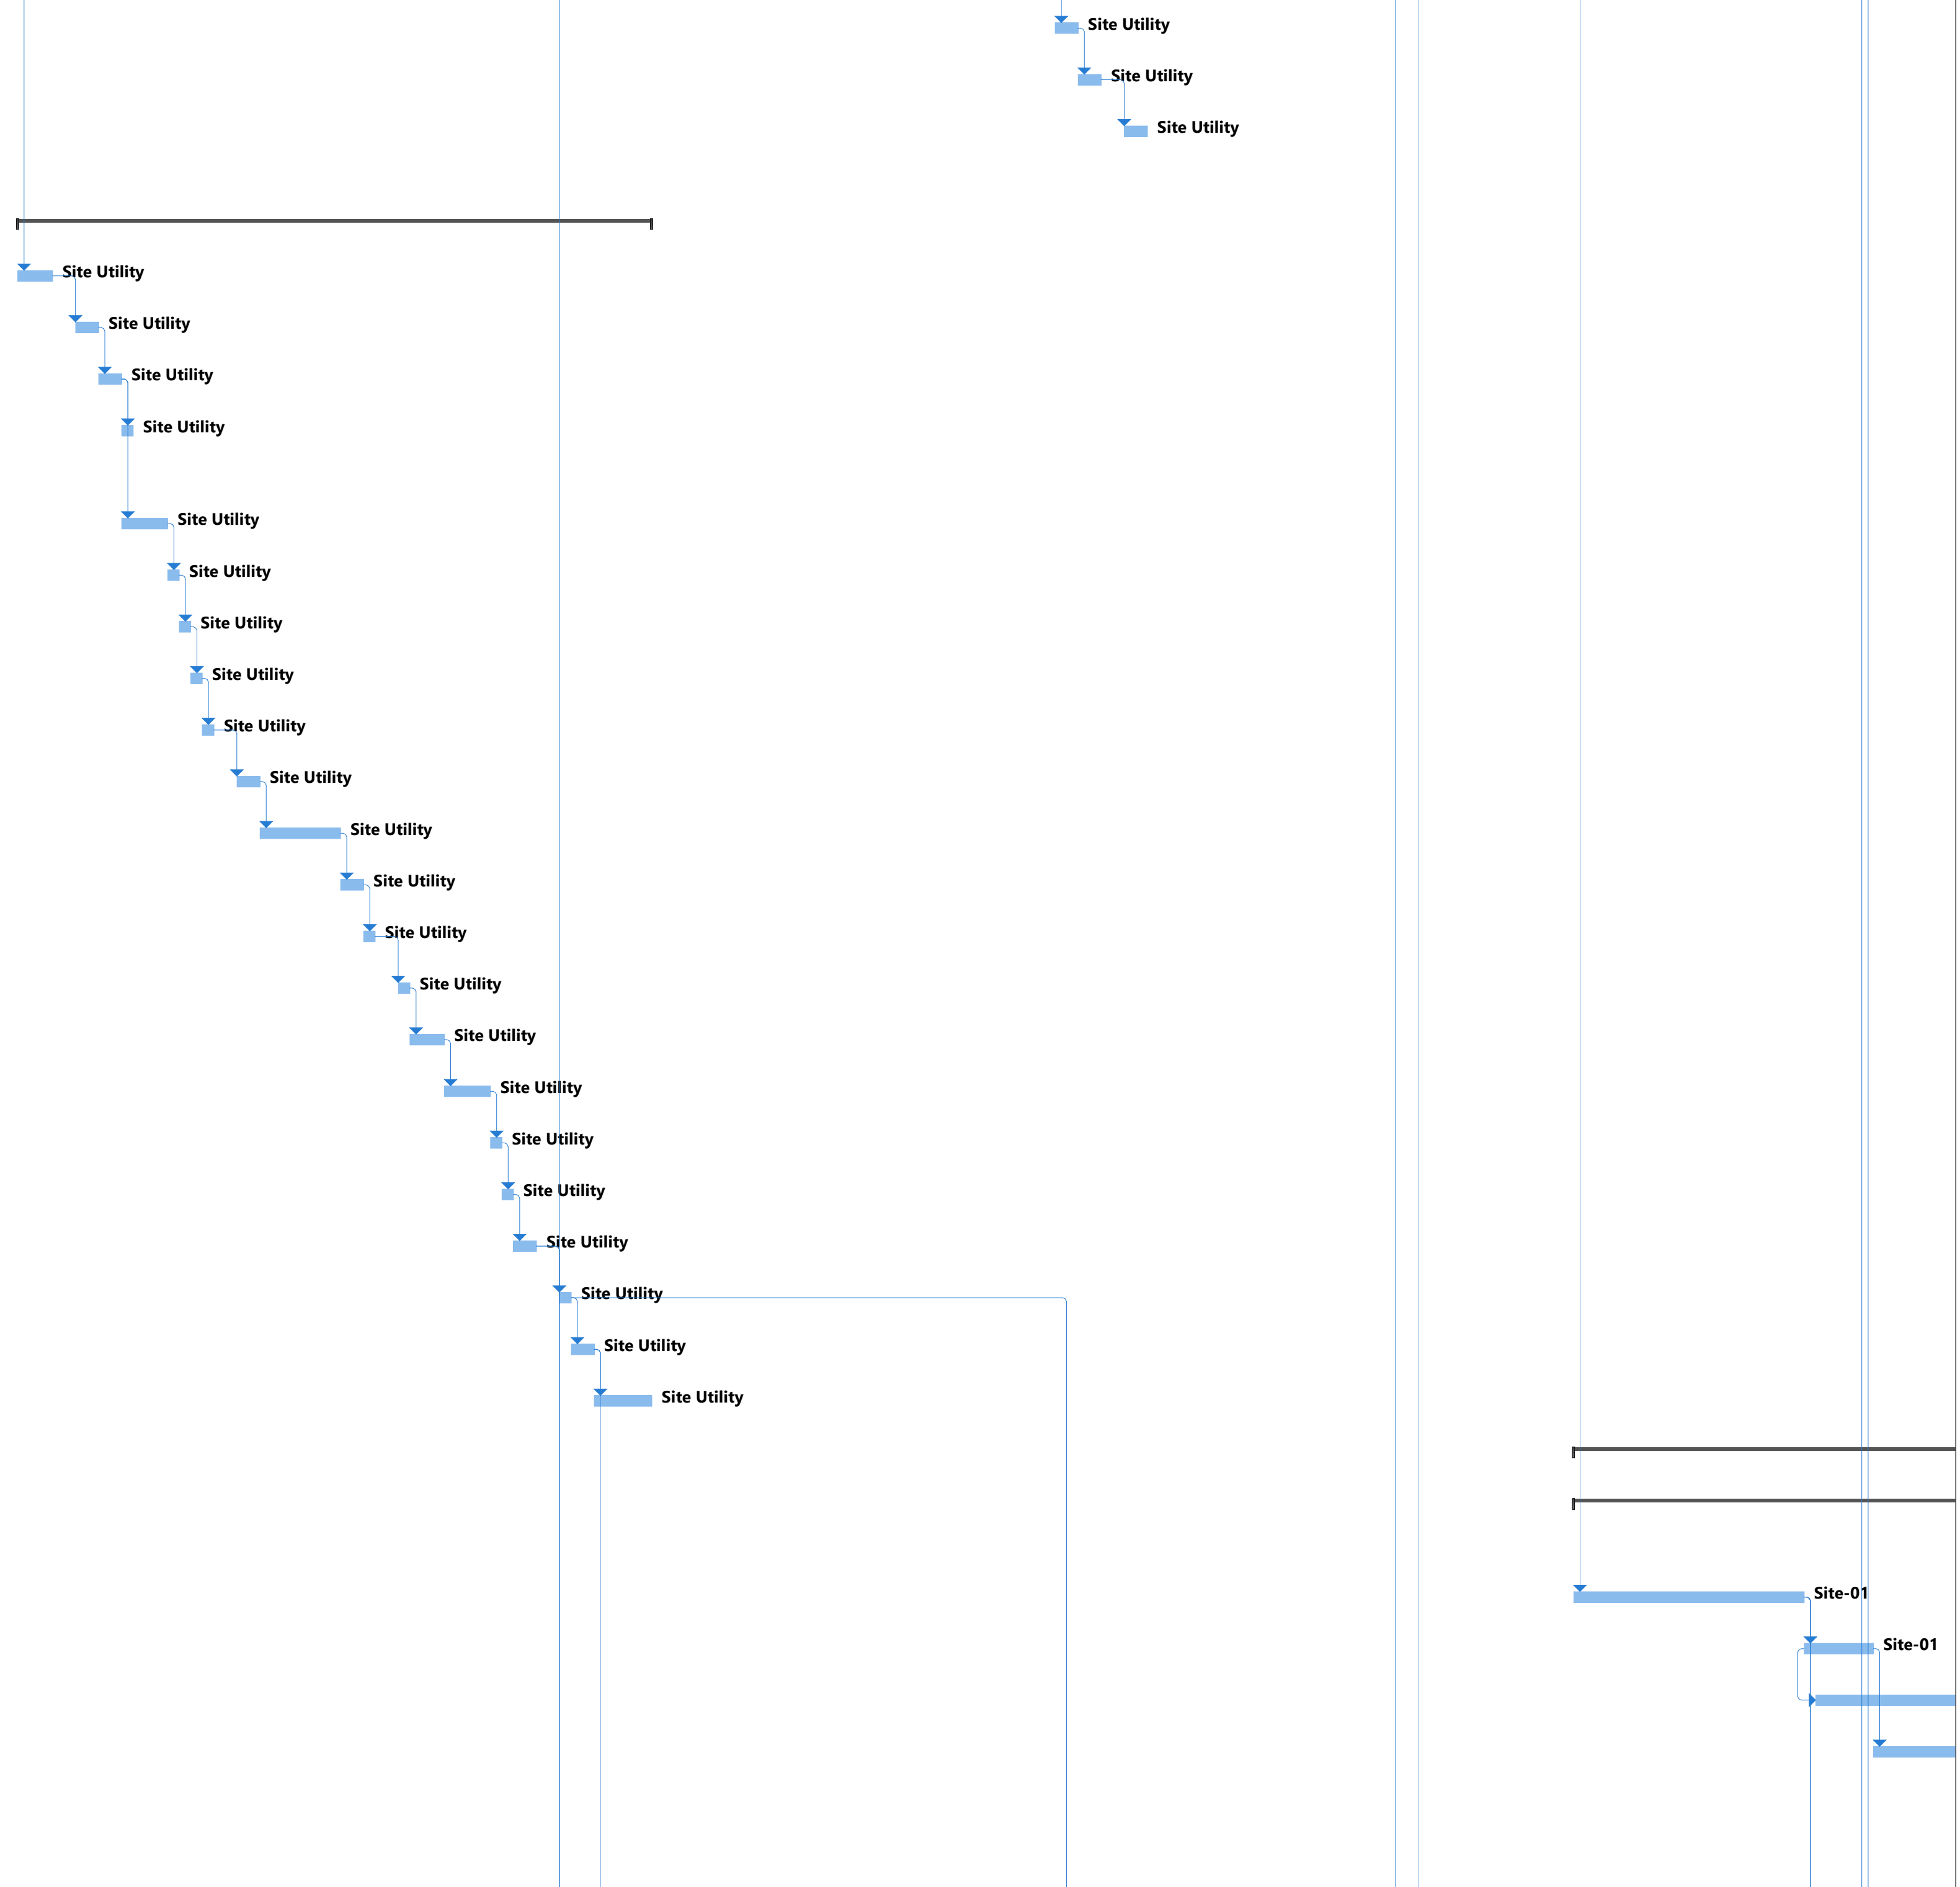

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
759	Task	Striping and Signage & Wheel Stops	6 days	Thu 3/25/21	Thu 4/1/21	NA	NA	0%	758SS+14 days	795										
760	Task	Boardwalk	53 days	Thu 10/15/20	Mon 12/28/20	NA	NA	0%												
761	Task	Design-Boardwalk- Complete by EOR-A/E	0 days	Thu 10/15/20	Thu 10/15/20	NA	NA	0%	39FS+48 days	762										
762	Task	Special Permit - City of Lakeland	0 days	Thu 10/15/20	Thu 10/15/20	NA	NA	0%	761	763										
763	Task	Survey Boundary-wetland	2 days	Fri 10/16/20	Mon 10/19/20	NA	NA	0%	762											
764	Task	Piles	14 days	Thu 10/15/20	Tue 11/3/20	NA	NA	0%												
765	Task	Pile Placement- Jet/Drive (average 16')	14 days	Thu 10/15/20	Tue 11/3/20	NA	NA	0%	749	766SS+4 days										
766	Task	Boardwalk Frame	11 days	Wed 10/21/20	Wed 11/4/20	NA	NA	0%	765SS+4 days	767SS+5 days										
767	Task	Boardwalk Deck	12 days	Wed 10/28/20	Thu 11/12/20	NA	NA	0%	766SS+5 days	768										
768	Task	Boardwalk Railing	32 days	Fri 11/13/20	Mon 12/28/20	NA	NA	0%	767											
769	Task	Pool	47 days	Mon 11/30/20	Tue 2/2/21	NA	NA	0%												
770	Task	Pool - Excavate and Rough In	12 days	Mon 11/30/20	Tue 12/15/20	NA	NA	0%	367	771,784										
771	Task	Inspections - Rough	0 days	Tue 12/15/20	Tue 12/15/20	NA	NA	0%	770	772										
772	Task	Pool - Shoot Shell	2 days	Wed 12/16/20	Thu 12/17/20	NA	NA	0%	771	773,778										
773	Task	Set Pool Coping	3 days	Fri 12/18/20	Tue 12/22/20	NA	NA	0%	772	774										
774	Task	Pool Cure Time	14 days	Wed 12/23/20	Mon 1/11/21	NA	NA	0%	773	775										
775	Task	Prep Pool and Diamond Bright	3 days	Tue 1/12/21	Thu 1/14/21	NA	NA	0%	774	776,780										
776	Task	Pool Deck Rough In	1 day	Fri 1/15/21	Fri 1/15/21	NA	NA	0%	775	777										
777	Task	Planter F/R/P and Waterproof	2 days	Mon 1/18/21	Tue 1/19/21	NA	NA	0%	776											
778	Task	Irrigation Rough	3 days	Fri 12/18/20	Tue 12/22/20	NA	NA	0%	772	779										
779	Task	Install Pool Deck Pavers	6 days	Wed 12/23/20	Wed 12/30/20	NA	NA	0%	778	785										
780	Task	Waterline Tile	3 days	Fri 1/15/21	Tue 1/19/21	NA	NA	0%	775	782,781										
781	Task	Extend Electrical Serv ice Equipment	2 days	Wed 1/20/21	Thu 1/21/21	NA	NA	0%	780											
782	Task	Set Pool Equipment	2 days	Wed 1/20/21	Thu 1/21/21	NA	NA	0%	780	783										
783	Task	Fill Pool	4 days	Fri 1/22/21	Wed 1/27/21	NA	NA	0%	782											
784	Task	Trellis	4 days	Wed 12/16/20	Mon 12/21/20	NA	NA	0%	770											
785	Task	Fencing	2 days	Thu 12/31/20	Fri 1/1/21	NA	NA	0%	779	786										
786	Task	Signage	1 day	Mon 1/4/21	Mon 1/4/21	NA	NA	0%	785	787										
787	Task	Landscaping	3 days	Tue 1/5/21	Thu 1/7/21	NA	NA	0%	786	788										
788	Task	Furniture & Equipment	0 days	Thu 1/7/21	Thu 1/7/21	NA	NA	0%	787	789										
789	Task	MEPS Trim	3 days	Fri 1/8/21	Tue 1/12/21	NA	NA	0%	788	790										
790	Task	Final Inspect - Pool Area	0 days	Tue 1/12/21	Tue 1/12/21	NA	NA	0%	789	791,811FF+30 days										
791	Task	Health Dept Inspection	0 days	Tue 1/12/21	Tue 1/12/21	NA	NA	0%	790	792										
792	Task	Punch Out and Clean	15 days	Wed 1/13/21	Tue 2/2/21	NA	NA	0%	791											
793	Task	Install Security access gates	51 days	Thu 1/28/21	Thu 4/8/21	NA	NA	0%												
794	Task	Extend Electrical Service Security Gates	4 days	Thu 1/28/21	Tue 2/2/21	NA	NA	0%	753											
795	Task	Install Post	1 day	Fri 4/2/21	Fri 4/2/21	NA	NA	0%	759,758	796										
796	Task	Install Gate	2 days	Mon 4/5/21	Tue 4/6/21	NA	NA	0%	795	797										
797	Task	Install Gate Control	2 days	Wed 4/7/21	Thu 4/8/21	NA	NA	0%	796											
798	Task	Site Amenities, Landscape, Hardscape and Ponds	3 days	Fri 2/19/21	Tue 2/23/21	NA	NA	0%												
799	Task	Dumpster Enclosure	1 day	Fri 2/19/21	Fri 2/19/21	NA	NA	0%	755	800										
800	Task	Perimeter Site Fence	1 day	Mon 2/22/21	Mon 2/22/21	NA	NA	0%	799	801										
801	Task	Furnishings (Bench, Bike Rack, Trash Cans)	1 day	Tue 2/23/21	Tue 2/23/21	NA	NA	0%	800											
802	Task	Landscape-Irrigation	61 days	Thu 1/28/21	Thu 4/22/21	NA	NA	0%												
803	Task	Well Development	3 days	Thu 1/28/21	Mon 2/1/21	NA	NA	0%	753	804										
804	Task	Irrigation-Rough in with sleeves	15 days	Tue 2/2/21	Mon 2/22/21	NA	NA	0%	803	805										
805	Task	Final Landscape Grading	15 days	Tue 2/23/21	Mon 3/15/21	NA	NA	0%	804	806										

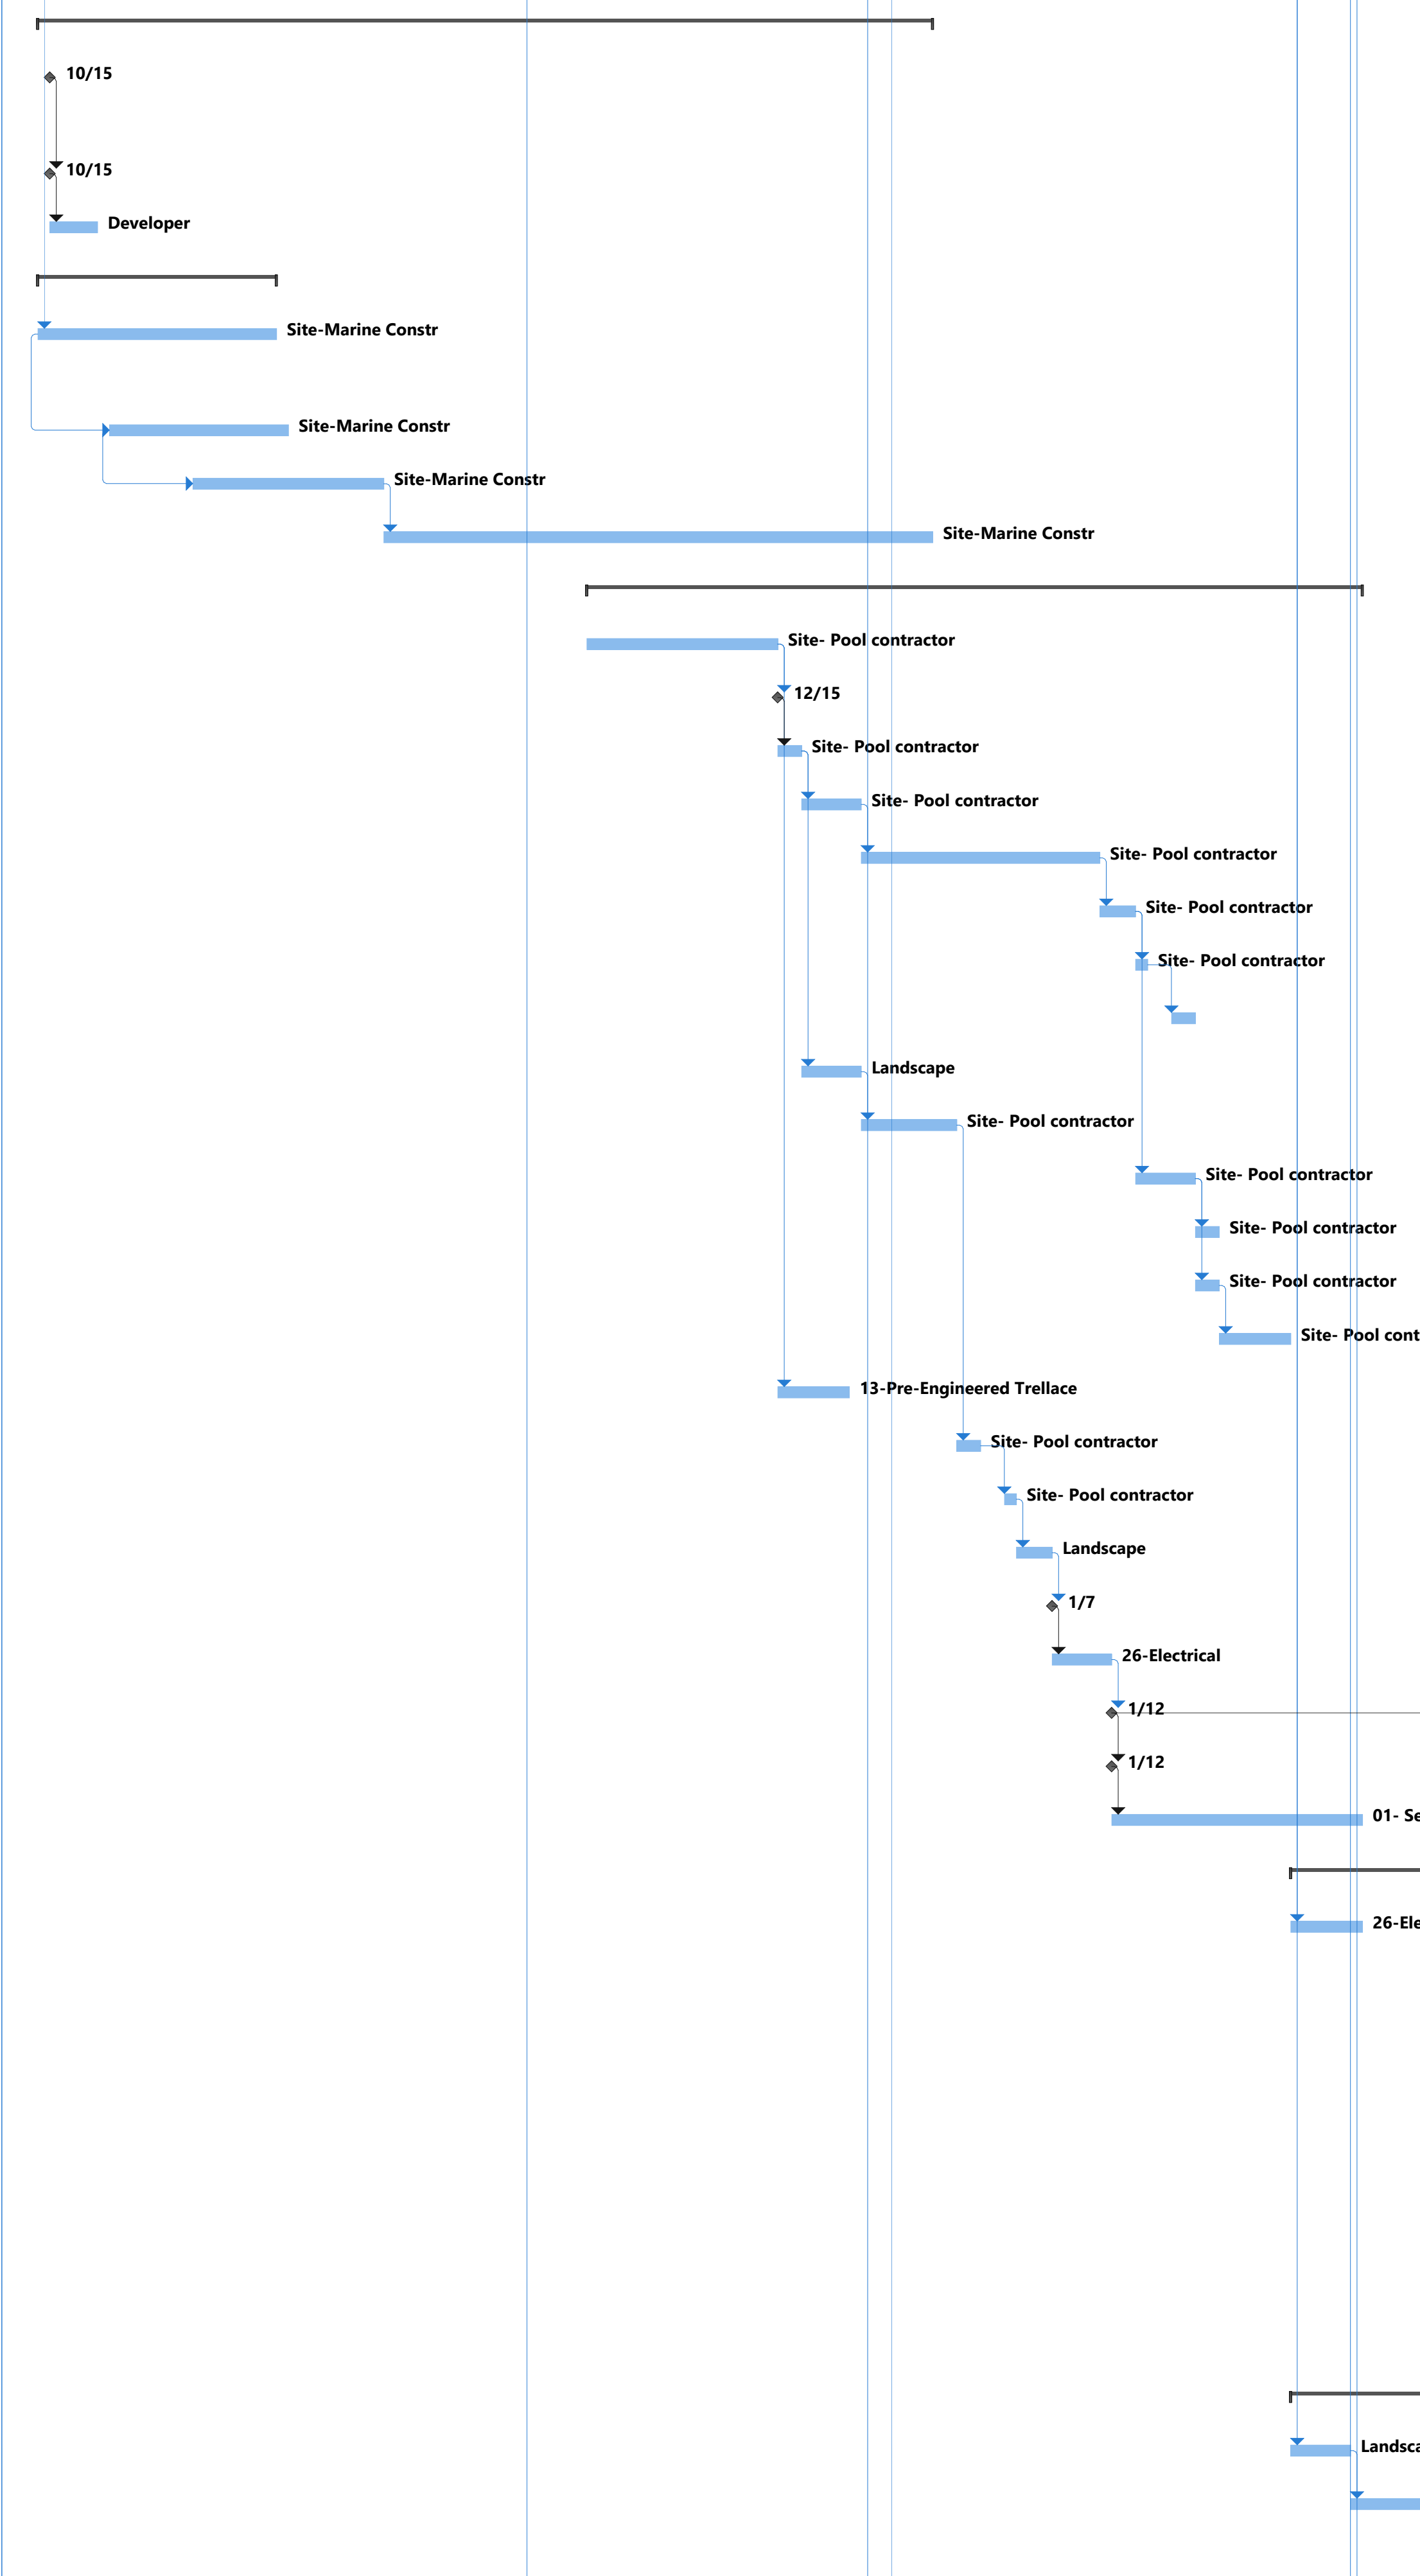

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan		
806		Set Irrigation with controls	10 days	Tue 3/16/21	Mon 3/29/21	NA	NA	0%	805	807,809									
807		Landscape	10 days	Tue 3/30/21	Mon 4/12/21	NA	NA	0%	806	808									
808		Mulch Beds	8 days	Tue 4/13/21	Thu 4/22/21	NA	NA	0%	807										
809		Sod Grass Areas	8 days	Tue 3/30/21	Thu 4/8/21	NA	NA	0%	806										
810		Playground	10 days	Tue 2/23/21	Mon 3/8/21	NA	NA	0%											
811		Layout Boundary	1 day	Tue 2/23/21	Tue 2/23/21	NA	NA	0%	790FF+30 days	812									
812		Set Equipment	4 days	Wed 2/24/21	Mon 3/1/21	NA	NA	0%	811	813									
813		Set Curb	2 days	Tue 3/2/21	Wed 3/3/21	NA	NA	0%	812	814									
814		Set Mulch	1 day	Thu 3/4/21	Thu 3/4/21	NA	NA	0%	813	815									
815		Erect Fencing	2 days	Fri 3/5/21	Mon 3/8/21	NA	NA	0%	814										
816		Clubhouse	131 days	Fri 12/25/20	Fri 6/25/21	NA	NA	0%											
817		Survey Pad	1 day	Fri 12/25/20	Fri 12/25/20	NA	NA	0%	668	818									
818		Batter Boards	1 day	Mon 12/28/20	Mon 12/28/20	NA	NA	0%	817	819									
819		Form SOG	5 days	Tue 12/29/20	Mon 1/4/21	NA	NA	0%	818	820									
820		Final Grade +/- .10	1 day	Tue 1/5/21	Tue 1/5/21	NA	NA	0%	819	821									
821		MEP Underground Rough	10 days	Wed 1/6/21	Tue 1/19/21	NA	NA	0%	820	822									
822		Inspection mep Undgrd	0 days	Tue 1/19/21	Tue 1/19/21	NA	NA	0%	821	823									
823		Treat, Reinforce, Inspect, and Pour SOG	6 days	Wed 1/20/21	Wed 1/27/21	NA	NA	0%	822	824									
824		Curing Compound/Cut Slab	1 day	Thu 1/28/21	Thu 1/28/21	NA	NA	0%	823	825									
825		Strip and Clean	1 day	Fri 1/29/21	Fri 1/29/21	NA	NA	0%	824	826									
826		Exterior Frame	4 days	Mon 2/1/21	Thu 2/4/21	NA	NA	0%	825	827									
827		Set Truss Package	2 days	Fri 2/5/21	Mon 2/8/21	NA	NA	0%	826	828									
828		Frame Roof	4 days	Tue 2/9/21	Fri 2/12/21	NA	NA	0%	827	829,834									
829		Sheath Roof	2 days	Mon 2/15/21	Tue 2/16/21	NA	NA	0%	828	830									
830		Dry-In Roof	2 days	Wed 2/17/21	Thu 2/18/21	NA	NA	0%	829	831,832,833,840									
831		Tape and Seal Zip	2 days	Fri 2/19/21	Mon 2/22/21	NA	NA	0%	830										
832		Install Windows	2 days	Fri 2/19/21	Mon 2/22/21	NA	NA	0%	830										
833		Inspect Engineering with Tie-down and Sheath	0 days	Thu 2/18/21	Thu 2/18/21	NA	NA	0%	830										
834		Interior Framing - Walls & Ceilings	5 days	Mon 2/15/21	Fri 2/19/21	NA	NA	0%	828	835,838SS+3 days									
835		Frame interior Soffit	2 days	Mon 2/22/21	Tue 2/23/21	NA	NA	0%	834	836SS									
836		Framing Inspection	0 days	Mon 2/22/21	Mon 2/22/21	NA	NA	0%	835SS	837									
837		Framing Punch Out	2 days	Mon 2/22/21	Tue 2/23/21	NA	NA	0%	836										
838		MEP F/S Rough Walls & Ceilings	8 days	Thu 2/18/21	Mon 3/1/21	NA	NA	0%	834SS+3 days	839									
839		MEP F/S Rough Inspections	0 days	Mon 3/1/21	Mon 3/1/21	NA	NA	0%	838	853									
840		Exterior Fascia	3 days	Fri 2/19/21	Tue 2/23/21	NA	NA	0%	830	841,843,844,846,									
841		Set Exterior Stucco Band	2 days	Wed 2/24/21	Thu 2/25/21	NA	NA	0%	840										
842		Roof	8 days	Mon 2/22/21	Wed 3/3/21	NA	NA	0%	840SS+1 day										
843		Install Exterior Doors- Temp Lock	2 days	Wed 2/24/21	Thu 2/25/21	NA	NA	0%	840										
844		Install Back Wall j-Molding	2 days	Wed 2/24/21	Thu 2/25/21	NA	NA	0%	840	845									
845		Exterior Styrofoam Inserts	1 day	Fri 2/26/21	Fri 2/26/21	NA	NA	0%	844										
846		Exterior Lathe -Stucco-	6 days	Wed 2/24/21	Wed 3/3/21	NA	NA	0%	840	848									
847		Exterior Veneer	10 days	Wed 2/24/21	Tue 3/9/21	NA	NA	0%	840	849									
848		Install Exterior Alum Soffit	4 days	Thu 3/4/21	Tue 3/9/21	NA	NA	0%	846										
849		Prime and First Coat of Paint - Exterior	2 days	Wed 3/10/21	Thu 3/11/21	NA	NA	0%	847	850									
850		Final Paint - Exterior	2 days	Fri 3/12/21	Mon 3/15/21	NA	NA	0%	849	851									
851		Exterior Railing	2 days	Tue 3/16/21	Wed 3/17/21	NA	NA	0%	850										
852		Temp Power	0 days	Mon 3/8/21	Mon 3/8/21	NA	NA	0%	854										
853		Insulation and Inspection	2 days	Tue 3/2/21	Wed 3/3/21	NA	NA	0%	839	854,856									
854		Interior Zip-Hallway	3 days	Thu 3/4/21	Mon 3/8/21	NA	NA	0%	853	855,852,1004,126									
855		Interior Stucco/Plaster over lathe	2 days	Tue 3/9/21	Wed 3/10/21	NA	NA	0%	854										

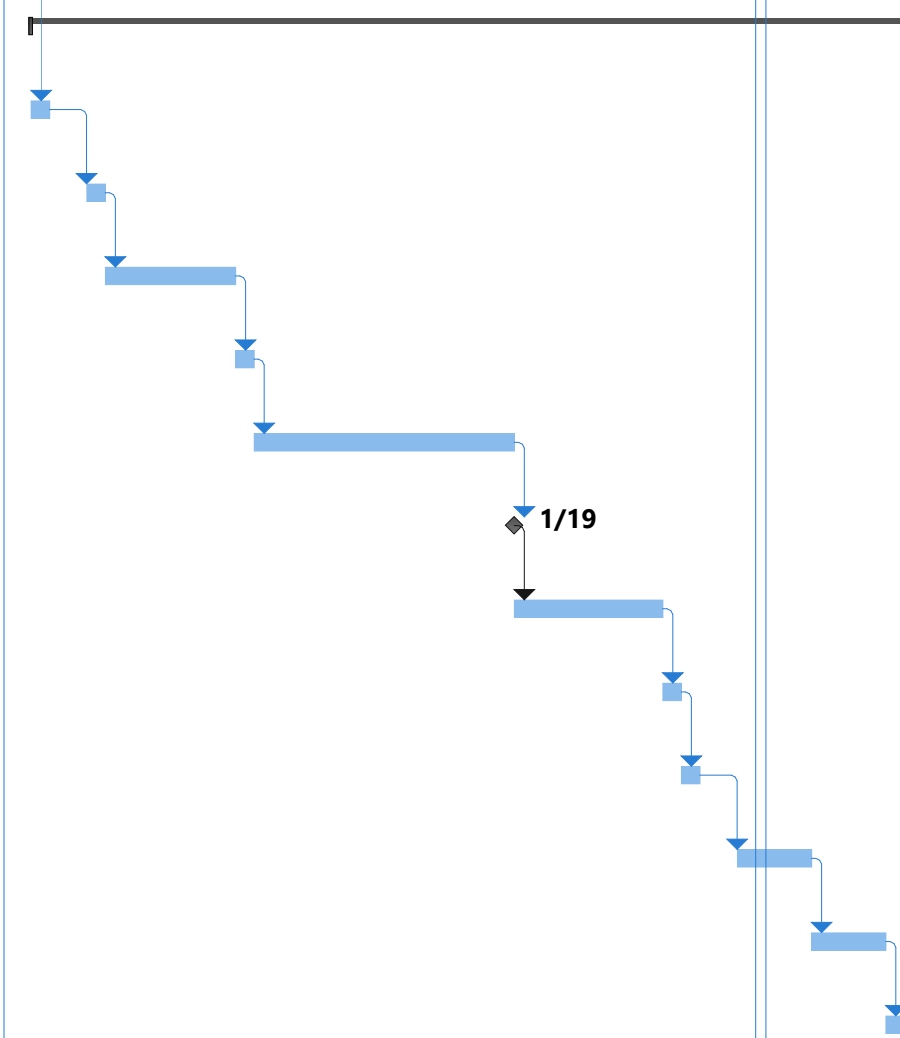


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter			
											Jul	Aug	Sep	Oct	Nov	Dec	Jan			
856		Finish Drywall	14 days	Thu 3/4/21	Tue 3/23/21	NA	NA	0%	853	857,858										
857		Install Doors	5 days	Wed 3/24/21	Tue 3/30/21	NA	NA	0%	856											
858		Running Trim	4 days	Wed 3/24/21	Mon 3/29/21	NA	NA	0%	856	859										
859		Prime Paint - Interior	3 days	Tue 3/30/21	Thu 4/1/21	NA	NA	0%	858	860										
860		2nd Coat of Paint - Interior	5 days	Fri 4/2/21	Thu 4/8/21	NA	NA	0%	859	861,865										
861		Install Bath and Floor Tile	10 days	Fri 4/9/21	Thu 4/22/21	NA	NA	0%	860	862										
862		Install Door Hardware	2 days	Fri 4/23/21	Mon 4/26/21	NA	NA	0%	861	863										
863		Install Cabinets and Countertops	3 days	Tue 4/27/21	Thu 4/29/21	NA	NA	0%	862	864										
864		Install Door Hardware	5 days	Fri 4/30/21	Thu 5/6/21	NA	NA	0%	863											
865		MEPF Trim	7 days	Fri 4/9/21	Mon 4/19/21	NA	NA	0%	860	866										
866		Install Flooring/Tile/LVT	10 days	Tue 4/20/21	Mon 5/3/21	NA	NA	0%	865	867										
867		Bath Accessories	6 days	Tue 5/4/21	Tue 5/11/21	NA	NA	0%	866	868										
868		MEPF Inspections	5 days	Wed 5/12/21	Tue 5/18/21	NA	NA	0%	867	869										
869		Final Paint - Interiors	6 days	Wed 5/19/21	Wed 5/26/21	NA	NA	0%	868	870										
870		Final clean	2 days	Thu 5/27/21	Fri 5/28/21	NA	NA	0%	869	871										
871		Punch Out and Clean	20 days	Mon 5/31/21	Fri 6/25/21	NA	NA	0%	870											
872		Maintenance Building	81 days	Tue 2/2/21	Tue 5/25/21	NA	NA	0%												
873		Survey Pad	1 day	Tue 2/2/21	Tue 2/2/21	NA	NA	0%	668,673	874										
874		Batter Boards	1 day	Wed 2/3/21	Wed 2/3/21	NA	NA	0%	873	875										
875		Form SOG	2 days	Thu 2/4/21	Fri 2/5/21	NA	NA	0%	874	876										
876		Final Grade +/- .10	0 days	Fri 2/5/21	Fri 2/5/21	NA	NA	0%	875	877										
877		MEP Underground Rough	2 days	Mon 2/8/21	Tue 2/9/21	NA	NA	0%	876	878										
878		Inspection mep Undgrd	0 days	Tue 2/9/21	Tue 2/9/21	NA	NA	0%	877	879										
879		Treat, Reinforce, Inspect, and Pour SOG	3 days	Wed 2/10/21	Fri 2/12/21	NA	NA	0%	878	880										
880		Curing Compound/Cut Slab	1 day	Mon 2/15/21	Mon 2/15/21	NA	NA	0%	879	881										
881		Strip and Clean	1 day	Tue 2/16/21	Tue 2/16/21	NA	NA	0%	880	882										
882		Exterior Frame	3 days	Wed 2/17/21	Fri 2/19/21	NA	NA	0%	881	883										
883		Set Truss Package	1 day	Mon 2/22/21	Mon 2/22/21	NA	NA	0%	882	884										
884		Frame Roof	3 days	Tue 2/23/21	Thu 2/25/21	NA	NA	0%	883	885,890										
885		Sheath Roof	1 day	Fri 2/26/21	Fri 2/26/21	NA	NA	0%	884	886										
886		Dry-In Roof	1 day	Mon 3/1/21	Mon 3/1/21	NA	NA	0%	885	887,888,889,895										
887		Tape and Seal Zip	1 day	Tue 3/2/21	Tue 3/2/21	NA	NA	0%	886											
888		Install Windows	1 day	Tue 3/2/21	Tue 3/2/21	NA	NA	0%	886											
889		Inspect Engineering with Tie-down and Sheath	0 days	Mon 3/1/21	Mon 3/1/21	NA	NA	0%	886	891										
890		Interior Framing - Walls & Ceilings	1 day	Fri 2/26/21	Fri 2/26/21	NA	NA	0%	884	893										
891		Framing Inspection	0 days	Mon 3/1/21	Mon 3/1/21	NA	NA	0%	889	892										
892		Framing Punch Out	2 days	Tue 3/2/21	Wed 3/3/21	NA	NA	0%	891											
893		MEP F/S Rough Walls & Ceilings	4 days	Mon 3/1/21	Thu 3/4/21	NA	NA	0%	890	894										
894		MEP F/S Rough Inspections	0 days	Thu 3/4/21	Thu 3/4/21	NA	NA	0%	893	898										
895		Exterior Fascia	1 day	Tue 3/2/21	Tue 3/2/21	NA	NA	0%	886	896,899,901,903,										
896		Set Exterior Stucco Band	2 days	Wed 3/3/21	Thu 3/4/21	NA	NA	0%	895	897										
897		Roof	1 day	Fri 3/5/21	Fri 3/5/21	NA	NA	0%	896											
898		Insulation and Inspection	1 day	Fri 3/5/21	Fri 3/5/21	NA	NA	0%	894	910,909										
899		Install Exterior Doors- Temp Lock	1 day	Wed 3/3/21	Wed 3/3/21	NA	NA	0%	895	900,908										
900		Install Garage Door Buck	1 day	Thu 3/4/21	Thu 3/4/21	NA	NA	0%	899											
901		Install Back Wall J-Molding	1 day	Wed 3/3/21	Wed 3/3/21	NA	NA	0%	895	902										
902		Exterior Styrofoam Inserts	1 day	Thu 3/4/21	Thu 3/4/21	NA	NA	0%	901											
903		exterior Siding-Trim	4 days	Wed 3/3/21	Mon 3/8/21	NA	NA	0%	895	905										
904		Exterior Veneer	5 days	Wed 3/3/21	Tue 3/9/21	NA	NA	0%	895	906										
905		Install Exterior Alum Soffit	1 day	Tue 3/9/21	Tue 3/9/21	NA	NA	0%	903											

Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Milestone Project Summary Inactive Milestone Manual Task Manual Summary Rollup Start-only External Tasks Deadline Manual Progress
Split Summary Inactive Task Inactive Summary Duration-only Manual Summary Finish-only External Milestone Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan		
906		Prime and First Coat of Paint - Exterior	1 day	Wed 3/10/21	Wed 3/10/21	NA	NA	0%	904	907									
907		Final Paint - Exterior	1 day	Thu 3/11/21	Thu 3/11/21	NA	NA	0%	906	908									
908		Erect Trellis	2 days	Fri 3/12/21	Mon 3/15/21	NA	NA	0%	907,899										
909		Temp Power	0 days	Fri 3/5/21	Fri 3/5/21	NA	NA	0%	898										
910		Finish Drywall	10 days	Mon 3/8/21	Fri 3/19/21	NA	NA	0%	898	911									
911		Install Doors	1 day	Mon 3/22/21	Mon 3/22/21	NA	NA	0%	910	912									
912		Running Trim	1 day	Tue 3/23/21	Tue 3/23/21	NA	NA	0%	911	913									
913		Prime Paint - Interior	1 day	Wed 3/24/21	Wed 3/24/21	NA	NA	0%	912	914									
914		2nd Coat of Paint - Interior	1 day	Thu 3/25/21	Thu 3/25/21	NA	NA	0%	913	915									
915		Install Bath and Floor Tile	1 day	Fri 3/26/21	Fri 3/26/21	NA	NA	0%	914	916									
916		Install Door Hardware	1 day	Mon 3/29/21	Mon 3/29/21	NA	NA	0%	915	917									
917		MEPF Trim	7 days	Tue 3/30/21	Wed 4/7/21	NA	NA	0%	916	918									
918		Install Flooring	1 day	Thu 4/8/21	Thu 4/8/21	NA	NA	0%	917	919									
919		Bath Accessories	6 days	Fri 4/9/21	Fri 4/16/21	NA	NA	0%	918	920									
920		MEPF Inspections	5 days	Mon 4/19/21	Fri 4/23/21	NA	NA	0%	919	921									
921		Final Paint - Interiors	6 days	Mon 4/26/21	Mon 5/3/21	NA	NA	0%	920	922									
922		Final clean	1 day	Tue 5/4/21	Tue 5/4/21	NA	NA	0%	921	923									
923		Punch Out and Clean	15 days	Wed 5/5/21	Tue 5/25/21	NA	NA	0%	922										
924		Apartments	155 days	Wed 12/23/20	Tue 7/27/21	NA	NA	0%											
925		Apartment Building One	155 days	Wed 12/23/20	Tue 7/27/21	NA	NA	0%											
926		Survey Pad	1 day	Wed 12/23/20	Wed 12/23/20	NA	NA	0%	667	928									
927		Concrete- SOG	20 days	Thu 12/24/20	Wed 1/20/21	NA	NA	0%											
928		Batter Boards	2 days	Thu 12/24/20	Fri 12/25/20	NA	NA	0%	926	929									
929		Form SOG	5 days	Mon 12/28/20	Fri 1/1/21	NA	NA	0%	928	930									
930		Final Grade +/-10	1 day	Mon 1/4/21	Mon 1/4/21	NA	NA	0%	929	931									
931		MEP Underground Rough	5 days	Tue 1/5/21	Mon 1/11/21	NA	NA	0%	930	932									
932		Inspection mep Undgrd	0 days	Mon 1/11/21	Mon 1/11/21	NA	NA	0%	931	933									
933		Treat, Reinforce, Inspect, and Pour SOG	5 days	Tue 1/12/21	Mon 1/18/21	NA	NA	0%	932	934									
934		Curing Compound/Cut Slab	1 day	Tue 1/19/21	Tue 1/19/21	NA	NA	0%	933	935									
935		Strip and Clean	1 day	Wed 1/20/21	Wed 1/20/21	NA	NA	0%	934	936									
936		Exterior Frame	14 days	Thu 1/21/21	Tue 2/9/21	NA	NA	0%	935	941									
937		1st Floor- Joist	12 days	Thu 1/21/21	Fri 2/5/21	NA	NA	0%											
938		2nd Floor to Joist	12 days	Thu 1/21/21	Fri 2/5/21	NA	NA	0%		949									
939		3rd floor to Joist	14 days	Thu 1/21/21	Tue 2/9/21	NA	NA	0%											
940		Roof Frame-Ext Dry-in	16 days	Wed 2/10/21	Wed 3/3/21	NA	NA	0%											
941		Set Truss Package	2 days	Wed 2/10/21	Thu 2/11/21	NA	NA	0%	936	942									
942		Frame Roof	4 days	Fri 2/12/21	Wed 2/17/21	NA	NA	0%	941	943,948									
943		Sheath Roof	4 days	Thu 2/18/21	Tue 2/23/21	NA	NA	0%	942	944									
944		Dry-In Roof	2 days	Wed 2/24/21	Thu 2/25/21	NA	NA	0%	943	945,946,947,992									
945		Tape and Seal Zip	4 days	Fri 2/26/21	Wed 3/3/21	NA	NA	0%	944										
946		Install Windows	4 days	Fri 2/26/21	Wed 3/3/21	NA	NA	0%	944	985									
947		Inspect Engineering with Tie-down and S/O	0 days	Thu 2/25/21	Thu 2/25/21	NA	NA	0%	944										
948		Interior Framing - Walls & Ceilings	36 days	Wed 2/17/21	Thu 4/8/21	NA	NA	0%	942										
949		1st Floor	12 days	Thu 2/18/21	Fri 3/5/21	NA	NA	0%	938	950,955SS+3 days									
950		2nd Floor	12 days	Mon 3/8/21	Tue 3/23/21	NA	NA	0%	949	951									
951		3rd Floor	12 days	Wed 3/24/21	Thu 4/8/21	NA	NA	0%	950	973									
952		Framing Inspection	0 days	Wed 2/17/21	Wed 2/17/21	NA	NA	0%		953									
953		Framing Punch Out	2 days	Thu 2/18/21	Fri 2/19/21	NA	NA	0%	952										
954		MEP Rough in	24 days	Tue 2/23/21	Fri 3/26/21	NA	NA	0%											
955		1st Fl MEP F/S Rough Walls & Ceilings	8 days	Tue 2/23/21	Thu 3/4/21	NA	NA	0%	949SS+3 days	961,957,956									

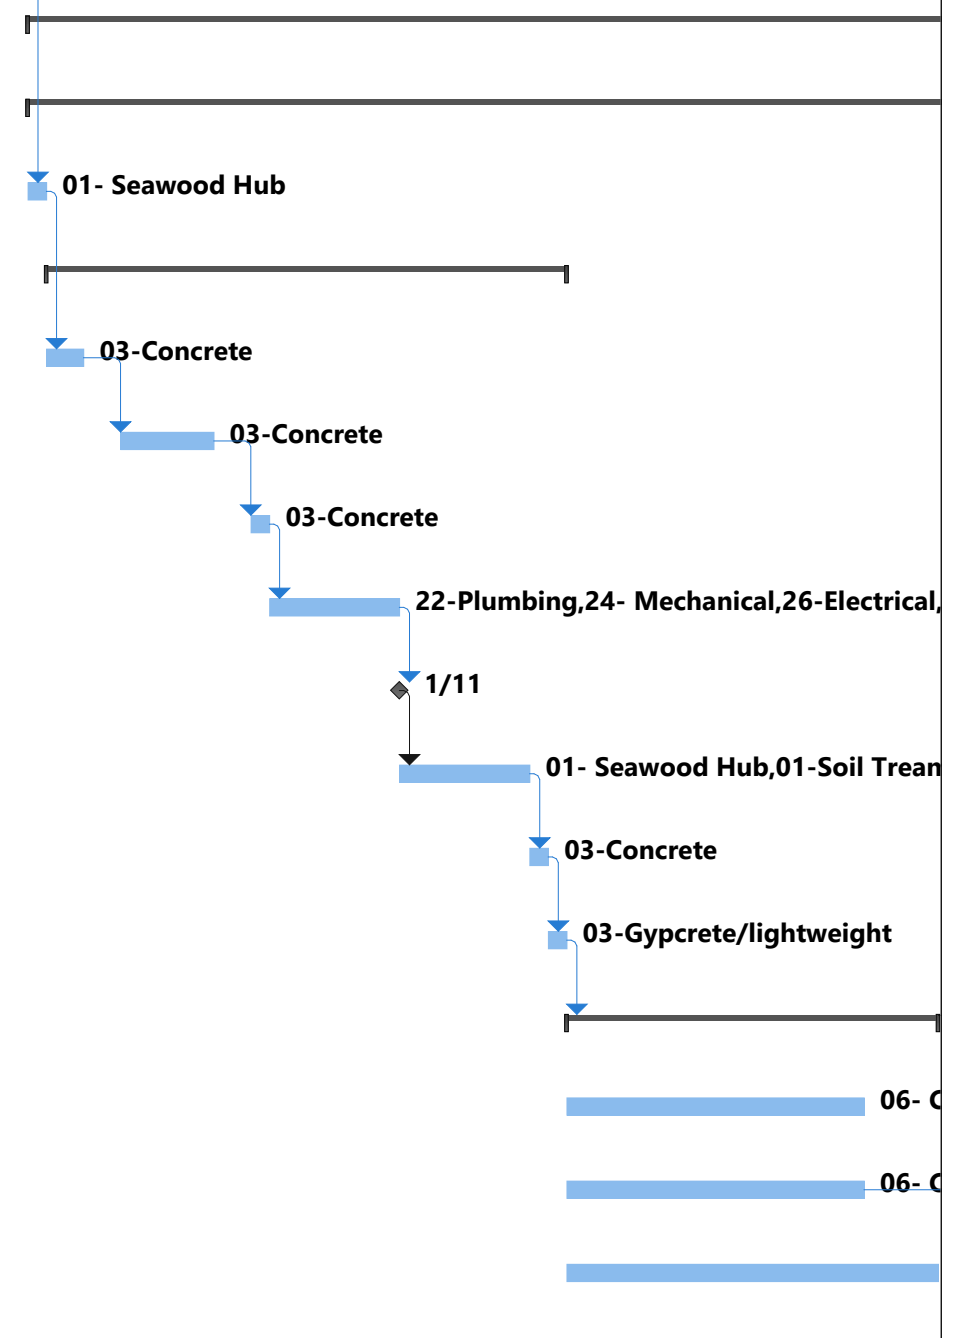


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan		
956		Inspection	0 days	Thu 3/4/21	Thu 3/4/21	NA	NA	0%	955	1009									
957		2nd FI MEP F/S Rough Walls & Ceilings	8 days	Fri 3/5/21	Tue 3/16/21	NA	NA	0%	955	961,959,958									
958		Inspection	0 days	Tue 3/16/21	Tue 3/16/21	NA	NA	0%	957										
959		3rd FI MEP F/S Rough Walls & Ceilings	8 days	Wed 3/17/21	Fri 3/26/21	NA	NA	0%	957	961,963,960									
960		Inspection	0 days	Fri 3/26/21	Fri 3/26/21	NA	NA	0%	959										
961		MEP F/S Rough Inspections	0 days	Fri 3/26/21	Fri 3/26/21	NA	NA	0%	955,957,959										
962		Gypcrete-Lightweight	26 days	Mon 3/29/21	Mon 5/3/21	NA	NA	0%											
963		2nd floor prep	5 days	Mon 3/29/21	Fri 4/2/21	NA	NA	0%	959	964									
964		2nd floor place GYP-crete	5 days	Mon 4/5/21	Fri 4/9/21	NA	NA	0%	963	965									
965		3rd Floor Prep	5 days	Mon 4/12/21	Fri 4/16/21	NA	NA	0%	964	966									
966		3rd Place Gypcrete	5 days	Mon 4/19/21	Fri 4/23/21	NA	NA	0%	965	968									
967		Lightweight Hallways 2nd & 3rd	6 days	Mon 4/26/21	Mon 5/3/21	NA	NA	0%											
968		Prep 2nd Floor Hallway	2 days	Mon 4/26/21	Tue 4/27/21	NA	NA	0%	966	969									
969		Cast 2nd Floor Hallway	1 day	Wed 4/28/21	Wed 4/28/21	NA	NA	0%	968	970									
970		Prep 3rd Floor Hallway	2 days	Thu 4/29/21	Fri 4/30/21	NA	NA	0%	969	971									
971		Cast 3rd Floor Hallway	1 day	Mon 5/3/21	Mon 5/3/21	NA	NA	0%	970										
972		Lightweight Balconies	12 days	Fri 4/9/21	Mon 4/26/21	NA	NA	0%											
973		Prep/Waterproof 2nd Floor	4 days	Fri 4/9/21	Wed 4/14/21	NA	NA	0%	951	974									
974		Prep/Waterproof 3rd Floor	4 days	Thu 4/15/21	Tue 4/20/21	NA	NA	0%	973	975									
975		Cast 2nd Floor	2 days	Wed 4/21/21	Thu 4/22/21	NA	NA	0%	974	976,989									
976		Cast 3rd Floor	2 days	Fri 4/23/21	Mon 4/26/21	NA	NA	0%	975	990									
977		Cast Stair Pans	4 days	Tue 3/16/21	Fri 3/19/21	NA	NA	0%											
978		Stairwell Front	2 days	Tue 3/16/21	Wed 3/17/21	NA	NA	0%											
979		1st Through 2nd	1 day	Tue 3/16/21	Tue 3/16/21	NA	NA	0%	986	980									
980		2nd Thru 3rd	1 day	Wed 3/17/21	Wed 3/17/21	NA	NA	0%	979	982									
981		Stairwell Rear	2 days	Thu 3/18/21	Fri 3/19/21	NA	NA	0%											
982		1st Thru 2nd	1 day	Thu 3/18/21	Thu 3/18/21	NA	NA	0%	980	983									
983		2nd Thru 3rd	1 day	Fri 3/19/21	Fri 3/19/21	NA	NA	0%	982	987									
984		Misc. Metals	42 days	Wed 3/3/21	Fri 4/30/21	NA	NA	0%											
985		Lead-Fabrication	0 days	Wed 3/3/21	Wed 3/3/21	NA	NA	0%	946	986									
986		Stairwell 1st thru 3rd	8 days	Thu 3/4/21	Mon 3/15/21	NA	NA	0%	985	987,979									
987		Railing 1st Thru 3rd Stairwells	6 days	Mon 3/22/21	Mon 3/29/21	NA	NA	0%	986,983	988									
988		Railing Façade Entry	2 days	Tue 3/30/21	Wed 3/31/21	NA	NA	0%	987	989									
989		Railing Balconies 2nd floor	3 days	Fri 4/23/21	Tue 4/27/21	NA	NA	0%	988,975	990									
990		Railing Balconies 3rd Floor	3 days	Wed 4/28/21	Fri 4/30/21	NA	NA	0%	989,976										
991		Exterior	35 days	Tue 2/23/21	Mon 4/12/21	NA	NA	0%											
992		Exterior Fascia	5 days	Fri 2/26/21	Thu 3/4/21	NA	NA	0%	944	993,995,996,998,									
993		Set Exterior Stucco Band	4 days	Fri 3/5/21	Wed 3/10/21	NA	NA	0%	992	994									
994		Roof	8 days	Thu 3/11/21	Mon 3/22/21	NA	NA	0%	993										
995		Install Exterior Doors- Temp Lock	6 days	Fri 3/5/21	Fri 3/12/21	NA	NA	0%	992										
996		Install Back Wall j-Molding	4 days	Fri 3/5/21	Wed 3/10/21	NA	NA	0%	992	997									
997		Exterior Styrofoam Inserts	3 days	Thu 3/11/21	Mon 3/15/21	NA	NA	0%	996										
998		Exterior Lathe -Stucco-	21 days	Fri 3/5/21	Fri 4/2/21	NA	NA	0%	992	1000,1005SS									
999		Exterior Veneer	10 days	Fri 3/5/21	Thu 3/18/21	NA	NA	0%	992	1001									
1000		Install Exterior Alum Soffit	6 days	Mon 4/5/21	Mon 4/12/21	NA	NA	0%	998										
1001		Prime and First Coat of Paint - Exterior	5 days	Fri 3/19/21	Thu 3/25/21	NA	NA	0%	999	1002									
1002		Final Paint - Exterior	5 days	Fri 3/26/21	Thu 4/1/21	NA	NA	0%	1001	1003									
1003		Exterior Railing	2 days	Fri 4/2/21	Mon 4/5/21	NA	NA	0%	1002										
1004		Temp Power	0 days	Mon 3/22/21	Mon 3/22/21	NA	NA	0%	854,1012										
1005		Cast Exterior Sidewalks	8 days	Fri 3/5/21	Tue 3/16/21	NA	NA	0%	998SS	1006SS-8 days									

Project: Scenario-03- Early Delie Date: Mon 7/20/20


Task Milestone Project Summary Inactive Milestone Manual Task Manual Summary Rollup Start-only External Tasks Deadline Manual Progress
 Split Summary Inactive Task Duration-only Manual Summary Finish-only External Milestone Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan		
1006		Bounding retaining Walls- Segmented Mc	8 days	Tue 2/23/21	Thu 3/4/21	NA	NA	0%	1005S-8 days										
1007		Interior Finishes	85 days	Fri 3/5/21	Thu 7/1/21	NA	NA	0%											
1008		Insulation and Inspection	9 days	Fri 3/5/21	Wed 3/17/21	NA	NA	0%		1012									
1009		1st Floor Insulation-Inspection	3 days	Fri 3/5/21	Tue 3/9/21	NA	NA	0%	956	1010,1015SS+1 d									
1010		2nd floor Insulation/ Inspection	3 days	Wed 3/10/21	Fri 3/12/21	NA	NA	0%	1009	1011									
1011		3rd Floor Insulation/ Inspection	3 days	Mon 3/15/21	Wed 3/17/21	NA	NA	0%	1010										
1012		Interior Zip-Hallway 1st thru 3rd	3 days	Thu 3/18/21	Mon 3/22/21	NA	NA	0%	1008	1013,1004									
1013		Interior Stucco/Plaster over lathe-Hallway 1st Thru 3rd	5 days	Tue 3/23/21	Mon 3/29/21	NA	NA	0%	1012										
1014		Drywall-GYP	36 days	Mon 3/8/21	Mon 4/26/21	NA	NA	0%											
1015		1st Floor Hang- Finish Drywall	20 days	Mon 3/8/21	Fri 4/2/21	NA	NA	0%	1009SS+1 day	1023,1024SS+2 d									
1016		Drywall Screw Inspection	0 days	Fri 4/2/21	Fri 4/2/21	NA	NA	0%	1015										
1017		2nd Floor Hang- Finish Drywall	20 days	Thu 3/18/21	Wed 4/14/21	NA	NA	0%	1015SS+8 days	1019SS+8 days,10									
1018		Drywall Screw Inspection	0 days	Wed 4/14/21	Wed 4/14/21	NA	NA	0%	1017										
1019		3rd Floor Hang- Finish Drywall	20 days	Tue 3/30/21	Mon 4/26/21	NA	NA	0%	1017SS+8 days	1029,1020									
1020		Drywall Screw Inspection	0 days	Mon 4/26/21	Mon 4/26/21	NA	NA	0%	1019										
1021		Doors and Trim	82 days	Wed 3/10/21	Thu 7/1/21	NA	NA	0%											
1022		1st Floor	23 days	Wed 3/10/21	Fri 4/9/21	NA	NA	0%											
1023		1st floor Install Doors	5 days	Mon 4/5/21	Fri 4/9/21	NA	NA	0%	1015										
1024		1st Running Trim	4 days	Wed 3/10/21	Mon 3/15/21	NA	NA	0%	1015SS+2 days	1033SS+4 days									
1025		2nd Floor	6 days	Thu 4/15/21	Thu 4/22/21	NA	NA	0%											
1026		2nd floor Install Doors	5 days	Thu 4/15/21	Wed 4/21/21	NA	NA	0%	1017	1027SS+2 days									
1027		2nd Running Trim	4 days	Mon 4/19/21	Thu 4/22/21	NA	NA	0%	1026SS+2 days	1036SS+4 days									
1028		3rd Floor	6 days	Tue 4/27/21	Tue 5/4/21	NA	NA	0%											
1029		3rd floor Install Doors	5 days	Tue 4/27/21	Mon 5/3/21	NA	NA	0%	1019	1030SS+2 days									
1030		3rd Floor Running Trim	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%	1029SS+2 days	1039SS+4 days									
1031		Paint	68 days	Tue 3/16/21	Thu 6/17/21	NA	NA	0%											
1032		1st Floor	32 days	Tue 3/16/21	Wed 4/28/21	NA	NA	0%											
1033		Prime Paint - Interior	6 days	Tue 3/16/21	Tue 3/23/21	NA	NA	0%	1024SS+4 days	1042									
1034		Finish Paint	4 days	Fri 4/23/21	Wed 4/28/21	NA	NA	0%	1047	1061,1054									
1035		2nd Floor	32 days	Fri 4/23/21	Mon 6/7/21	NA	NA	0%											
1036		Prime Paint - Interior	6 days	Fri 4/23/21	Fri 4/30/21	NA	NA	0%	1027SS+4 days	1043									
1037		Finish Paint	4 days	Wed 6/2/21	Mon 6/7/21	NA	NA	0%	1049	1063,1056									
1038		3rd Floor	32 days	Wed 5/5/21	Thu 6/17/21	NA	NA	0%											
1039		Prime Paint - Interior	6 days	Wed 5/5/21	Wed 5/12/21	NA	NA	0%	1030SS+4 days	1044									
1040		Finish Paint	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%	1051	1065,1058									
1041		Install Cabinets and Countertops	48 days	Wed 3/24/21	Fri 5/28/21	NA	NA	0%											
1042		1st floor	12 days	Wed 3/24/21	Thu 4/8/21	NA	NA	0%	1033	1047									
1043		2nd Floor	12 days	Mon 5/3/21	Tue 5/18/21	NA	NA	0%	1036	1049									
1044		3rd Floor	12 days	Thu 5/13/21	Fri 5/28/21	NA	NA	0%	1039	1051									
1045		Tile and Flooring	46 days	Fri 4/9/21	Fri 6/11/21	NA	NA	0%											
1046		1st Floor	10 days	Fri 4/9/21	Thu 4/22/21	NA	NA	0%											
1047		Install Bath and Floor Tile	10 days	Fri 4/9/21	Thu 4/22/21	NA	NA	0%	1042	1034									
1048		2nd Floor	10 days	Wed 5/19/21	Tue 6/1/21	NA	NA	0%											
1049		Install Bath and Floor Tile	10 days	Wed 5/19/21	Tue 6/1/21	NA	NA	0%	1043	1037									
1050		3rd Floor	10 days	Mon 5/31/21	Fri 6/11/21	NA	NA	0%											
1051		Install Bath and Floor Tile	10 days	Mon 5/31/21	Fri 6/11/21	NA	NA	0%	1044	1040									
1052		Door Hardware Install	40 days	Thu 4/29/21	Wed 6/23/21	NA	NA	0%											
1053		1st Floor	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%											
1054		Install Door Hardware	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%	1034										

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan		
1055	Mode	2nd Floor	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%											
1056		Install Door Hardware	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%	1037										
1057		3rd Floor	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%											
1058		Install Door Hardware	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%	1040										
1059		MEP Trim	40 days	Thu 4/29/21	Wed 6/23/21	NA	NA	0%											
1060		1st Floor	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%											
1061		MEP Trim	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%	1034	1071,1078									
1062		2nd Floor	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%											
1063		MEP Trim	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%	1037	1073,1080									
1064		3rd Floor	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%											
1065		MEP Trim	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%	1040	1067,1075,1082									
1066		MEPF Inspections	6 days	Thu 6/24/21	Thu 7/1/21	NA	NA	0%											
1067		Final MEP Inspections	2 days	Thu 6/24/21	Fri 6/25/21	NA	NA	0%	1065	1068									
1068		Equipment start up	4 days	Mon 6/28/21	Thu 7/1/21	NA	NA	0%	1067										
1069		Install Flooring/Tile/LVT	40 days	Wed 5/5/21	Tue 6/29/21	NA	NA	0%											
1070		1st Floor	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%											
1071		Flooring	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%	1061										
1072		2nd Floor	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%											
1073		Flooring	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%	1063										
1074		3rd Floor	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%											
1075		Flooring	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%	1065										
1076		Bath Accessories	40 days	Wed 5/5/21	Tue 6/29/21	NA	NA	0%											
1077		1st Floor	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%											
1078		Specialties-DIV 10	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%	1061										
1079		2nd Floor	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%											
1080		Specialties-DIV 10	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%	1063	1087									
1081		3rd Floor	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%											
1082		Specialties-DIV 10	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%	1065	1084									
1083		Punch Walk Thru	2 days	Wed 6/30/21	Thu 7/1/21	NA	NA	0%											
1084		HUD Inspection	1 day	Wed 6/30/21	Wed 6/30/21	NA	NA	0%	1082	1085,1090									
1085		Owner/A-E	1 day	Thu 7/1/21	Thu 7/1/21	NA	NA	0%	1084	1090									
1086		Inspections	2 days	Fri 6/18/21	Mon 6/21/21	NA	NA	0%											
1087		Final Inspections City of Lakeland	2 days	Fri 6/18/21	Mon 6/21/21	NA	NA	0%	1080										
1088		Punch Out and Clean	18 days	Fri 7/2/21	Tue 7/27/21	NA	NA	0%											
1089		1st Floor	5 days	Fri 7/2/21	Thu 7/8/21	NA	NA	0%											
1090		Punch and Clean	5 days	Fri 7/2/21	Thu 7/8/21	NA	NA	0%	1085,1084	1092									
1091		2nd Floor	5 days	Fri 7/9/21	Thu 7/15/21	NA	NA	0%											
1092		Punch and Clean	5 days	Fri 7/9/21	Thu 7/15/21	NA	NA	0%	1090	1094									
1093		3rd Floor	8 days	Fri 7/16/21	Tue 7/27/21	NA	NA	0%											
1094		Punch and Clean	5 days	Fri 7/16/21	Thu 7/22/21	NA	NA	0%	1092	1095									
1095		Final Bldg.	2 days	Fri 7/23/21	Mon 7/26/21	NA	NA	0%	1094	1096									
1096		Final Fire	1 day	Tue 7/27/21	Tue 7/27/21	NA	NA	0%	1095	1097									
1097		C-O	0 days	Tue 7/27/21	Tue 7/27/21	NA	NA	0%	1096										
1098		Final Area - 01 Operational	0 days	Mon 3/8/21	Mon 3/8/21	NA	NA	0%											
1100		Area - 02	238 days	Mon 10/12/20	Wed 9/8/21	NA	NA	0%											
1101		Site Work - Site Utilities and MEP Underground	238 days	Mon 10/12/20	Wed 9/8/21	NA	NA	0%											
1102		SWPP-	36 days	Mon 10/12/20	Mon 11/30/20	NA	NA	0%											
1103		Control Boundary/Wetland- Benchmark	2 days	Mon 10/12/20	Tue 10/13/20	NA	NA	0%	568FS+29 days,741104										
1104		Clear Silt Fence Line	10 days	Wed 10/14/20	Tue 10/27/20	NA	NA	0%	1103	1105									



ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
1105		SWPP/Roadway/Silt Fence/Boundary	8 days	Wed 10/28/20	Fri 11/6/20	NA	NA	0%	1104	1106										
1106		Clear/Grub Site Area -02	12 days	Mon 11/9/20	Tue 11/24/20	NA	NA	0%	1105	1107,1117										
1107		Construction Fence	4 days	Wed 11/25/20	Mon 11/30/20	NA	NA	0%	1106											
1108		Retaining Wall	66 days	Tue 2/9/21	Tue 5/11/21	NA	NA	0%												
1109		Retaining Wall Foundation Engineering Complete- See Note Cut Details Sheet 20	0 days	Tue 2/16/21	Tue 2/16/21	NA	NA	0%	46,1128	1110										
1110		Station 54+74 to Station 41+19- Modular Block-780l/f	30 days	Wed 2/17/21	Tue 3/30/21	NA	NA	0%	1109	1114,1115,1111										
1111		Station 33+75 through Station 31+75 243 l/f	12 days	Wed 3/31/21	Thu 4/15/21	NA	NA	0%	1110											
1112		Carriage House Retaining Wall - CMU (See Masonry)	8 days	Tue 2/9/21	Thu 2/18/21	NA	NA	0%	1126	1113										
1113		Waterproofing Rear with Drain Tie-in	3 days	Fri 2/19/21	Tue 2/23/21	NA	NA	0%	1112											
1114		Install Fencing	14 days	Wed 3/31/21	Mon 4/19/21	NA	NA	0%	1110											
1115		Bounding Retaining Wall AP 02 Thru- AP06 - 1000 l/f approx.	30 days	Wed 3/31/21	Tue 5/11/21	NA	NA	0%	1110											
1116		Site Earthwork	60 days	Wed 11/25/20	Tue 2/16/21	NA	NA	0%												
1117		Roadway thru Apartment- Through Bldg. Pad	8 days	Wed 11/25/20	Fri 12/4/20	NA	NA	0%	1106,748	1118,1149,1152										
1118		Bldg. Pad set -AP-02	6 days	Tue 12/15/20	Tue 12/22/20	NA	NA	0%	1117,1153	1119,1187										
1119		Bldg. Pad Set AP-03	6 days	Wed 12/23/20	Wed 12/30/20	NA	NA	0%	1118	1361,1120										
1120		Bldg. Pad Garage -01 thru -04	6 days	Thu 12/31/20	Thu 1/7/21	NA	NA	0%	1119	1121,2562										
1121		Bldg. Pad Set AP-04	6 days	Fri 1/8/21	Fri 1/15/21	NA	NA	0%	1120	1535,1122										
1122		Building Pad Set AP-05	6 days	Mon 1/18/21	Mon 1/25/21	NA	NA	0%	1121	1709,1123										
1123		Bldg. Pad Set AP-06	6 days	Tue 1/26/21	Tue 2/2/21	NA	NA	0%	1122	1883,1124,1132,1										
1124		Bldg. Pad CH-01 thru CH 06	8 days	Wed 2/3/21	Fri 2/12/21	NA	NA	0%	1123											
1125		Cut Embankment at Retaining Wall	4 days	Wed 2/3/21	Mon 2/8/21	NA	NA	0%	1123	1126										
1126		Construct Retaining Wall Foundation	0 days	Mon 2/8/21	Mon 2/8/21	NA	NA	0%	1125	1127,1112										
1127		Build Bldg. Pad	4 days	Tue 2/9/21	Fri 2/12/21	NA	NA	0%	1126											
1128		Build Roadway Through Stabilized Subgrade	10 days	Wed 2/3/21	Tue 2/16/21	NA	NA	0%	1123	1172,1109										
1129		Site Utilities- Area-02	66 days	Mon 12/7/20	Mon 3/8/21	NA	NA	0%												
1130		On Site-Area-02	66 days	Mon 12/7/20	Mon 3/8/21	NA	NA	0%												
1131		Lift station -01	13 days	Wed 2/3/21	Fri 2/19/21	NA	NA	0%												
1132		Excavation- Set Dewatering to Pond 03	3 days	Wed 2/3/21	Fri 2/5/21	NA	NA	0%	1123	1133										
1133		Set Pre-Cast	1 day	Mon 2/8/21	Mon 2/8/21	NA	NA	0%	1132	1134										
1134		Backfill- 12" Lifts	1 day	Tue 2/9/21	Tue 2/9/21	NA	NA	0%	1133	1135										
1135		Test Lifts	1 day	Wed 2/10/21	Wed 2/10/21	NA	NA	0%	1134	1136										
1136		Tie-in FM Invert	1 day	Thu 2/11/21	Thu 2/11/21	NA	NA	0%	1135	1137,1142										
1137		Tie-in SS Gravity-	1 day	Fri 2/12/21	Fri 2/12/21	NA	NA	0%	1136	1138,1146										
1138		Tie-in SS Gravity @ Wye- Establish Elevation - Main	1 day	Mon 2/15/21	Mon 2/15/21	NA	NA	0%	1137	1139										
1139		Set Pumps	2 days	Tue 2/16/21	Wed 2/17/21	NA	NA	0%	1138	1140										
1140		Set Control Panels	2 days	Thu 2/18/21	Fri 2/19/21	NA	NA	0%	1139											
1141		Force main to SHM-01	17 days	Fri 2/12/21	Mon 3/8/21	NA	NA	0%												
1142		Extend FM to MH-SMH-01- 900 l/f	13 days	Fri 2/12/21	Tue 3/2/21	NA	NA	0%	1136	1143,1144										
1143		Check Elevation-Conflict/Crossing	1 day	Wed 3/3/21	Wed 3/3/21	NA	NA	0%	1142	1144										
1144		Set MH end of run- With Tie-in	3 days	Thu 3/4/21	Mon 3/8/21	NA	NA	0%	1143,1142	1099										
1145		Sanitary Gravity	6 days	Mon 2/15/21	Mon 2/22/21	NA	NA	0%												

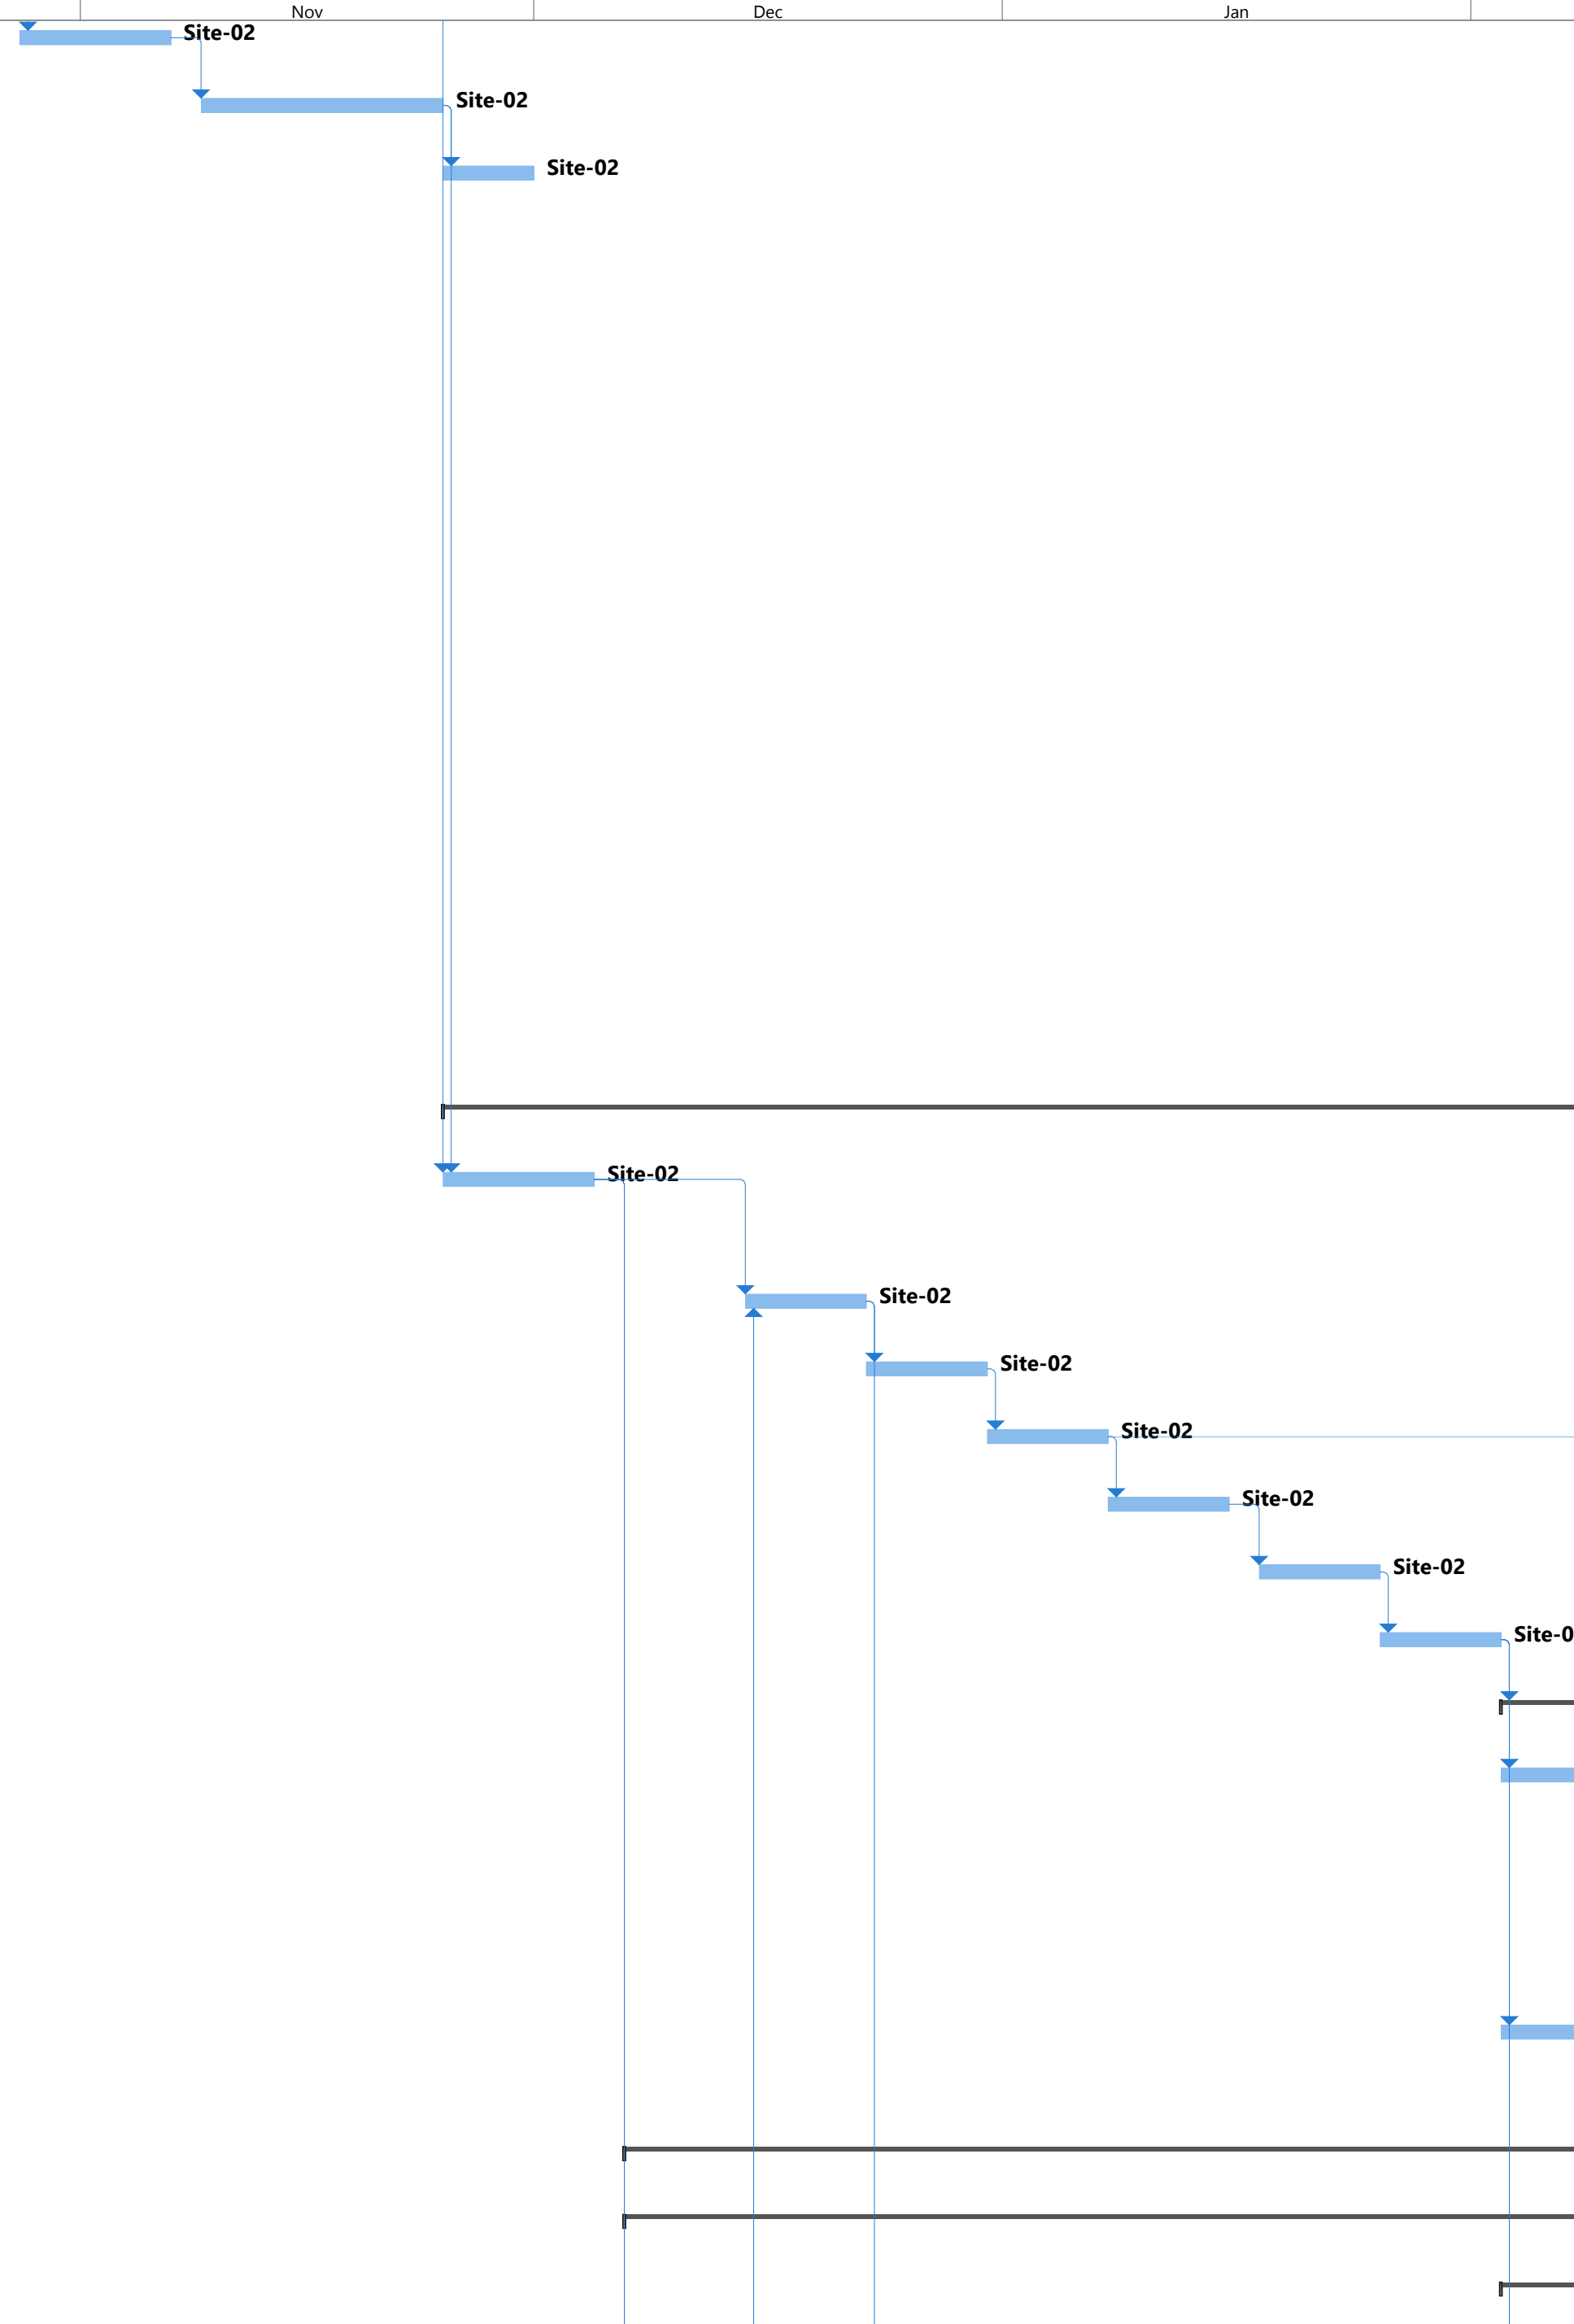

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
1146		SS Gravity-AP-02	4 days	Mon 2/15/21	Thu 2/18/21	NA	NA	0%	1137	1147										
1147		SS Gravity- AP-03	2 days	Fri 2/19/21	Mon 2/22/21	NA	NA	0%	1146	1216										
1148		Water & Fire Main	13 days	Mon 12/7/20	Wed 12/23/20	NA	NA	0%												
1149		Extend Water to AP with FDC	8 days	Mon 12/7/20	Wed 12/16/20	NA	NA	0%	1117	1150										
1150		Extend Fire with FDC- Hydrant to AP 02-06	5 days	Thu 12/17/20	Wed 12/23/20	NA	NA	0%	1149	1216										
1151		Storm Sewer	50 days	Mon 12/7/20	Fri 2/12/21	NA	NA	0%												
1152		Survey- Control elevations Set	2 days	Mon 12/7/20	Tue 12/8/20	NA	NA	0%	1117	1155,1153										
1153		DBI-OFF-1 Thru DBI-Off3 Thru Energy Dissipator- Building 2-3	4 days	Wed 12/9/20	Mon 12/14/20	NA	NA	0%	1152	1118,1154										
1154		DBI-13 Inlet to Mitered Pond 03	3 days	Tue 12/15/20	Thu 12/17/20	NA	NA	0%	1153	1155										
1155		DBI-2A Inlet to Mitered End Pond 03	3 days	Fri 12/18/20	Tue 12/22/20	NA	NA	0%	1152,1154	1156										
1156		DMH-3	3 days	Wed 12/23/20	Fri 12/25/20	NA	NA	0%	1155	1157										
1157		DBI-5	3 days	Mon 12/28/20	Wed 12/30/20	NA	NA	0%	1156	1159,1158										
1158		Survey Control- Verify Elevation Placed	2 days	Thu 12/31/20	Fri 1/1/21	NA	NA	0%	1157	1169										
1159		DBI-2	3 days	Thu 12/31/20	Mon 1/4/21	NA	NA	0%	1157	1160										
1160		DBI-1	3 days	Tue 1/5/21	Thu 1/7/21	NA	NA	0%	1159	1161										
1161		DBI-4	2 days	Fri 1/8/21	Mon 1/11/21	NA	NA	0%	1160	1163,1162										
1162		12" ABS Courtyard to Inlet -AP-02, AP-03 AP-06	8 days	Tue 1/12/21	Thu 1/21/21	NA	NA	0%	1161	1163										
1163		DBI-8	3 days	Fri 1/22/21	Tue 1/26/21	NA	NA	0%	1161,1162	1164										
1164		DBI-11	3 days	Wed 1/27/21	Fri 1/29/21	NA	NA	0%	1163	1165										
1165		DBI-7	3 days	Mon 2/1/21	Wed 2/3/21	NA	NA	0%	1164	1166										
1166		DBI 10	2 days	Thu 2/4/21	Fri 2/5/21	NA	NA	0%	1165	1167										
1167		DBI-12	2 days	Mon 2/8/21	Tue 2/9/21	NA	NA	0%	1166	1168										
1168		DBI-9	1 day	Wed 2/10/21	Wed 2/10/21	NA	NA	0%	1167	1169										
1169		Survey Control- Verify Elevation Placed	2 days	Thu 2/11/21	Fri 2/12/21	NA	NA	0%	1168,1158	2720										
1170		Roadway Paving	47 days	Wed 4/28/21	Thu 7/1/21	NA	NA	0%												
1171		Roadway and Parking Area-02	47 days	Wed 4/28/21	Thu 7/1/21	NA	NA	0%												
1172		Subgrade\Lime rock - Parking Lots	14 days	Wed 4/28/21	Mon 5/17/21	NA	NA	0%	1128,1962	1173,1175,1179										
1173		Install Curbing	14 days	Tue 5/18/21	Fri 6/4/21	NA	NA	0%	1172	1174SS+1 day,118										
1174		Sidewalks Site	15 days	Wed 5/19/21	Tue 6/8/21	NA	NA	0%	1173SS+1 day	1179										
1175		Dress Base with tack	12 days	Tue 5/18/21	Wed 6/2/21	NA	NA	0%	1172	1176										
1176		Asphalt Placement	21 days	Thu 6/3/21	Thu 7/1/21	NA	NA	0%	1175	1177SS+14 days										
1177		Striping and Signage & Wheel Stops	6 days	Wed 6/23/21	Wed 6/30/21	NA	NA	0%	1176SS+14 days											
1178		Landscape-Irrigation	66 days	Wed 6/9/21	Wed 9/8/21	NA	NA	0%												
1185		Apartment Building Two	155 days	Wed 12/23/20	Tue 7/27/21	NA	NA	0%												
1186		Apartment Building Two	155 days	Wed 12/23/20	Tue 7/27/21	NA	NA	0%												
1187		Survey Pad	1 day	Wed 12/23/20	Wed 12/23/20	NA	NA	0%	1118	1189										
1188		Concrete- SOG	20 days	Thu 12/24/20	Wed 1/20/21	NA	NA	0%												
1189		Batter Boards	2 days	Thu 12/24/20	Fri 12/25/20	NA	NA	0%	1187	1190										
1190		Form SOG	5 days	Mon 12/28/20	Fri 1/1/21	NA	NA	0%	1189	1191										
1191		Final Grade +/-10	1 day	Mon 1/4/21	Mon 1/4/21	NA	NA	0%	1190	1192										
1192		MEP Underground Rough	5 days	Tue 1/5/21	Mon 1/11/21	NA	NA	0%	1191	1193										
1193		Inspection mep Undgrd	0 days	Mon 1/11/21	Mon 1/11/21	NA	NA	0%	1192	1194										
1194		Treat, Reinforce, Inspect, and Pour SOG	5 days	Tue 1/12/21	Mon 1/18/21	NA	NA	0%	1193	1195										
1195		Curing Compound/Cut Slab	1 day	Tue 1/19/21	Tue 1/19/21	NA	NA	0%	1194	1196										
1196		Strip and Clean	1 day	Wed 1/20/21	Wed 1/20/21	NA	NA	0%	1195	1197										



ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter			
											Jul	Aug	Sep	Oct	Nov	Dec	Jan			
1197		Exterior Frame	14 days	Thu 1/21/21	Tue 2/9/21	NA	NA	0%	1196	1202										
1198		1st Floor- Joist	12 days	Thu 1/21/21	Fri 2/5/21	NA	NA	0%												
1199		2nd Floor to Joist	12 days	Thu 1/21/21	Fri 2/5/21	NA	NA	0%		1210										
1200		3rd floor to Joist	14 days	Thu 1/21/21	Tue 2/9/21	NA	NA	0%												
1201		Roof Frame-Ext Dry-in	16 days	Wed 2/10/21	Wed 3/3/21	NA	NA	0%												
1202		Set Truss Package	2 days	Wed 2/10/21	Thu 2/11/21	NA	NA	0%	1197	1203										
1203		Frame Roof	4 days	Fri 2/12/21	Wed 2/17/21	NA	NA	0%	1202	1204,1209										
1204		Sheath Roof	4 days	Thu 2/18/21	Tue 2/23/21	NA	NA	0%	1203	1205										
1205		Dry-In Roof	2 days	Wed 2/24/21	Thu 2/25/21	NA	NA	0%	1204	1206,1207,1208,1										
1206		Tape and Seal Zip	4 days	Fri 2/26/21	Wed 3/3/21	NA	NA	0%	1205											
1207		Install Windows	4 days	Fri 2/26/21	Wed 3/3/21	NA	NA	0%	1205	1246										
1208		Inspect Engineering with Tie-down and Sheathing	0 days	Thu 2/25/21	Thu 2/25/21	NA	NA	0%	1205											
1209		Interior Framing - Walls & Ceilings	36 days	Wed 2/17/21	Thu 4/8/21	NA	NA	0%	1203											
1210		1st Floor	12 days	Thu 2/18/21	Fri 3/5/21	NA	NA	0%	1199	1211,1216SS+3 d										
1211		2nd Floor	12 days	Mon 3/8/21	Tue 3/23/21	NA	NA	0%	1210	1212										
1212		3rd Floor	12 days	Wed 3/24/21	Thu 4/8/21	NA	NA	0%	1211	1234										
1213		Framing Inspection	0 days	Wed 2/17/21	Wed 2/17/21	NA	NA	0%		1214										
1214		Framing Punch Out	2 days	Thu 2/18/21	Fri 2/19/21	NA	NA	0%	1213											
1215		MEP Rough in	24 days	Tue 2/23/21	Fri 3/26/21	NA	NA	0%												
1216		1st FI MEP F/S Rough Walls & Ceilings	8 days	Tue 2/23/21	Thu 3/4/21	NA	NA	0%	1210SS+3 days,1150,1147	1222,1218,1217										
1217		Inspection	0 days	Thu 3/4/21	Thu 3/4/21	NA	NA	0%	1216	1270										
1218		2nd FI MEP F/S Rough Walls & Ceilings	8 days	Fri 3/5/21	Tue 3/16/21	NA	NA	0%	1216	1222,1220,1219										
1219		Inspection	0 days	Tue 3/16/21	Tue 3/16/21	NA	NA	0%	1218											
1220		3rd FI MEP F/S Rough Walls & Ceilings	8 days	Wed 3/17/21	Fri 3/26/21	NA	NA	0%	1218	1222,1224,1221										
1221		Inspection	0 days	Fri 3/26/21	Fri 3/26/21	NA	NA	0%	1220											
1222		MEP F/S Rough Inspections	0 days	Fri 3/26/21	Fri 3/26/21	NA	NA	0%	1216,1218,1220											
1223		Gypcrete-Lightweight	26 days	Mon 3/29/21	Mon 5/3/21	NA	NA	0%												
1224		2nd floor prep	5 days	Mon 3/29/21	Fri 4/2/21	NA	NA	0%	1220	1225										
1225		2nd floor place GYP-crete	5 days	Mon 4/5/21	Fri 4/9/21	NA	NA	0%	1224	1226										
1226		3rd Floor Prep	5 days	Mon 4/12/21	Fri 4/16/21	NA	NA	0%	1225	1227										
1227		3rd Place Gypcrete	5 days	Mon 4/19/21	Fri 4/23/21	NA	NA	0%	1226	1229										
1228		Lightweight Hallways 2nd & 3rd	6 days	Mon 4/26/21	Mon 5/3/21	NA	NA	0%												
1229		Prep 2nd Floor Hallway	2 days	Mon 4/26/21	Tue 4/27/21	NA	NA	0%	1227	1230										
1230		Cast 2nd Floor Hallway	1 day	Wed 4/28/21	Wed 4/28/21	NA	NA	0%	1229	1231										
1231		Prep 3rd Floor Hallway	2 days	Thu 4/29/21	Fri 4/30/21	NA	NA	0%	1230	1232										
1232		Cast 3rd Floor Hallway	1 day	Mon 5/3/21	Mon 5/3/21	NA	NA	0%	1231											
1233		Lightweight Balconies	12 days	Fri 4/9/21	Mon 4/26/21	NA	NA	0%												
1234		Prep/Waterproof 2nd Floor	4 days	Fri 4/9/21	Wed 4/14/21	NA	NA	0%	1212	1235										
1235		Prep/Waterproof 3rd Floor	4 days	Thu 4/15/21	Tue 4/20/21	NA	NA	0%	1234	1236										
1236		Cast 2nd Floor	2 days	Wed 4/21/21	Thu 4/22/21	NA	NA	0%	1235	1237,1250										

06-C
06-C

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter
											Jul	Aug	Sep	Oct	Nov	Dec	Jan
1237	Task	Cast 3rd Floor	2 days	Fri 4/23/21	Mon 4/26/21	NA	NA	0%	1236	1251							
1238	Task	Cast Stair Pans	4 days	Tue 3/16/21	Fri 3/19/21	NA	NA	0%									
1239	Task	Stairwell Front	2 days	Tue 3/16/21	Wed 3/17/21	NA	NA	0%									
1240	Task	1st Thru 2nd	1 day	Tue 3/16/21	Tue 3/16/21	NA	NA	0%	1247	1241							
1241	Task	2nd Thru 3rd	1 day	Wed 3/17/21	Wed 3/17/21	NA	NA	0%	1240	1243							
1242	Task	Stairwell Rear	2 days	Thu 3/18/21	Fri 3/19/21	NA	NA	0%									
1243	Task	1st Thru 2nd	1 day	Thu 3/18/21	Thu 3/18/21	NA	NA	0%	1241	1244							
1244	Task	2nd Thru 3rd	1 day	Fri 3/19/21	Fri 3/19/21	NA	NA	0%	1243	1248							
1245	Task	Misc. Metals	42 days	Wed 3/3/21	Fri 4/30/21	NA	NA	0%									
1246	Task	Lead-Fabrication	0 days	Wed 3/3/21	Wed 3/3/21	NA	NA	0%	1207	1247							
1247	Task	Stairwell 1st thru 3rd	8 days	Thu 3/4/21	Mon 3/15/21	NA	NA	0%	1246	1240,1248							
1248	Task	Railing 1st Thru 3rd Stairwells	6 days	Mon 3/22/21	Mon 3/29/21	NA	NA	0%	1244,1247	1249							
1249	Task	Railing Façade Entry	2 days	Tue 3/30/21	Wed 3/31/21	NA	NA	0%	1248	1250							
1250	Task	Railing Balconies 2nd floor	3 days	Fri 4/23/21	Tue 4/27/21	NA	NA	0%	1236,1249	1251							
1251	Task	Railing Balconies 3rd Floor	3 days	Wed 4/28/21	Fri 4/30/21	NA	NA	0%	1237,1250								
1252	Task	Exterior	35 days	Tue 2/23/21	Mon 4/12/21	NA	NA	0%									
1253	Task	Exterior Fascia	5 days	Fri 2/26/21	Thu 3/4/21	NA	NA	0%	1205	1254,1256,1257,1							
1254	Task	Set Exterior Stucco Band	4 days	Fri 3/5/21	Wed 3/10/21	NA	NA	0%	1253	1255							
1255	Task	Roof	8 days	Thu 3/11/21	Mon 3/22/21	NA	NA	0%	1254								
1256	Task	Install Exterior Doors- Temp Lock	6 days	Fri 3/5/21	Fri 3/12/21	NA	NA	0%	1253								
1257	Task	Install Back Wall j-Molding	4 days	Fri 3/5/21	Wed 3/10/21	NA	NA	0%	1253	1258							
1258	Task	Exterior Styrofoam Inserts	3 days	Thu 3/11/21	Mon 3/15/21	NA	NA	0%	1257								
1259	Task	Exterior Lathe -Stucco-	21 days	Fri 3/5/21	Fri 4/2/21	NA	NA	0%	1253	1261,1266SS							
1260	Task	Exterior Veneer	10 days	Fri 3/5/21	Thu 3/18/21	NA	NA	0%	1253	1262							
1261	Task	Install Exterior Alum Soffit	6 days	Mon 4/5/21	Mon 4/12/21	NA	NA	0%	1259								
1262	Task	Prime and First Coat of Paint - Exterior	5 days	Fri 3/19/21	Thu 3/25/21	NA	NA	0%	1260	1263							
1263	Task	Final Paint - Exterior	5 days	Fri 3/26/21	Thu 4/1/21	NA	NA	0%	1262	1264							
1264	Task	Exterior Railing	2 days	Fri 4/2/21	Mon 4/5/21	NA	NA	0%	1263								
1265	Task	Temp Power	0 days	Mon 3/22/21	Mon 3/22/21	NA	NA	0%	854,1273								
1266	Task	Cast Exterior Sidewalks	8 days	Fri 3/5/21	Tue 3/16/21	NA	NA	0%	1259SS	1267SS-8 days							
1267	Task	Bounding retaining Walls- Segmented Modular	8 days	Tue 2/23/21	Thu 3/4/21	NA	NA	0%	1266SS-8 days								
1268	Task	Interior Finishes	85 days	Fri 3/5/21	Thu 7/1/21	NA	NA	0%									
1269	Task	Insulation and Inspection	9 days	Fri 3/5/21	Wed 3/17/21	NA	NA	0%		1273							
1270	Task	1st Floor Insulation-Inspection	3 days	Fri 3/5/21	Tue 3/9/21	NA	NA	0%	1217	1271,1276SS+1 d							
1271	Task	2nd floor Insulation/ Inspection	3 days	Wed 3/10/21	Fri 3/12/21	NA	NA	0%	1270	1272							
1272	Task	3rd Floor Insulation/ Inspection	3 days	Mon 3/15/21	Wed 3/17/21	NA	NA	0%	1271								
1273	Task	Interior Zip-Hallway 1st thru 3rd	3 days	Thu 3/18/21	Mon 3/22/21	NA	NA	0%	1269	1265,1274							
1274	Task	Interior Stucco/Plaster over lathe- Hallway 1st Thru 3rd	5 days	Tue 3/23/21	Mon 3/29/21	NA	NA	0%	1273								
1275	Task	Drywall-GYP	36 days	Mon 3/8/21	Mon 4/26/21	NA	NA	0%									
1276	Task	1st Floor Hang- Finish Drywall	20 days	Mon 3/8/21	Fri 4/2/21	NA	NA	0%	1270SS+1 day	1285SS+2 days,12							
1277	Task	Drywall Screw Inspection	0 days	Fri 4/2/21	Fri 4/2/21	NA	NA	0%	1276								

Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Split Milestone Summary Project Summary Inactive Task Inactive Milestone Inactive Summary Manual Task Duration-only Manual Summary Rollup Manual Summary Start-only Finish-only External Tasks External Milestone Deadline Progress Manual Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan		
1278		2nd Floor Hang- Finish Drywall	20 days	Thu 3/18/21	Wed 4/14/21	NA	NA	0%	1276SS+8 days	1280SS+8 days,12									
1279		Drywall Screw Inspection	0 days	Wed 4/14/21	Wed 4/14/21	NA	NA	0%	1278										
1280		3rd Floor Hang- Finish Drywall	20 days	Tue 3/30/21	Mon 4/26/21	NA	NA	0%	1278SS+8 days	1290,1281									
1281		Drywall Screw Inspection	0 days	Mon 4/26/21	Mon 4/26/21	NA	NA	0%	1280										
1282		Doors and Trim	40 days	Wed 3/10/21	Tue 5/4/21	NA	NA	0%											
1283		1st Floor	23 days	Wed 3/10/21	Fri 4/9/21	NA	NA	0%											
1284		1st floor Install Doors	5 days	Mon 4/5/21	Fri 4/9/21	NA	NA	0%	1276										
1285		1st Running Trim	4 days	Wed 3/10/21	Mon 3/15/21	NA	NA	0%	1276SS+2 days	1294SS+4 days									
1286		2nd Floor	6 days	Thu 4/15/21	Thu 4/22/21	NA	NA	0%											
1287		2nd floor Install Doors	5 days	Thu 4/15/21	Wed 4/21/21	NA	NA	0%	1278	1288SS+2 days									
1288		2nd Running Trim	4 days	Mon 4/19/21	Thu 4/22/21	NA	NA	0%	1287SS+2 days	1297SS+4 days									
1289		3rd Floor	6 days	Tue 4/27/21	Tue 5/4/21	NA	NA	0%											
1290		3rd floor Install Doors	5 days	Tue 4/27/21	Mon 5/3/21	NA	NA	0%	1280	1291SS+2 days									
1291		3rd Floor Running Trim	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%	1290SS+2 days	1300SS+4 days									
1292		Paint	68 days	Tue 3/16/21	Thu 6/17/21	NA	NA	0%											
1293		1st Floor	32 days	Tue 3/16/21	Wed 4/28/21	NA	NA	0%											
1294		Prime Paint - Interior	6 days	Tue 3/16/21	Tue 3/23/21	NA	NA	0%	1285SS+4 days	1303									
1295		Finish Paint	4 days	Fri 4/23/21	Wed 4/28/21	NA	NA	0%	1308	1322,1315									
1296		2nd Floor	32 days	Fri 4/23/21	Mon 6/7/21	NA	NA	0%											
1297		Prime Paint - Interior	6 days	Fri 4/23/21	Fri 4/30/21	NA	NA	0%	1288SS+4 days	1304									
1298		Finish Paint	4 days	Wed 6/2/21	Mon 6/7/21	NA	NA	0%	1310	1324,1317									
1299		3rd Floor	32 days	Wed 5/5/21	Thu 6/17/21	NA	NA	0%											
1300		Prime Paint - Interior	6 days	Wed 5/5/21	Wed 5/12/21	NA	NA	0%	1291SS+4 days	1305									
1301		Finish Paint	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%	1312	1326,1319									
1302		Install Cabinets and Countertops	48 days	Wed 3/24/21	Fri 5/28/21	NA	NA	0%											
1303		1st floor	12 days	Wed 3/24/21	Thu 4/8/21	NA	NA	0%	1294	1308									
1304		2nd Floor	12 days	Mon 5/3/21	Tue 5/18/21	NA	NA	0%	1297	1310									
1305		3rd Floor	12 days	Thu 5/13/21	Fri 5/28/21	NA	NA	0%	1300	1312									
1306		Tile and Flooring	46 days	Fri 4/9/21	Fri 6/11/21	NA	NA	0%											
1307		1st Floor	10 days	Fri 4/9/21	Thu 4/22/21	NA	NA	0%											
1308		Install Bath and Floor Tile	10 days	Fri 4/9/21	Thu 4/22/21	NA	NA	0%	1303	1295									
1309		2nd Floor	10 days	Wed 5/19/21	Tue 6/1/21	NA	NA	0%											
1310		Install Bath and Floor Tile	10 days	Wed 5/19/21	Tue 6/1/21	NA	NA	0%	1304	1298									
1311		3rd Floor	10 days	Mon 5/31/21	Fri 6/11/21	NA	NA	0%											
1312		Install Bath and Floor Tile	10 days	Mon 5/31/21	Fri 6/11/21	NA	NA	0%	1305	1301									
1313		Door Hardware Install	40 days	Thu 4/29/21	Wed 6/23/21	NA	NA	0%											
1314		1st Floor	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%											
1315		Install Door Hardware	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%	1295										
1316		2nd Floor	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%											
1317		Install Door Hardware	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%	1298										
1318		3rd Floor	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%											
1319		Install Door Hardware	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%	1301										
1320		MEP Trim	40 days	Thu 4/29/21	Wed 6/23/21	NA	NA	0%											
1321		1st Floor	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%											
1322		MEP Trim	4 days	Thu 4/29/21	Tue 5/4/21	NA	NA	0%	1295	1332,1339									
1323		2nd Floor	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%											
1324		MEP Trim	4 days	Tue 6/8/21	Fri 6/11/21	NA	NA	0%	1298	1334,1341									
1325		3rd Floor	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%											
1326		MEP Trim	4 days	Fri 6/18/21	Wed 6/23/21	NA	NA	0%	1301	1328,1336,1343									
1327		MEPF Inspections	6 days	Thu 6/24/21	Thu 7/1/21	NA	NA	0%											

Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Milestone Project Summary Inactive Milestone Manual Task Manual Summary Rollup Start-only External Tasks Deadline Manual Progress
Split Summary Inactive Task Inactive Summary Duration-only Manual Summary Finish-only External Milestone Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan		
1328	Task	Final MEP Inspections	2 days	Thu 6/24/21	Fri 6/25/21	NA	NA	0%	1326	1329									
1329	Task	Equipment start up	4 days	Mon 6/28/21	Thu 7/1/21	NA	NA	0%	1328										
1330	Task	Install Flooring/Tile/LVT	40 days	Wed 5/5/21	Tue 6/29/21	NA	NA	0%											
1331	Task	1st Floor	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%											
1332	Task	Flooring	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%	1322										
1333	Task	2nd Floor	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%											
1334	Task	Flooring	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%	1324										
1335	Task	3rd Floor	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%											
1336	Task	Flooring	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%	1326										
1337	Task	Bath Accessories	40 days	Wed 5/5/21	Tue 6/29/21	NA	NA	0%											
1338	Task	1st Floor	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%											
1339	Task	Specialties-DIV 10	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%	1322										
1340	Task	2nd Floor	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%											
1341	Task	Specialties-DIV 10	4 days	Mon 6/14/21	Thu 6/17/21	NA	NA	0%	1324	1348									
1342	Task	3rd Floor	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%											
1343	Task	Specialties-DIV 10	4 days	Thu 6/24/21	Tue 6/29/21	NA	NA	0%	1326	1345									
1344	Task	Punch Walk Thru	2 days	Wed 6/30/21	Thu 7/1/21	NA	NA	0%											
1345	Task	HUD Inspection	1 day	Wed 6/30/21	Wed 6/30/21	NA	NA	0%	1343	1346,1351									
1346	Task	Owner/A-E	1 day	Thu 7/1/21	Thu 7/1/21	NA	NA	0%	1345	1351									
1347	Task	Inspections	2 days	Fri 6/18/21	Mon 6/21/21	NA	NA	0%											
1348	Task	Final Inspections City of Lakeland	2 days	Fri 6/18/21	Mon 6/21/21	NA	NA	0%	1341										
1349	Task	Punch Out and Clean	18 days	Fri 7/2/21	Tue 7/27/21	NA	NA	0%											
1350	Task	1st Floor	5 days	Fri 7/2/21	Thu 7/8/21	NA	NA	0%											
1351	Task	Punch and Clean	5 days	Fri 7/2/21	Thu 7/8/21	NA	NA	0%	1345,1346	1353									
1352	Task	2nd Floor	5 days	Fri 7/9/21	Thu 7/15/21	NA	NA	0%											
1353	Task	Punch and Clean	5 days	Fri 7/9/21	Thu 7/15/21	NA	NA	0%	1351	1355									
1354	Task	3rd Floor	8 days	Fri 7/16/21	Tue 7/27/21	NA	NA	0%											
1355	Task	Punch and Clean	5 days	Fri 7/16/21	Thu 7/22/21	NA	NA	0%	1353	1356									
1356	Task	Final Bldg.	2 days	Fri 7/23/21	Mon 7/26/21	NA	NA	0%	1355	1357									
1357	Task	Final Fire	1 day	Tue 7/27/21	Tue 7/27/21	NA	NA	0%	1356	1358									
1358	Task	C-O	0 days	Tue 7/27/21	Tue 7/27/21	NA	NA	0%	1357										
1359	Task	Apartment Building Three	155 days	Thu 12/31/20	Wed 8/4/21	NA	NA	0%											
1360	Task	Apartment Building Three	155 days	Thu 12/31/20	Wed 8/4/21	NA	NA	0%											
1533	Task	Apartment Building Four	155 days	Mon 1/18/21	Fri 8/20/21	NA	NA	0%											
1534	Task	Apartment Building Four	155 days	Mon 1/18/21	Fri 8/20/21	NA	NA	0%											
1707	Task	Apartment Building Five	155 days	Tue 1/26/21	Mon 8/30/21	NA	NA	0%											
1708	Task	Apartment Building Five	155 days	Tue 1/26/21	Mon 8/30/21	NA	NA	0%											
1881	Task	Apartment Building Six	155 days	Wed 2/3/21	Tue 9/7/21	NA	NA	0%											
1882	Task	Apartment Building Six	155 days	Wed 2/3/21	Tue 9/7/21	NA	NA	0%											
2055	Task	Carriage Homes	138 days	Tue 2/16/21	Thu 8/26/21	NA	NA	0%											
2056	Task	Carriage Unit Building One	93 days	Tue 2/16/21	Thu 6/24/21	NA	NA	0%											
2057	Task	Survey	1 day	Tue 2/16/21	Tue 2/16/21	NA	NA	0%	1372	2058									
2058	Task	Batter Boards	1 day	Wed 2/17/21	Wed 2/17/21	NA	NA	0%	2057	2059									
2059	Task	Form SOG	2 days	Thu 2/18/21	Fri 2/19/21	NA	NA	0%	2058	2060									
2060	Task	Final Grade +/- .10	0 days	Fri 2/19/21	Fri 2/19/21	NA	NA	0%	2059	2061									
2061	Task	Treat, Reinforce, Inspect, and Pour SOG	3 days	Mon 2/22/21	Wed 2/24/21	NA	NA	0%	2060	2062,2601									
2062	Task	Curing Compound/Cut Slab	1 day	Thu 2/25/21	Thu 2/25/21	NA	NA	0%	2061	2063									
2063	Task	Strip and Clean	1 day	Fri 2/26/21	Fri 2/26/21	NA	NA	0%	2062	2064,2141									
2064	Task	Exterior Frame	5 days	Mon 3/1/21	Fri 3/5/21	NA	NA	0%	2063	2065									
2065	Task	Set Truss Package	1 day	Mon 3/8/21	Mon 3/8/21	NA	NA	0%	2064	2066									

Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Split Milestone Summary Inactive Milestone Inactive Summary Project Summary Inactive Task Manual Task Duration-only Manual Summary Rollup Manual Summary Start-only Finish-only External Tasks External Milestone Deadline Progress Manual Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter			4th Quarter			1st Quarter		
											Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
2066	Task	Frame Roof	2 days	Tue 3/9/21	Wed 3/10/21	NA	NA	0%	2065	2067									
2067	Task	Sheath Roof	2 days	Thu 3/11/21	Fri 3/12/21	NA	NA	0%	2066	2068									
2068	Task	Dry-In Roof	1 day	Mon 3/15/21	Mon 3/15/21	NA	NA	0%	2067	2069,2070,2071,2072									
2069	Task	Tape and Seal Zip	1 day	Tue 3/16/21	Tue 3/16/21	NA	NA	0%	2068										
2070	Task	Install Windows	1 day	Tue 3/16/21	Tue 3/16/21	NA	NA	0%	2068										
2071	Task	Inspect Engineering with Tie-down and Sheath	0 days	Mon 3/15/21	Mon 3/15/21	NA	NA	0%	2068	2072									
2072	Task	Framing Inspection	0 days	Mon 3/15/21	Mon 3/15/21	NA	NA	0%	2071	2073,2074									
2073	Task	Framing Punch Out	2 days	Tue 3/16/21	Wed 3/17/21	NA	NA	0%	2072										
2074	Task	MEP F/S Rough Walls & Ceilings	4 days	Tue 3/16/21	Fri 3/19/21	NA	NA	0%	2072	2075									
2075	Task	MEP F/S Rough Inspections	0 days	Fri 3/19/21	Fri 3/19/21	NA	NA	0%	2074	2078									
2076	Task	Exterior Fascia	1 day	Tue 3/16/21	Tue 3/16/21	NA	NA	0%	2068	2079,2081,2082,2083									
2077	Task	Roof	2 days	Wed 3/17/21	Thu 3/18/21	NA	NA	0%	2076										
2078	Task	Insulation and Inspection	2 days	Mon 3/22/21	Tue 3/23/21	NA	NA	0%	2075	2089									
2079	Task	Install Exterior Doors- Temp Lock	1 day	Wed 3/17/21	Wed 3/17/21	NA	NA	0%	2076	2080									
2080	Task	Install Garage Door Buck	1 day	Thu 3/18/21	Thu 3/18/21	NA	NA	0%	2079	2084									
2081	Task	Install Back Wall j-Molding	1 day	Wed 3/17/21	Wed 3/17/21	NA	NA	0%	2076										
2082	Task	exterior Siding-Trim	4 days	Wed 3/17/21	Mon 3/22/21	NA	NA	0%	2076	2083,2085									
2083	Task	Install Exterior Alum Soffit	1 day	Tue 3/23/21	Tue 3/23/21	NA	NA	0%	2082										
2084	Task	Install Garage Doors	3 days	Fri 3/19/21	Tue 3/23/21	NA	NA	0%	2080	2089									
2085	Task	Prime and First Coat of Paint - Exterior	1 day	Tue 3/23/21	Tue 3/23/21	NA	NA	0%	2082	2086									
2086	Task	Final Paint - Exterior	1 day	Wed 3/24/21	Wed 3/24/21	NA	NA	0%	2085										
2087	Task	Interior Finishes	55 days	Wed 3/24/21	Tue 6/8/21	NA	NA	0%											
2088	Task	Drywall-GYP	18 days	Wed 3/24/21	Fri 4/16/21	NA	NA	0%											
2089	Task	1st Floor Hang- Finish Drywall	4 days	Wed 3/24/21	Mon 3/29/21	NA	NA	0%	2078,2084	1981SS+2 days,1982									
2090	Task	Drywall Screw Inspection	0 days	Mon 3/29/21	Mon 3/29/21	NA	NA	0%	2089										
2091	Task	2nd Floor Hang- Finish Drywall	14 days	Tue 3/30/21	Fri 4/16/21	NA	NA	0%	2089SS+4 days	1983,2092,2097									
2092	Task	Drywall Screw Inspection	0 days	Fri 4/16/21	Fri 4/16/21	NA	NA	0%	2091										
2093	Task	1st Floor	5 days	Tue 3/30/21	Mon 4/5/21	NA	NA	0%											
2094	Task	1st floor Install Doors	2 days	Tue 3/30/21	Wed 3/31/21	NA	NA	0%	2089	2095,2101									
2095	Task	Stairway	3 days	Thu 4/1/21	Mon 4/5/21	NA	NA	0%	2094	2101SS+4 days									
2096	Task	2nd Floor	6 days	Mon 4/19/21	Mon 4/26/21	NA	NA	0%											
2097	Task	2nd floor Install Doors	2 days	Mon 4/19/21	Tue 4/20/21	NA	NA	0%	2091	2098SS+2 days									
2098	Task	2nd Running Trim	4 days	Wed 4/21/21	Mon 4/26/21	NA	NA	0%	2097SS+2 days	2104SS+4 days									
2099	Task	Paint	27 days	Wed 4/7/21	Thu 5/13/21	NA	NA	0%											
2100	Task	1st Floor	19 days	Wed 4/7/21	Mon 5/3/21	NA	NA	0%											
2101	Task	Prime Paint - Interior	1 day	Wed 4/7/21	Wed 4/7/21	NA	NA	0%	2094,2095SS+4 d.	2104									
2102	Task	Finish Paint	2 days	Fri 4/30/21	Mon 5/3/21	NA	NA	0%	2104	2118,2113,2105									
2103	Task	2nd Floor	13 days	Tue 4/27/21	Thu 5/13/21	NA	NA	0%											
2104	Task	Prime Paint - Interior	3 days	Tue 4/27/21	Thu 4/29/21	NA	NA	0%	2098SS+4 days,212102,2107										
2105	Task	Finish Paint	2 days	Wed 5/12/21	Thu 5/13/21	NA	NA	0%	2102,2110	2120,2115,2113									
2106	Task	Install Cabinets and Countertops	3 days	Fri 4/30/21	Tue 5/4/21	NA	NA	0%											
2107	Task	2nd Floor	3 days	Fri 4/30/21	Tue 5/4/21	NA	NA	0%	2104	2110,2118									
2108	Task	Tile and Flooring	5 days	Wed 5/5/21	Tue 5/11/21	NA	NA	0%											
2109	Task	2nd Floor	5 days	Wed 5/5/21	Tue 5/11/21	NA	NA	0%											
2110	Task	Install Bath and Floor Tile	5 days	Wed 5/5/21	Tue 5/11/21	NA	NA	0%	2107	2105									
2111	Task	Door Hardware Install	8 days	Fri 5/14/21	Tue 5/25/21	NA	NA	0%											
2112	Task	1st Floor	4 days	Fri 5/14/21	Wed 5/19/21	NA	NA	0%											
2113	Task	Install Door Hardware	4 days	Fri 5/14/21	Wed 5/19/21	NA	NA	0%	2102,2105	2115									
2114	Task	2nd Floor	4 days	Thu 5/20/21	Tue 5/25/21	NA	NA	0%											
2115	Task	Install Door Hardware	4 days	Thu 5/20/21	Tue 5/25/21	NA	NA	0%	2105,2113										

Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Split Milestone Summary Project Summary Inactive Task Manual Task Duration-only Manual Summary Rollup Manual Summary Start-only Finish-only External Tasks External Milestone Deadline Progress


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
2116		MEP Trim	11 days	Wed 5/5/21	Wed 5/19/21	NA	NA	0%												
2117		1st Floor	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%												
2118		MEP Trim	4 days	Wed 5/5/21	Mon 5/10/21	NA	NA	0%	2102,2107	2120										
2119		2nd Floor	4 days	Fri 5/14/21	Wed 5/19/21	NA	NA	0%												
2120		MEP Trim	4 days	Fri 5/14/21	Wed 5/19/21	NA	NA	0%	2105,2118	2126,2129,2122										
2121		MEPF Inspections	6 days	Thu 5/20/21	Thu 5/27/21	NA	NA	0%												
2122		Final MEP Inspections	2 days	Thu 5/20/21	Fri 5/21/21	NA	NA	0%	2120	2123,2134										
2123		Equipment start up	4 days	Mon 5/24/21	Thu 5/27/21	NA	NA	0%	2122	2126										
2124		Install Flooring/Tile/LVT	4 days	Fri 5/28/21	Wed 6/2/21	NA	NA	0%												
2125		2nd Floor	4 days	Fri 5/28/21	Wed 6/2/21	NA	NA	0%												
2126		Flooring	4 days	Fri 5/28/21	Wed 6/2/21	NA	NA	0%	2120,2123	2129										
2127		Bath Accessories	4 days	Thu 6/3/21	Tue 6/8/21	NA	NA	0%												
2128		2nd Floor	4 days	Thu 6/3/21	Tue 6/8/21	NA	NA	0%												
2129		Specialties-DIV 10	4 days	Thu 6/3/21	Tue 6/8/21	NA	NA	0%	2120,2126	2134,2131										
2130		Punch Walk Thru	2 days	Wed 6/9/21	Thu 6/10/21	NA	NA	0%												
2131		HUD Inspection	1 day	Wed 6/9/21	Wed 6/9/21	NA	NA	0%	2129	2132,2137										
2132		Owner/A-E	1 day	Thu 6/10/21	Thu 6/10/21	NA	NA	0%	2131	2137										
2133		Inspections	2 days	Wed 6/9/21	Thu 6/10/21	NA	NA	0%												
2134		Final Inspections City of Lakeland	2 days	Wed 6/9/21	Thu 6/10/21	NA	NA	0%	2122,2129	2137										
2135		Punch Out and Clean	10 days	Fri 6/11/21	Thu 6/24/21	NA	NA	0%												
2136		1st Floor	5 days	Fri 6/11/21	Thu 6/17/21	NA	NA	0%												
2137		Punch and Clean	5 days	Fri 6/11/21	Thu 6/17/21	NA	NA	0%	2131,2132,2134	2139										
2138		2nd Floor	5 days	Fri 6/18/21	Thu 6/24/21	NA	NA	0%												
2139		Punch and Clean	5 days	Fri 6/18/21	Thu 6/24/21	NA	NA	0%	2137											
2140		Carriage Unit Building Two	93 days	Mon 3/1/21	Wed 7/7/21	NA	NA	0%												
2224		Carriage Unit Building Three	93 days	Fri 3/12/21	Tue 7/20/21	NA	NA	0%												
2308		Carriage Unit Building Four	93 days	Thu 3/25/21	Mon 8/2/21	NA	NA	0%												
2392		Carriage Unit Building Five	93 days	Wed 4/7/21	Fri 8/13/21	NA	NA	0%												
2476		Carriage Unit Building Six	93 days	Tue 4/20/21	Thu 8/26/21	NA	NA	0%												
2560		Garage Buildings	79 days	Mon 5/3/21	Thu 8/19/21	NA	NA	0%												
2561		Garage Building One	53 days	Mon 5/3/21	Wed 7/14/21	NA	NA	0%												
2562		Survey	1 day	Mon 5/3/21	Mon 5/3/21	NA	NA	0%	1120,2483	2563										
2563		Batter Boards	1 day	Tue 5/4/21	Tue 5/4/21	NA	NA	0%	2562	2564										
2564		Form SOG	2 days	Wed 5/5/21	Thu 5/6/21	NA	NA	0%	2563	2565										
2565		Final Grade +/- .10	0 days	Thu 5/6/21	Thu 5/6/21	NA	NA	0%	2564	2566										
2566		Treat, Reinforce, Inspect, and Pour SOG	3 days	Fri 5/7/21	Tue 5/11/21	NA	NA	0%	2565	2567,2601										
2567		Curing Compound/Cut Slab	1 day	Wed 5/12/21	Wed 5/12/21	NA	NA	0%	2566	2568										
2568		Strip and Clean	1 day	Thu 5/13/21	Thu 5/13/21	NA	NA	0%	2567	2569,2601										
2569		Exterior Frame	3 days	Fri 5/14/21	Tue 5/18/21	NA	NA	0%	2568	2570										
2570		Set Truss Package	1 day	Wed 5/19/21	Wed 5/19/21	NA	NA	0%	2569	2571										
2571		Frame Roof	3 days	Thu 5/20/21	Mon 5/24/21	NA	NA	0%	2570	2572										
2572		Sheath Roof	1 day	Tue 5/25/21	Tue 5/25/21	NA	NA	0%	2571	2573										
2573		Dry-In Roof	1 day	Wed 5/26/21	Wed 5/26/21	NA	NA	0%	2572	2574,2575,2576,2577										
2574		Tape and Seal Zip	1 day	Thu 5/27/21	Thu 5/27/21	NA	NA	0%	2573											
2575		Install Windows	1 day	Thu 5/27/21	Thu 5/27/21	NA	NA	0%	2573											
2576		Inspect Engineering with Tie-down and Sheath	0 days	Wed 5/26/21	Wed 5/26/21	NA	NA	0%	2573	2577										
2577		Framing Inspection	0 days	Wed 5/26/21	Wed 5/26/21	NA	NA	0%	2576	2578,2579										
2578		Framing Punch Out	2 days	Thu 5/27/21	Fri 5/28/21	NA	NA	0%	2577											
2579		MEP F/S Rough Walls & Ceilings	4 days	Thu 5/27/21	Tue 6/1/21	NA	NA	0%	2577	2580										
2580		MEP F/S Rough Inspections	0 days	Tue 6/1/21	Tue 6/1/21	NA	NA	0%	2579	2583										

Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Split Milestone Summary Inactive Milestone Inactive Summary Project Summary Inactive Task Manual Task Duration-only Manual Summary Rollup Manual Summary Start-only Finish-only External Tasks External Milestone Deadline Progress Manual Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Successors	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan
2581		Exterior Fascia	1 day	Thu 5/27/21	Thu 5/27/21	NA	NA	0%	2573	2584,2586,2587,2										
2582		Roof	2 days	Fri 5/28/21	Mon 5/31/21	NA	NA	0%	2581											
2583		Insulation and Inspection	1 day	Wed 6/2/21	Wed 6/2/21	NA	NA	0%	2580	2591										
2584		Install Exterior Doors- Temp Lock	1 day	Fri 5/28/21	Fri 5/28/21	NA	NA	0%	2581	2585										
2585		Install Garage Door Buck	1 day	Mon 5/31/21	Mon 5/31/21	NA	NA	0%	2584											
2586		Install Back Wall j-Molding	1 day	Fri 5/28/21	Fri 5/28/21	NA	NA	0%	2581											
2587		exterior Siding-Trim	4 days	Fri 5/28/21	Wed 6/2/21	NA	NA	0%	2581	2588,2589										
2588		Install Exterior Alum Soffit	1 day	Thu 6/3/21	Thu 6/3/21	NA	NA	0%	2587											
2589		Prime and First Coat of Paint - Exterior	1 day	Thu 6/3/21	Thu 6/3/21	NA	NA	0%	2587	2590										
2590		Final Paint - Exterior	1 day	Fri 6/4/21	Fri 6/4/21	NA	NA	0%	2589											
2591		Finish Drywall	10 days	Thu 6/3/21	Wed 6/16/21	NA	NA	0%	2583	2592										
2592		Install Doors	1 day	Thu 6/17/21	Thu 6/17/21	NA	NA	0%	2591	2593										
2593		Prime Paint - Interior	1 day	Fri 6/18/21	Fri 6/18/21	NA	NA	0%	2592	2594										
2594		2nd Coat of Paint - Interior	1 day	Mon 6/21/21	Mon 6/21/21	NA	NA	0%	2593	2595										
2595		MEPF Trim	5 days	Tue 6/22/21	Mon 6/28/21	NA	NA	0%	2594	2596										
2596		MEPF Inspections	0 days	Mon 6/28/21	Mon 6/28/21	NA	NA	0%	2595	2597										
2597		Final Paint - Interiors	6 days	Tue 6/29/21	Tue 7/6/21	NA	NA	0%	2596	2598,2599										
2598		Final clean	1 day	Wed 7/7/21	Wed 7/7/21	NA	NA	0%	2597	2599										
2599		Punch Out and Clean	5 days	Thu 7/8/21	Wed 7/14/21	NA	NA	0%	2598,2597											
2600		Garage Building Two	53 days	Fri 5/14/21	Tue 7/27/21	NA	NA	0%												
2639		Garage Building Three	53 days	Thu 5/27/21	Mon 8/9/21	NA	NA	0%												
2678		Garage Building Four	53 days	Tue 6/8/21	Thu 8/19/21	NA	NA	0%												
2717		FF&E	15 days	Fri 8/20/21	Thu 9/9/21	NA	NA	0%												
2719		Project Close	5 days	Fri 9/10/21	Thu 9/16/21	NA	NA	0%												










Project: Scenario-03- Early Delle Date: Mon 7/20/20

Task	Milestone	Project Summary	Inactive Milestone	Manual Task	Manual Summary Rollup	Start-only	External Tasks	Deadline	Manual Progress
Split	Summary	Inactive Task	Inactive Summary	Duration-only	Manual Summary	Finish-only	External Milestone	Progress	







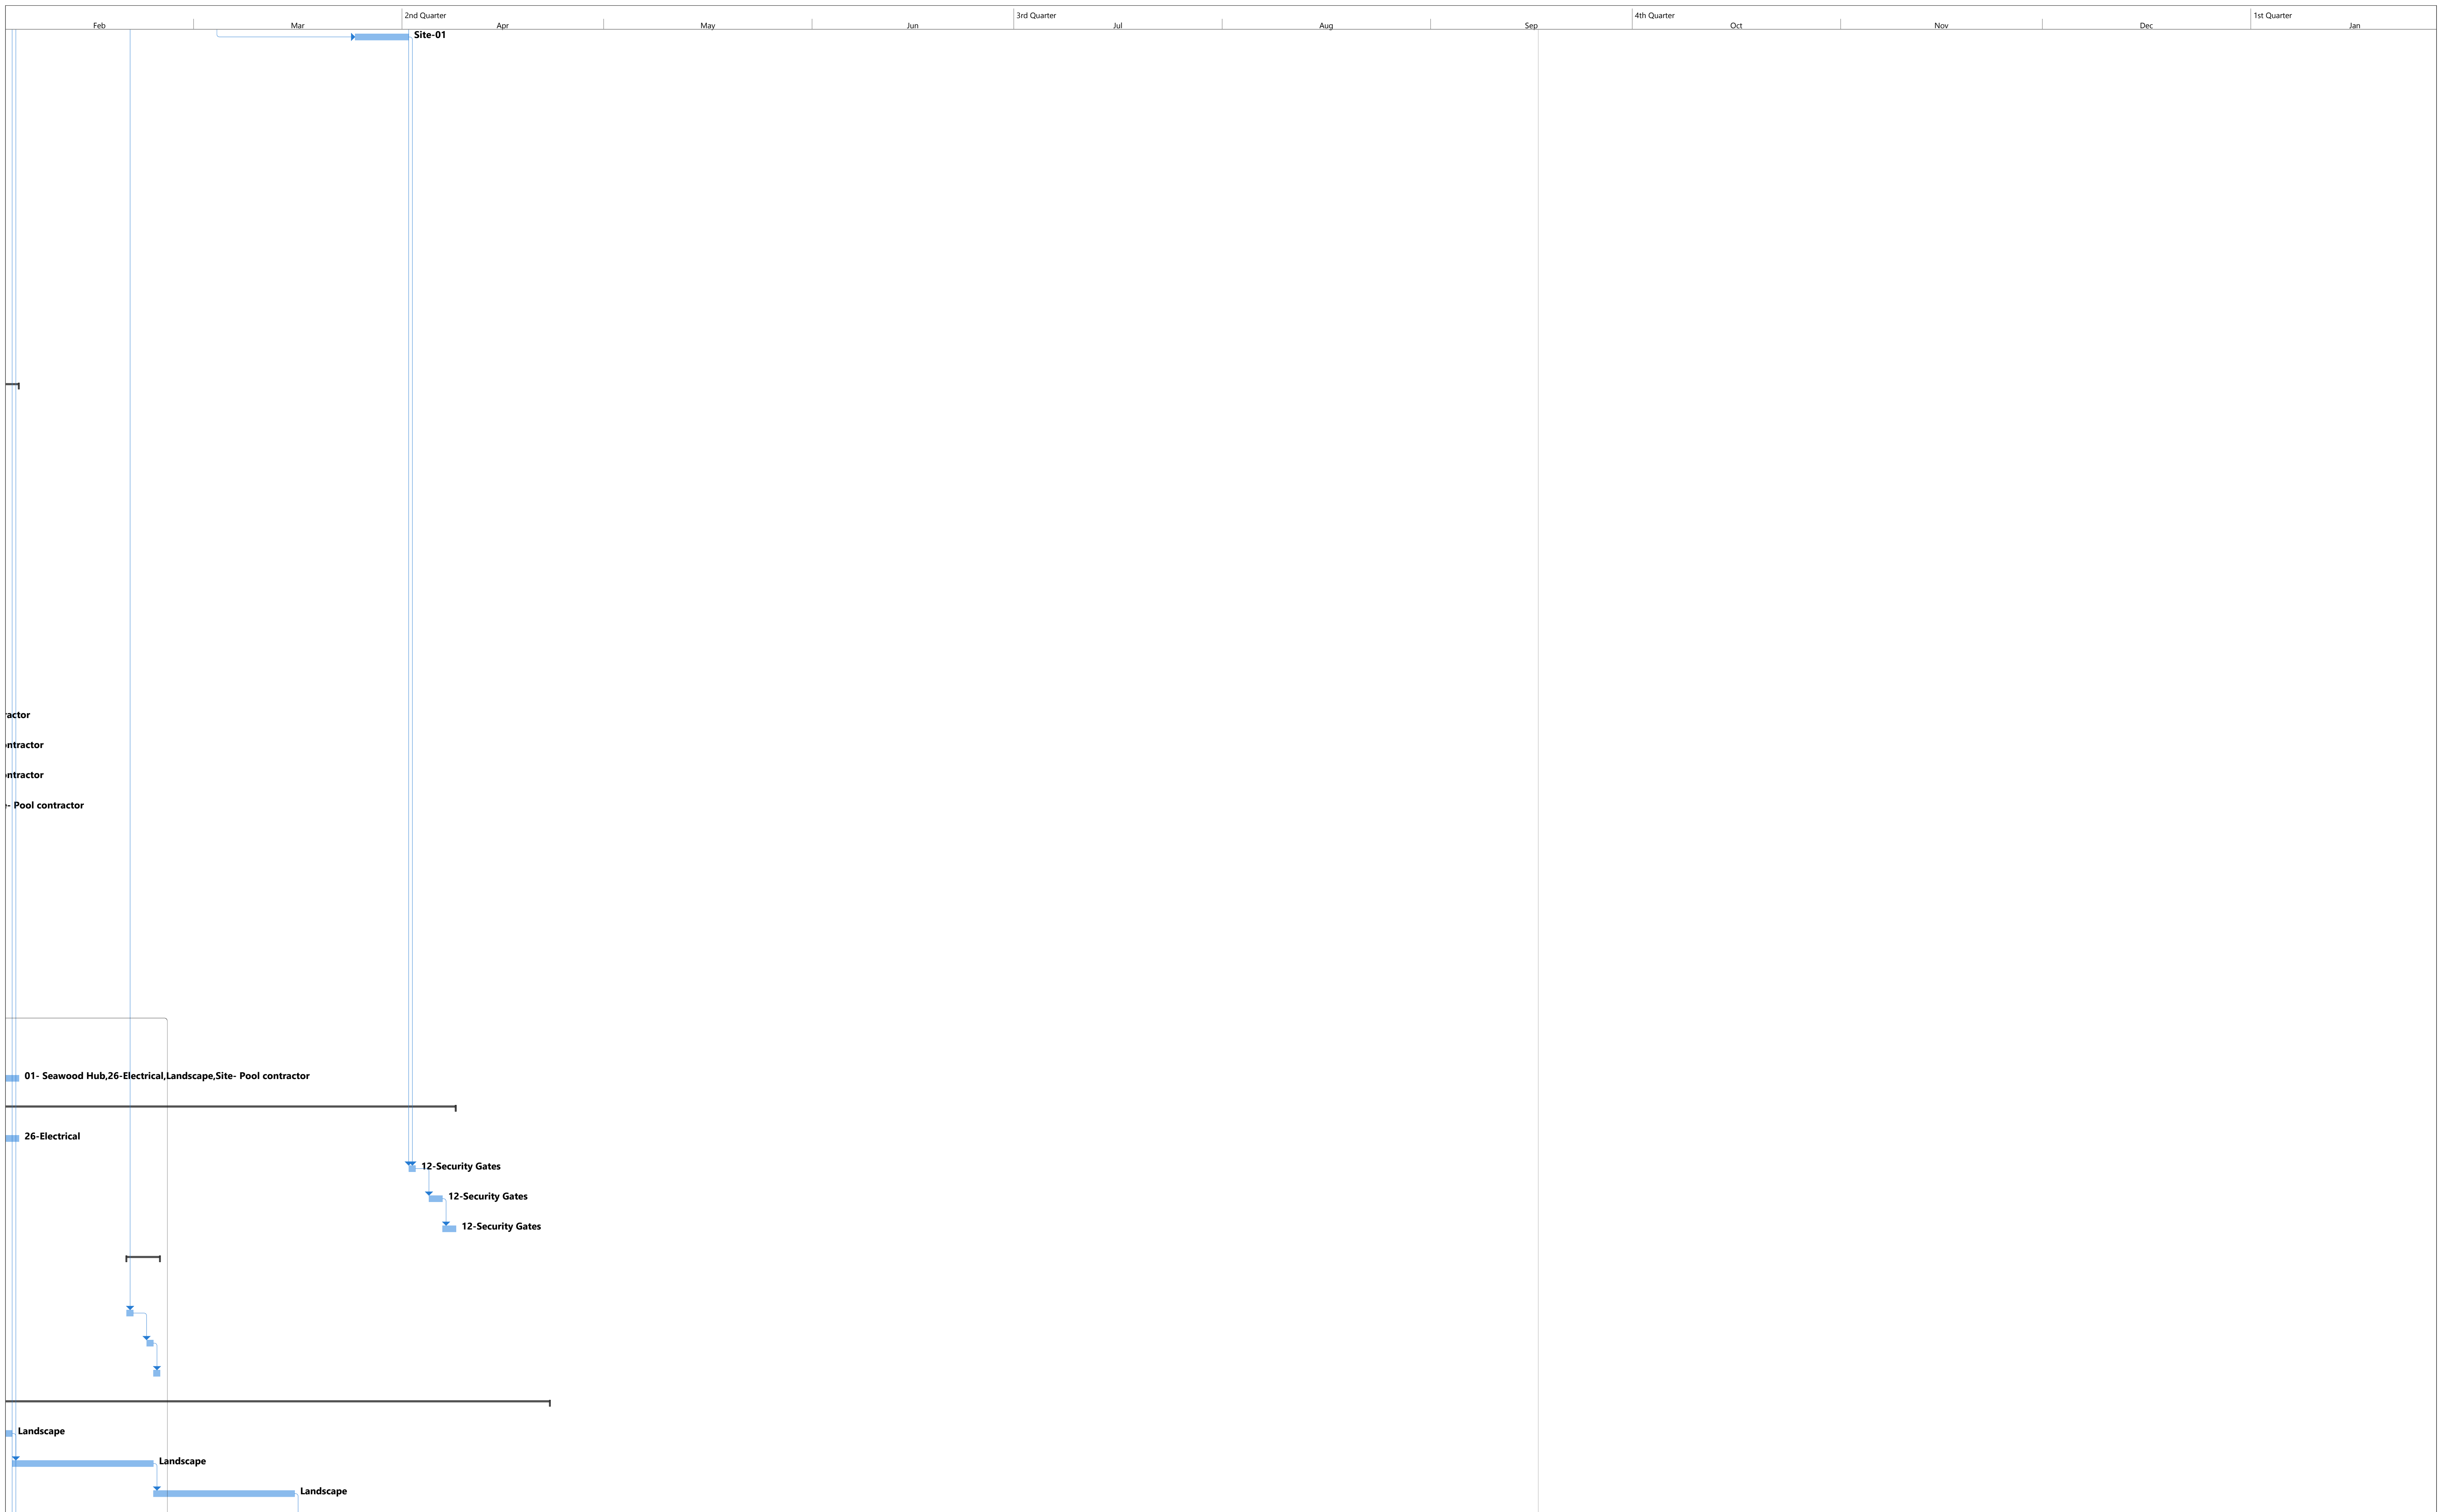

Project: Scenario-03- Early Delie Date: Mon 7/20/20

Task Split	Milestone Summary	Project Summary Inactive Task	Inactive Milestone Inactive Summary	Manual Task Duration-only	Manual Summary Rollup Manual Summary	Start-only Finish-only	External Tasks External Milestone	Deadline Progress	Manual Progress
------------	-------------------	-------------------------------	-------------------------------------	---------------------------	--------------------------------------	------------------------	-----------------------------------	-------------------	-----------------








a,26-Electrical,22-Fire Suppression

b,01-Soil Treatment,03-Concrete

ightweight

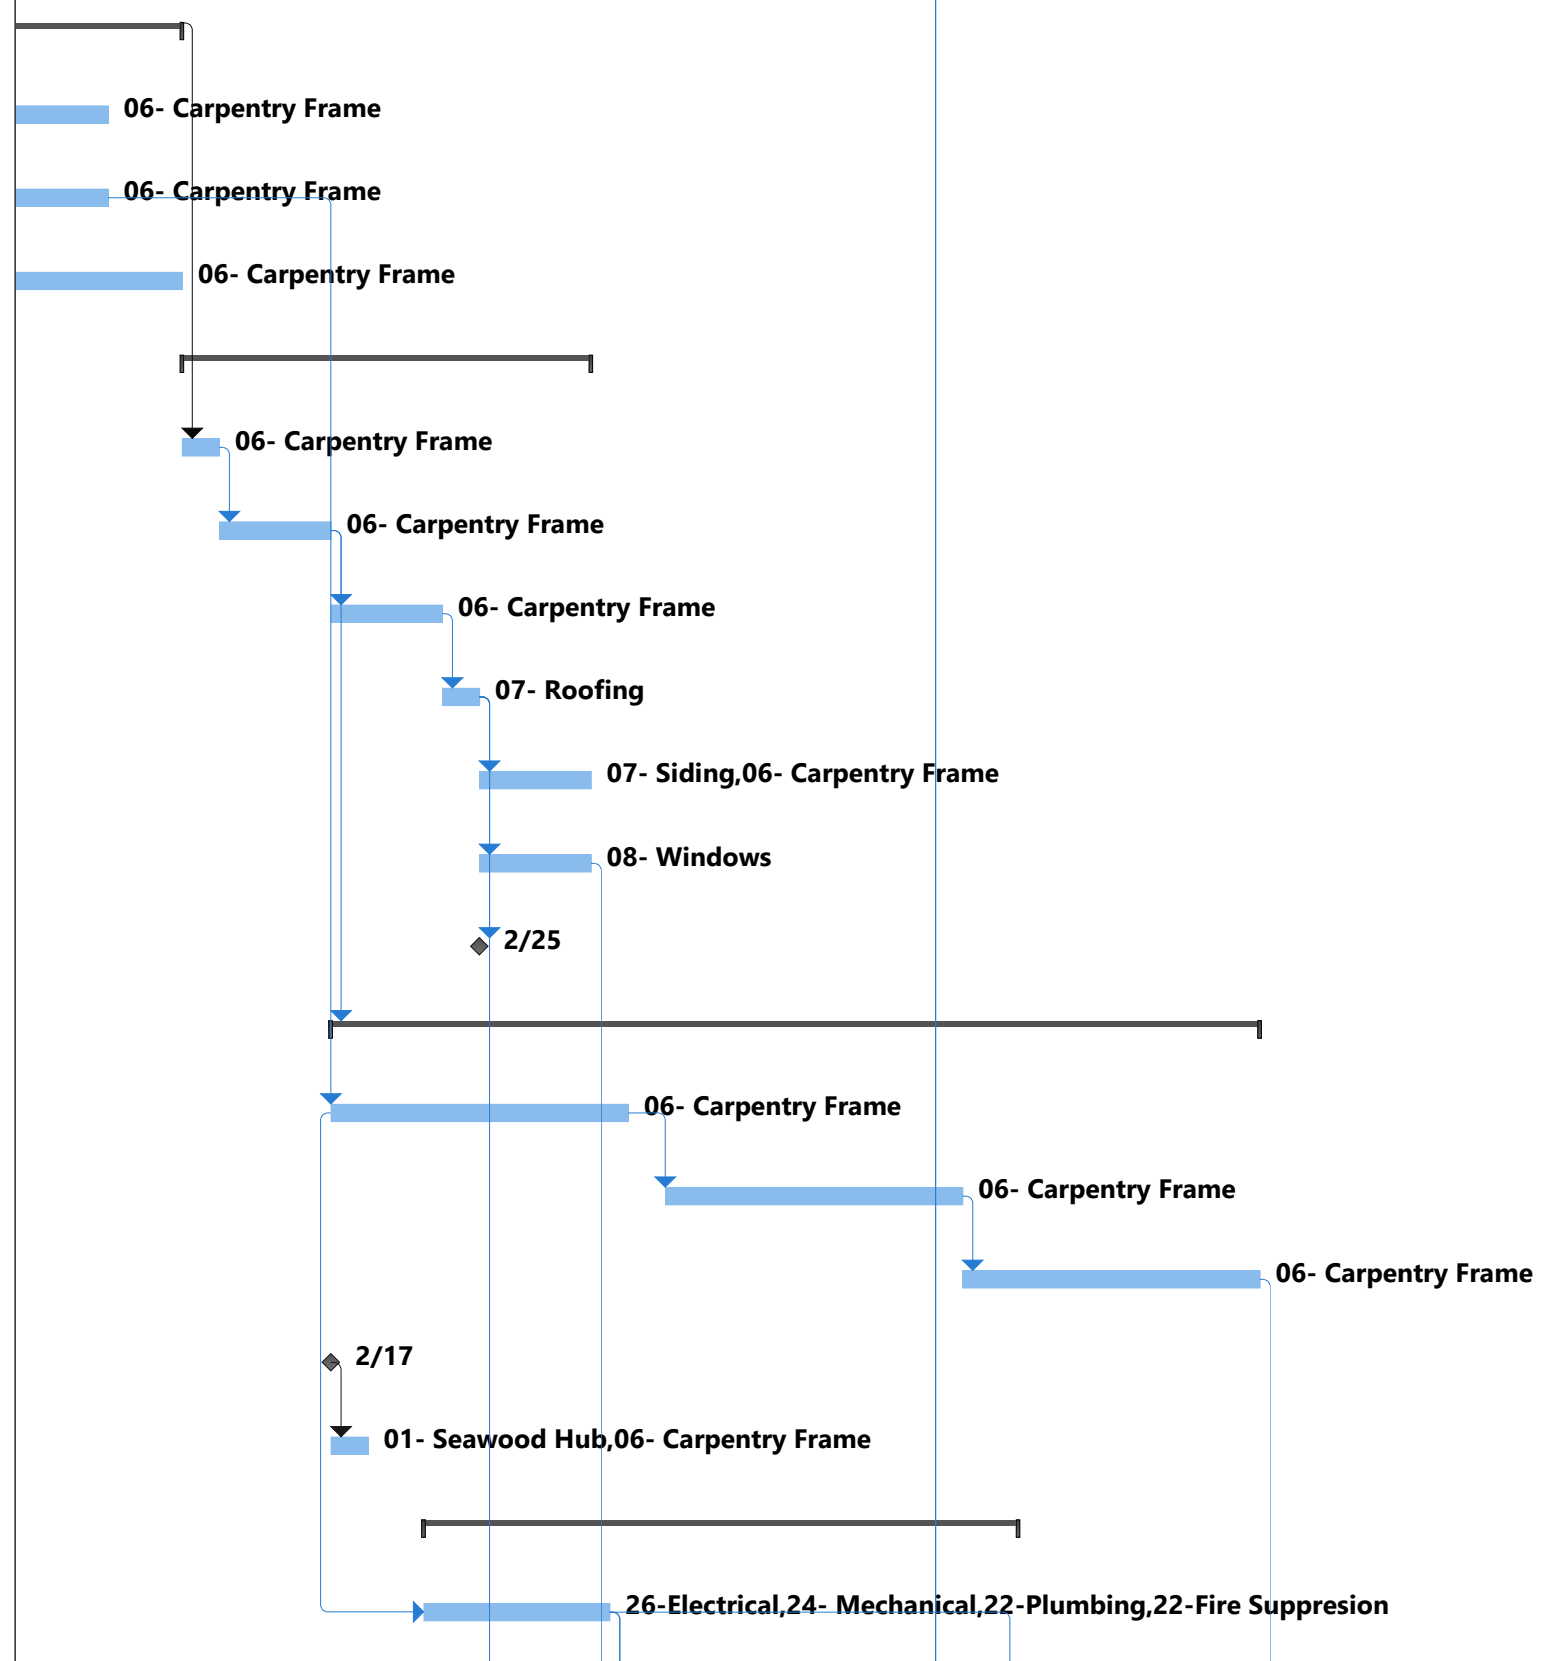

Project: Scenario-03- Early Delie
Date: Mon 7/20/20

