



ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Gantt Chart								
										Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3	
0		Update 12-3-20 Start 1-4-20 Scheule	760 days	Fri 12/6/19	Thu 11/3/22	Fri 12/6/19	NA	0%		[Gantt Bar]								
1		Championsgate/Lynwind	402 days	Fri 12/6/19	Mon 6/21/21	Fri 12/6/19	NA	0%		[Gantt Bar]								
571		Construction Schedule	478 days	Mon 1/4/21	Thu 11/3/22	NA	NA	0%		[Gantt Bar]								
572		Site Development	245 days	Mon 1/4/21	Mon 12/13/21	NA	NA	0%	55,93FS+26 days	[Gantt Bar]								
573		Clear Silt Fence Line	5 days	Tue 1/5/21	Mon 1/11/21	NA	NA	0%		[Gantt Bar]								
574		SWPP/Roadway/Silt Fence/Boundary	4 days	Thu 1/7/21	Tue 1/12/21	NA	NA	0%	573SS+2 days	[Gantt Bar]								
575		Clear/Grub Site Area	12 days	Wed 1/13/21	Thu 1/28/21	NA	NA	0%	574	[Gantt Bar]								
576		Construction Fence	4 days	Tue 1/19/21	Fri 1/22/21	NA	NA	0%	575SS+4 days	[Gantt Bar]								
577		Construction Entrance/Road- Grey Heron	5 days	Tue 1/12/21	Mon 1/18/21	NA	NA	0%	573	[Gantt Bar]								
578		Survey-Pond Boundary- West	5 days	Fri 1/29/21	Thu 2/4/21	NA	NA	0%	577,575	[Gantt Bar]								
579		Survey Entrance-Headwall Town center	1 day	Tue 1/19/21	Tue 1/19/21	NA	NA	0%	577	[Gantt Bar]								
580		Pond Construction -De-water Backfill	15 days	Fri 2/5/21	Thu 2/25/21	NA	NA	0%		[Gantt Bar]								
581		Set Coffe Cell Town Center elevation 103	4 days	Fri 2/5/21	Wed 2/10/21	NA	NA	0%	578	[Gantt Bar]								
582		Set Discharge Line-Pumps to Sediment Pond Entry Grey Heron	3 days	Mon 2/8/21	Wed 2/10/21	NA	NA	0%	581SS+1 day	[Gantt Bar]								
583		Set Testing-Flock and prepare Discharge into Southwestern Pond GreyHeron	4 days	Thu 2/11/21	Tue 2/16/21	NA	NA	0%	582SS+3 days	[Gantt Bar]								
584		De-water operations Eastern Pond through Entry- Draw Down Eastern Pond	7 days	Wed 2/17/21	Thu 2/25/21	NA	NA	0%	583	[Gantt Bar]								
585		Town Center Entry	18 days	Wed 2/24/21	Fri 3/19/21	NA	NA	0%		[Gantt Bar]								
586		Set 60" RCP Entry	5 days	Wed 2/24/21	Tue 3/2/21	NA	NA	0%	584SS+5 days	[Gantt Bar]								
587		Construct Headwall Town Center	10 days	Wed 3/3/21	Tue 3/16/21	NA	NA	0%	586	[Gantt Bar]								
588		Backfill Headwall-	3 days	Wed 3/17/21	Fri 3/19/21	NA	NA	0%	587	[Gantt Bar]								
589		Excavate Sediment-Eastern Pond	9 days	Fri 2/26/21	Wed 3/10/21	NA	NA	0%	584	[Gantt Bar]								
590		Excavate Sediment- Pond East bottom	7 days	Fri 2/26/21	Mon 3/8/21	NA	NA	0%	584	[Gantt Bar]								
591		Haul Off Spoils	8 days	Mon 3/1/21	Wed 3/10/21	NA	NA	0%	590SS+1 day	[Gantt Bar]								
592		Stabilize Pond Bottom	2 days	Tue 3/9/21	Wed 3/10/21	NA	NA	0%	590	[Gantt Bar]								
593		Inspect And Approve Backfill Operations	0 days	Wed 3/10/21	Wed 3/10/21	NA	NA	0%		[Gantt Bar]								
594		EOR Review	0 days	Wed 3/10/21	Wed 3/10/21	NA	NA	0%	592	[Gantt Bar]								
595		GEOTEch Review-Inspect	0 days	Wed 3/10/21	Wed 3/10/21	NA	NA	0%	594	[Gantt Bar]								
596		Retaining Wall -West Bldg 1-2 to Headwall	37 days	Thu 3/11/21	Fri 4/30/21	NA	NA	0%		[Gantt Bar]								
597		Excavate Retaining Wall Foundation	5 days	Thu 3/11/21	Wed 3/17/21	NA	NA	0%	589,590	[Gantt Bar]								
598		Set Big Blcok Ret.	15 days	Thu 3/18/21	Wed 4/7/21	NA	NA	0%	597	[Gantt Bar]								
599		Backfill GEOTECH Soils and Drainage- concurrent Backfill	9 days	Thu 4/15/21	Tue 4/27/21	NA	NA	0%	598,611SS	[Gantt Bar]								
600		Cast Cap-	3 days	Wed 4/28/21	Fri 4/30/21	NA	NA	0%	599	[Gantt Bar]								
601		Retaining Wall -East Clubhouse-Amenity	46 days	Tue 5/25/21	Tue 7/27/21	NA	NA	0%		[Gantt Bar]								
602		Excavate Retaining Wall Foundation	18 days	Tue 5/25/21	Thu 6/17/21	NA	NA	0%	618	[Gantt Bar]								
603		Set Big Block	21 days	Fri 6/18/21	Fri 7/16/21	NA	NA	0%	602	[Gantt Bar]								
604		Backfill Geotech Soils and Drainage- concurrent Backfill	15 days	Fri 6/25/21	Thu 7/15/21	NA	NA	0%	603SS+5 days	[Gantt Bar]								
605		Cast Caps	8 days	Fri 7/16/21	Tue 7/27/21	NA	NA	0%	604	[Gantt Bar]								
606		Pond Construction -Main Eastern	18 days	Mon 3/22/21	Wed 4/14/21	NA	NA	0%		[Gantt Bar]								

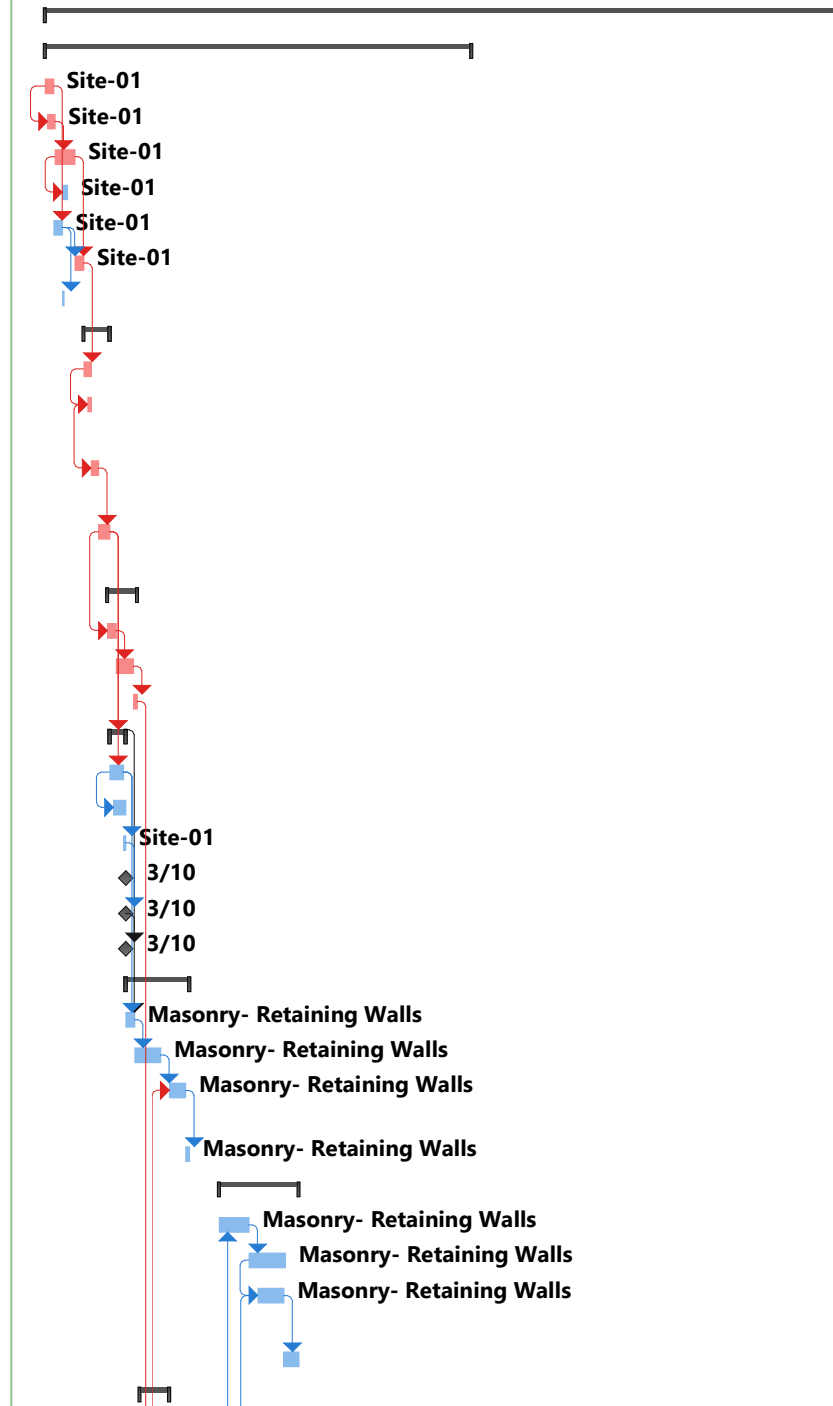


Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021	Q1	Q2	Q3	Q4	2022	Q1	Q2	Q3
607	➔	Excavate Boundary At Retaining Walls East of Headwall Entry	12 days	Mon 3/22/21	Tue 4/6/21	NA	NA	0%	588										
608	➔	Layback Trench at Wall Foudnation	6 days	Wed 4/7/21	Wed 4/14/21	NA	NA	0%	607										
609	➔	Borrow- To Western Pond	43 days	Thu 4/15/21	Mon 6/14/21	NA	NA	0%											
610	➔	Excavation- Haul Place to Eastern Pond	30 days	Thu 4/15/21	Wed 5/26/21	NA	NA	0%	608										
611	➔	Backfill Operation at Retainign Wall Concurrent to Geodrainge fill	13 days	Thu 4/15/21	Mon 5/3/21	NA	NA	0%	610SS										
612	➔	Backfill Pond Western Bldg 1-2	30 days	Tue 5/4/21	Mon 6/14/21	NA	NA	0%	611										
613	➔	Borrow to Eastern Wall	15 days	Fri 6/25/21	Thu 7/15/21	NA	NA	0%											
614	➔	Backfill Retaining wall East	15 days	Fri 6/25/21	Thu 7/15/21	NA	NA	0%	604SS										
615	➔	Backfil and Grade- Clubhouse	5 days	Fri 7/9/21	Thu 7/15/21	NA	NA	0%	614FF										
616	➔	De-water at Retaining Wall Foundation-East	36 days	Wed 4/7/21	Wed 5/26/21	NA	NA	0%											
617	➔	Set Sump- Connect to Sediment Discharge	2 days	Wed 4/7/21	Thu 4/8/21	NA	NA	0%	607										
618	➔	Continue De-watering plus 1' below WallFoundation at 105/99.00 elevation	32 days	Fri 4/9/21	Mon 5/24/21	NA	NA	0%	617										
619	➔	Stabilize slope/rough grade backinto open pond	2 days	Tue 5/25/21	Wed 5/26/21	NA	NA	0%	618										
620	➔	Retaining Wall -CIP at Lawn/Bridgeway	22 days	Fri 7/16/21	Mon 8/16/21	NA	NA	0%											
621	➔	Excavate Retaining Wall Foundation -	3 days	Fri 7/16/21	Tue 7/20/21	NA	NA	0%	607,614										
622	➔	Set Rebar	2 days	Thu 7/22/21	Fri 7/23/21	NA	NA	0%	621SS+4 days										
623	➔	Inspect Foundation	0 days	Tue 7/27/21	Tue 7/27/21	NA	NA	0%	622SS+4 days										
624	➔	Cast Foundation	1 day	Wed 7/28/21	Wed 7/28/21	NA	NA	0%	623SS										
625	➔	Set Forms	5 days	Mon 8/2/21	Fri 8/6/21	NA	NA	0%	624SS+3 days										
626	➔	Inspect/Bar-Cast-Strip	6 days	Mon 8/9/21	Mon 8/16/21	NA	NA	0%	625										
627	➔	Town Center/Grey Heron	63 days	Tue 1/5/21	Thu 4/1/21	NA	NA	0%											
628	➔	Submittals	63 days	Tue 1/5/21	Thu 4/1/21	NA	NA	0%											
638	➔	48 hour Lane Closure process established	21 days	Tue 1/5/21	Tue 2/2/21	NA	NA	0%											
641	➔	Construction-Off site	35 days	Wed 2/3/21	Tue 3/23/21	NA	NA	0%											
642	➔	Lane Closure Notification East and West Lane at Median	2 days	Wed 2/3/21	Thu 2/4/21	NA	NA	0%	629										
643	➔	MOT Set Western lane	1 day	Fri 2/5/21	Fri 2/5/21	NA	NA	0%	642										
644	➔	MOT Set Eastern lane	1 day	Mon 2/8/21	Mon 2/8/21	NA	NA	0%	643										
645	➔	Excavate Roadway Media	2 days	Tue 2/9/21	Wed 2/10/21	NA	NA	0%	644										
646	➔	Tie-in Stabilizer	2 days	Thu 2/11/21	Fri 2/12/21	NA	NA	0%	645										
647	➔	PDOT Inspect/ Soils test	1 day	Mon 2/15/21	Mon 2/15/21	NA	NA	0%	646										
648	➔	Concrete Curb Install	1 day	Tue 2/16/21	Tue 2/16/21	NA	NA	0%	647										
649	➔	Tie-In Base	1 day	Wed 2/17/21	Wed 2/17/21	NA	NA	0%	648										
650	➔	Asphalt	1 day	Thu 2/18/21	Thu 2/18/21	NA	NA	0%	649										
651	➔	Asphalt Cure	14 days	Fri 2/19/21	Wed 3/10/21	NA	NA	0%	650										
652	➔	Temp stripe	1 day	Fri 2/19/21	Fri 2/19/21	NA	NA	0%	650										
653	➔	Data/Telephone- Entry-Griffin	33 days	Fri 2/5/21	Tue 3/23/21	NA	NA	0%											
654	➔	ATT/Cable Provider Extend Service Lateral Across Griffin	5 days	Fri 2/5/21	Thu 2/11/21	NA	NA	0%	642										
655	➔	Extend Service lateral Into Site	14 days	Fri 2/12/21	Wed 3/3/21	NA	NA	0%	654										

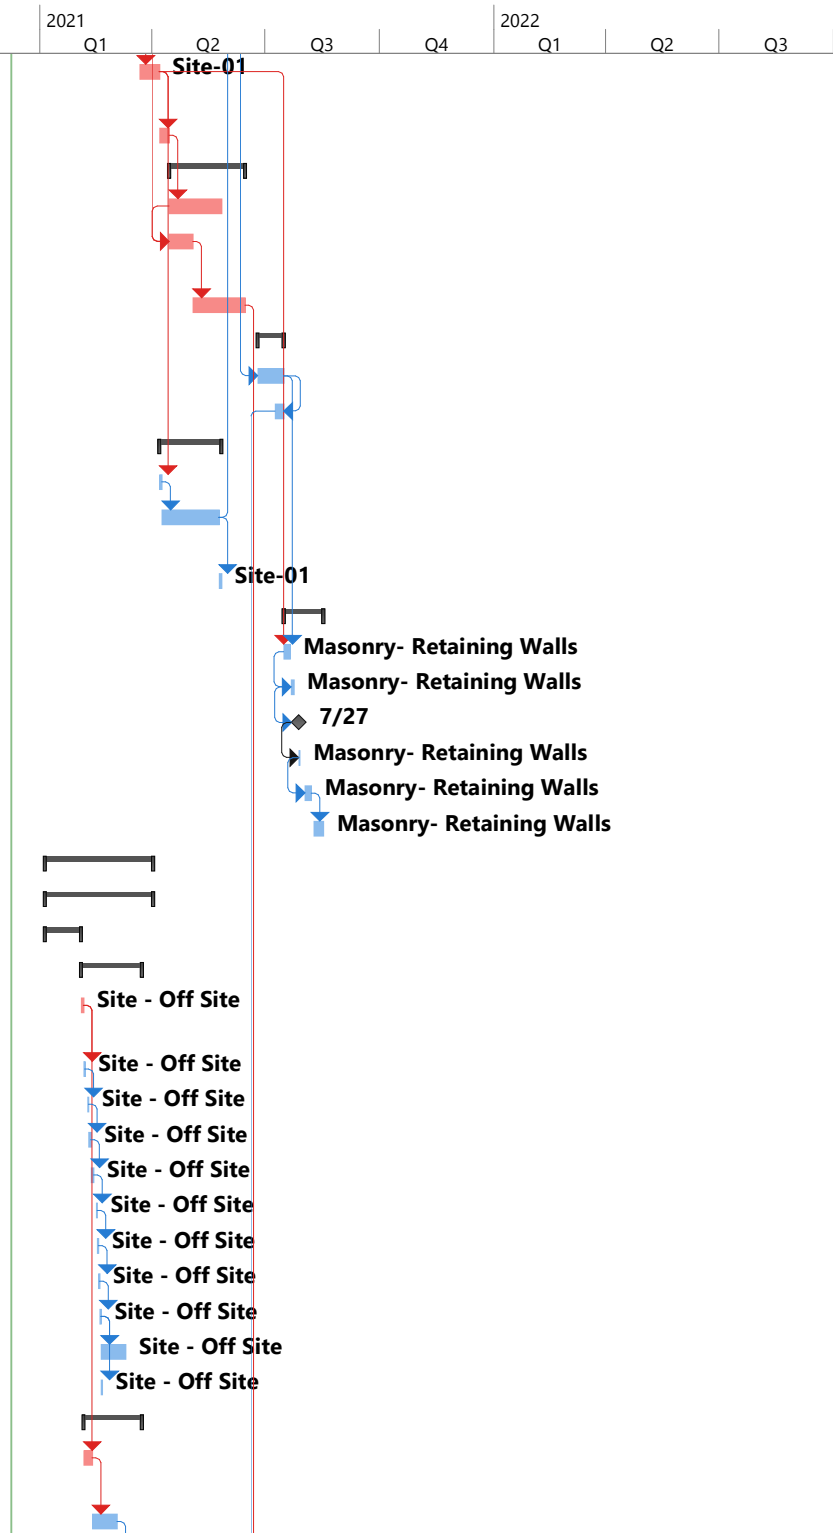


Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3
656		Extend Site conduit to each Bldg.	14 days	Thu 3/4/21	Tue 3/23/21	NA	NA	0%	655								
657		Site Earthwork	130 days	Tue 6/15/21	Mon 12/13/21	NA	NA	0%									
658		Import Clubhouse- Through Bldg. Pad.	0 days	Fri 7/9/21	Fri 7/9/21	NA	NA	0%	615SS								
659		Import Apartment Building Pads	53 days	Tue 6/15/21	Thu 8/26/21	NA	NA	0%	612								
660		Bldg. Pads- 6&3	12 days	Tue 6/15/21	Wed 6/30/21	NA	NA	0%	659SS								
661		Bldg. Pads- 4&1	18 days	Fri 8/27/21	Tue 9/21/21	NA	NA	0%	659								
662		Bldg. pads 5&2	18 days	Wed 9/22/21	Fri 10/15/21	NA	NA	0%	661,660								
663		Build Roadway through Stabilizer	21 days	Mon 10/18/21	Mon 11/15/21	NA	NA	0%	662								
664		Build Maintenance Bldg. Pad	2 days	Tue 11/16/21	Wed 11/17/21	NA	NA	0%	663								
665		Grade Slopes at Retention Ponds/Stabilize	18 days	Thu 11/18/21	Mon 12/13/21	NA	NA	0%	664								
666		Site Utilities	194 days	Tue 1/5/21	Fri 10/1/21	NA	NA	0%									
724		Roadway Paving	60 days	Tue 1/5/21	Mon 3/29/21	NA	NA	0%									
733		Boardwalk	20 days	Mon 1/4/21	Mon 2/1/21	NA	NA	0%									
741		Pool	50 days	Tue 1/5/21	Mon 3/15/21	NA	NA	0%									
765		Install Security access gates	51 days	Mon 1/25/21	Mon 4/5/21	NA	NA	0%									
770		Site Amenities, Landscape, Hardscape and Ponds	58 days	Tue 2/16/21	Thu 5/6/21	NA	NA	0%									
774		Landscape-Irrigation	61 days	Mon 1/25/21	Mon 4/19/21	NA	NA	0%									
782		Mail Kiosk 1-2	39 days	Tue 3/16/21	Fri 5/7/21	NA	NA	0%									
788		Clubhouse	161 days	Fri 7/9/21	Fri 2/18/22	NA	NA	0%									
844		Dog Spa- Maintenance Building	81 days	Thu 11/18/21	Thu 3/10/22	NA	NA	0%									
896		Apartments	336 days	Thu 7/22/21	Thu 11/3/22	NA	NA	0%									
897		Apartment Building Six	193 days	Thu 7/22/21	Mon 4/18/22	NA	NA	0%									
898		Survey Pad	1 day	Thu 7/22/21	Thu 7/22/21	NA	NA	0%	660FS+15 days								
899		Concrete- SOG	20 days	Fri 7/23/21	Thu 8/19/21	NA	NA	0%									
900		Batter Boards	2 days	Fri 7/23/21	Mon 7/26/21	NA	NA	0%	898								
901		Form SOG	5 days	Tue 7/27/21	Mon 8/2/21	NA	NA	0%	900								
902		Final Grade +/- .10	1 day	Tue 8/3/21	Tue 8/3/21	NA	NA	0%	901								
903		MEP Underground Rough	5 days	Wed 8/4/21	Tue 8/10/21	NA	NA	0%	902								
904		Inspection mep Undgrd	0 days	Tue 8/10/21	Tue 8/10/21	NA	NA	0%	903								
905		Treat, Reinforce, Inspect, and Pour SOG	5 days	Wed 8/11/21	Tue 8/17/21	NA	NA	0%	904								
906		Curing Compound/Cut Slab	1 day	Wed 8/18/21	Wed 8/18/21	NA	NA	0%	905								
907		Strip and Clean	1 day	Thu 8/19/21	Thu 8/19/21	NA	NA	0%	906								
908		Elevator Pit	12 days	Fri 7/23/21	Mon 8/9/21	NA	NA	0%									
909		Excavate	1 day	Fri 7/23/21	Fri 7/23/21	NA	NA	0%	898								
910		Set Sump Roughin	1 day	Mon 7/26/21	Mon 7/26/21	NA	NA	0%	909								
911		Set Bar- Inspect- Cast Slab	2 days	Tue 7/27/21	Wed 7/28/21	NA	NA	0%	910								
912		Set Form Walls	2 days	Thu 7/29/21	Fri 7/30/21	NA	NA	0%	911								
913		Roughin E&P Walls	1 day	Mon 8/2/21	Mon 8/2/21	NA	NA	0%	912								
914		Set Bar- Inspect-Pour	3 days	Tue 8/3/21	Thu 8/5/21	NA	NA	0%	913								
915		Strip-Backfill-	2 days	Fri 8/6/21	Mon 8/9/21	NA	NA	0%	914								
916		CMU Elevator Shaft	72 days	Fri 8/6/21	Mon 11/15/21	NA	NA	0%									
917		1st Floor	9 days	Fri 8/6/21	Wed 8/18/21	NA	NA	0%									

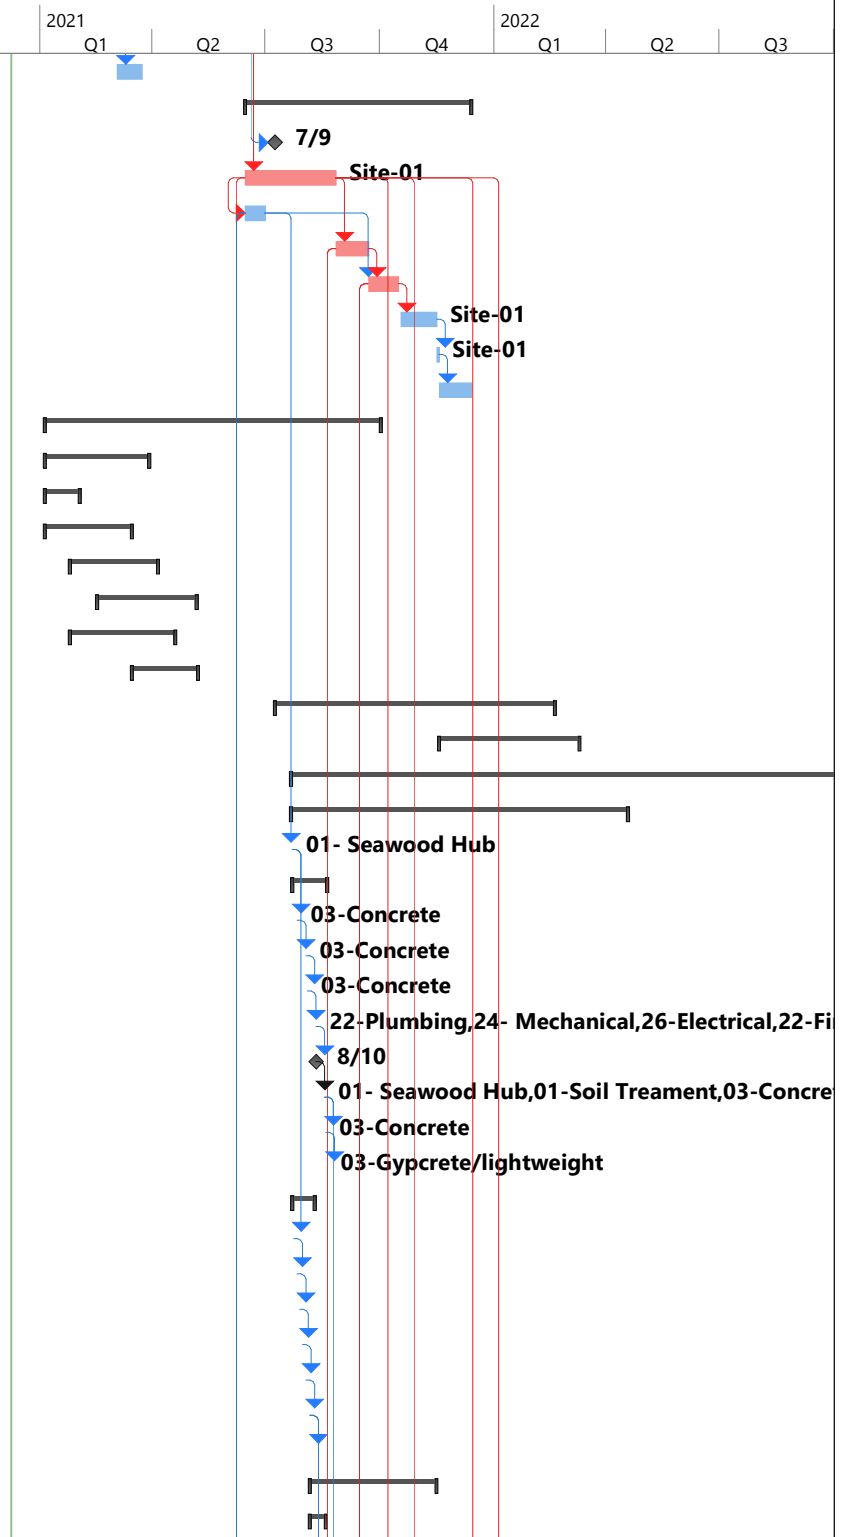

Project Update- 12-3-20 Project Start 1-4-21	Task	Inactive Task	Manual Summary Rollup	External Milestone	Critical
	Split	Inactive Milestone	Manual Summary	Deadline	Critical Split
	Milestone	Inactive Summary	Start-only	Path Driving Predecessor Milestone Task	Progress
	Summary	Manual Task	Finish-only	Path Driving Predecessor Summary Task	Manual Progress
	Project Summary	Duration-only	External Tasks	Path Driving Predecessor Normal Task	

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3
918	→	CMU through Bond Beam	3 days	Fri 8/6/21	Tue 8/10/21	NA	NA	0%	914								
919	→	Bar and Inspect Pads	2 days	Wed 8/11/21	Thu 8/12/21	NA	NA	0%	918								
920	→	Inspect	0 days	Thu 8/12/21	Thu 8/12/21	NA	NA	0%	919								
921	→	Cast-Grout Mix 300psi	1 day	Fri 8/13/21	Fri 8/13/21	NA	NA	0%	920								
922	→	Bond Beam Set-Bar-Inspect	2 days	Mon 8/16/21	Tue 8/17/21	NA	NA	0%	921								
923	→	Cast Bond Beam	1 day	Wed 8/18/21	Wed 8/18/21	NA	NA	0%	922								
924	→	2nd Floor	9 days	Tue 9/21/21	Fri 10/1/21	NA	NA	0%									
925	→	CMU through Bond Beam	3 days	Tue 9/21/21	Thu 9/23/21	NA	NA	0%	923,948								
926	→	Bar and Inspect Pads	2 days	Fri 9/24/21	Mon 9/27/21	NA	NA	0%	925								
927	→	Inspect	0 days	Mon 9/27/21	Mon 9/27/21	NA	NA	0%	926								
928	→	Cast-Grout Mix 300psi	1 day	Tue 9/28/21	Tue 9/28/21	NA	NA	0%	927								
929	→	Bond Beam Set-Bar-Inspect	2 days	Wed 9/29/21	Thu 9/30/21	NA	NA	0%	928								
930	→	Cast Bond Beam	1 day	Fri 10/1/21	Fri 10/1/21	NA	NA	0%	929								
931	→	3rd Floor	9 days	Thu 10/7/21	Tue 10/19/21	NA	NA	0%									
932	→	CMU through Bond Beam	3 days	Thu 10/7/21	Mon 10/11/21	NA	NA	0%	930,948,949								
933	→	Bar and Inspect Pads	2 days	Tue 10/12/21	Wed 10/13/21	NA	NA	0%	932								
934	→	Inspect	0 days	Wed 10/13/21	Wed 10/13/21	NA	NA	0%	933								
935	→	Cast-Grout Mix 300psi	1 day	Thu 10/14/21	Thu 10/14/21	NA	NA	0%	934								
936	→	Bond Beam Set-Bar-Inspect	2 days	Fri 10/15/21	Mon 10/18/21	NA	NA	0%	935								
937	→	Cast Bond Beam	1 day	Tue 10/19/21	Tue 10/19/21	NA	NA	0%	936								
938	→	4th Floor-Thru Rooftop	14 days	Wed 10/27/21	Mon 11/15/21	NA	NA	0%									
939	→	CMU through Bond Beam	3 days	Wed 10/27/21	Fri 10/29/21	NA	NA	0%	937,949,950								
940	→	Bar and Inspect Pads	2 days	Mon 11/1/21	Tue 11/2/21	NA	NA	0%	939								
941	→	Inspect	0 days	Tue 11/2/21	Tue 11/2/21	NA	NA	0%	940								
942	→	Cast-Grout Mix 300psi	1 day	Wed 11/3/21	Wed 11/3/21	NA	NA	0%	941								
943	→	Bond Beam Set-Bar-Inspect	2 days	Thu 11/4/21	Fri 11/5/21	NA	NA	0%	942								
944	→	Cast Bond Beam	1 day	Mon 11/8/21	Mon 11/8/21	NA	NA	0%	943								
945	→	Form Roof-Bar-Inspect-Cast- Reg. Mix 3000PSI	5 days	Tue 11/9/21	Mon 11/15/21	NA	NA	0%	944								
946	→	Exterior Frame	50 days	Wed 8/18/21	Tue 10/26/21	NA	NA	0%									
947	→	1st Floor- Joist	12 days	Wed 8/18/21	Thu 9/2/21	NA	NA	0%	905								
948	→	2nd Floor to Joist	12 days	Fri 9/3/21	Mon 9/20/21	NA	NA	0%	947								
949	→	3rd floor to Joist	12 days	Tue 9/21/21	Wed 10/6/21	NA	NA	0%	948								
950	→	4th floor to Joist	14 days	Thu 10/7/21	Tue 10/26/21	NA	NA	0%	949								
951	→	Roof Frame-Ext Dry-in	16 days	Wed 10/27/21	Wed 11/17/21	NA	NA	0%									
952	→	Set Truss Package	2 days	Wed 10/27/21	Thu 10/28/21	NA	NA	0%	950								
953	→	Frame Roof	4 days	Fri 10/29/21	Wed 11/3/21	NA	NA	0%	952								
954	→	Sheath Roof	4 days	Thu 11/4/21	Tue 11/9/21	NA	NA	0%	953								
955	→	Dry-In Roof	2 days	Wed 11/10/21	Thu 11/11/21	NA	NA	0%	954								
956	→	Tape and Seal Zip	4 days	Fri 11/12/21	Wed 11/17/21	NA	NA	0%	955								
957	→	Install Windows	4 days	Fri 11/12/21	Wed 11/17/21	NA	NA	0%	955								
958	→	Inspect Engineering with Tie-down and Sheathing	0 days	Thu 11/11/21	Thu 11/11/21	NA	NA	0%	955								

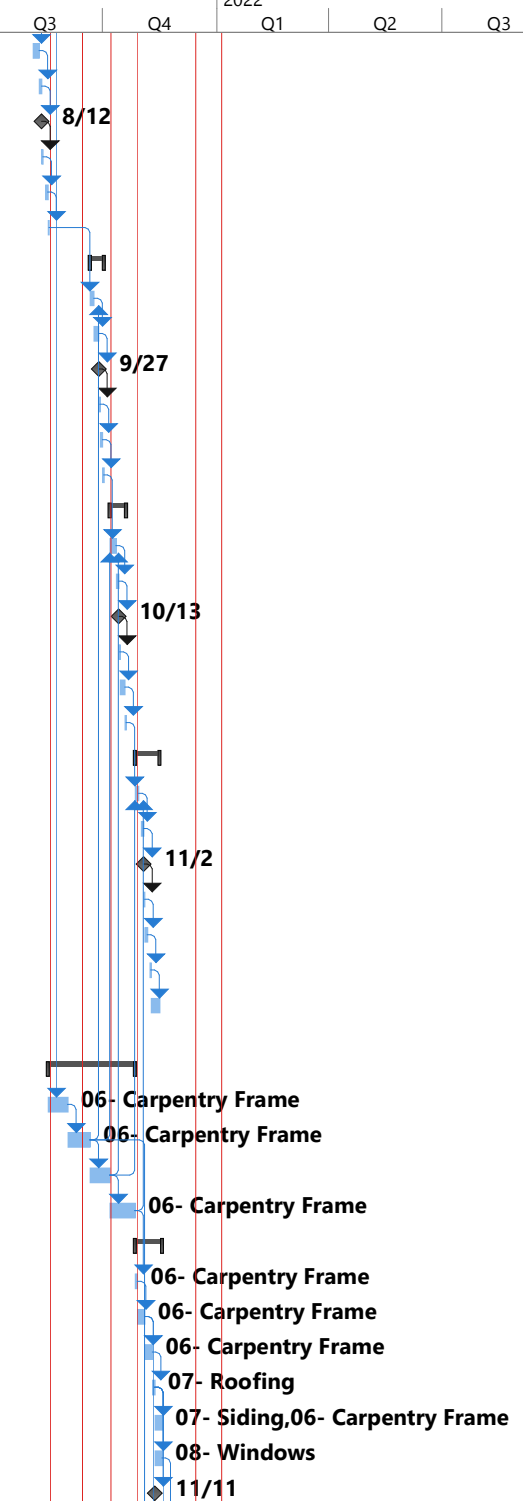

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task		


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Gantt Chart												
										Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3					
959		Interior Framing - Walls & Ceilings	48 days	Wed 11/3/21	Mon 1/10/22	NA	NA	0%	953													
960		1st Floor	12 days	Thu 11/4/21	Fri 11/19/21	NA	NA	0%	948													
961		2nd Floor	12 days	Mon 11/22/21	Tue 12/7/21	NA	NA	0%	960													
962		3rd Floor	12 days	Wed 12/8/21	Thu 12/23/21	NA	NA	0%	961													
963		4th Floor	12 days	Fri 12/24/21	Mon 1/10/22	NA	NA	0%	962													
964		Framing Inspection	0 days	Wed 11/3/21	Wed 11/3/21	NA	NA	0%														
965		Framing Punch Out	2 days	Thu 11/4/21	Fri 11/5/21	NA	NA	0%	964													
966		MEP Rough in	32 days	Tue 11/9/21	Wed 12/22/21	NA	NA	0%														
967		1st FI MEP F/S Rough Walls & Ceilings	8 days	Tue 11/9/21	Thu 11/18/21	NA	NA	0%	960SS+3 days													
968		Inspection	0 days	Thu 11/18/21	Thu 11/18/21	NA	NA	0%	967													
969		2nd FI MEP F/S Rough Walls & Ceilings	8 days	Fri 11/19/21	Tue 11/30/21	NA	NA	0%	967													
970		Inspection	0 days	Tue 11/30/21	Tue 11/30/21	NA	NA	0%	969													
971		3rd FI MEP F/S Rough Walls & Ceilings	8 days	Wed 12/1/21	Fri 12/10/21	NA	NA	0%	969													
972		Inspect	0 days	Fri 12/10/21	Fri 12/10/21	NA	NA	0%	971													
973		4th FI MEP F/S Rough Walls & Ceilings	8 days	Mon 12/13/21	Wed 12/22/21	NA	NA	0%	971													
974		Inspection	0 days	Wed 12/22/21	Wed 12/22/21	NA	NA	0%	973													
975		MEP F/S Rough Inspections	0 days	Wed 12/22/21	Wed 12/22/21	NA	NA	0%	967,969,973													
976		Gypcrete-Lightweight	30 days	Thu 12/23/21	Wed 2/2/22	NA	NA	0%														
977		2nd floor prep	5 days	Thu 12/23/21	Wed 12/29/21	NA	NA	0%	973													
978		2nd floor place GYP-crete	5 days	Thu 12/30/21	Wed 1/5/22	NA	NA	0%	977													
979		3rd Floor Prep	5 days	Thu 1/6/22	Wed 1/12/22	NA	NA	0%	978													
980		3rd Place Gypcrete	5 days	Thu 1/13/22	Wed 1/19/22	NA	NA	0%	979													
981		4th Floor Prep	5 days	Thu 1/20/22	Wed 1/26/22	NA	NA	0%	980													
982		4th Floor Gypcrete	5 days	Thu 1/27/22	Wed 2/2/22	NA	NA	0%	981													
983		Lightweight Hallways 2nd & 3rd	9 days	Thu 1/20/22	Tue 2/1/22	NA	NA	0%														
984		Prep 2nd Floor Hallway	2 days	Thu 1/20/22	Fri 1/21/22	NA	NA	0%	980													
985		Cast 2nd Floor Hallway	1 day	Mon 1/24/22	Mon 1/24/22	NA	NA	0%	984													
986		Prep 3rd Floor Hallway	2 days	Tue 1/25/22	Wed 1/26/22	NA	NA	0%	985													
987		Cast 3rd Floor Hallway	1 day	Thu 1/27/22	Thu 1/27/22	NA	NA	0%	986													
988		Prep 4th Floor Hallway	2 days	Fri 1/28/22	Mon 1/31/22	NA	NA	0%	987													
989		Cast 4th Floor Hallway	1 day	Tue 2/1/22	Tue 2/1/22	NA	NA	0%	988													
990		Lightweight Balconies	14 days	Tue 1/11/22	Fri 1/28/22	NA	NA	0%														
991		Prep/Waterproof 2nd Floor	4 days	Tue 1/11/22	Fri 1/14/22	NA	NA	0%	963													
992		Prep/Waterproof 3rd Floor	4 days	Mon 1/17/22	Thu 1/20/22	NA	NA	0%	991													
993		Cast 2nd Floor	2 days	Fri 1/21/22	Mon 1/24/22	NA	NA	0%	992													
994		Cast 3rd Floor	2 days	Tue 1/25/22	Wed 1/26/22	NA	NA	0%	993													
995		Prep/Waterproof 4th Floor	4 days	Fri 1/21/22	Wed 1/26/22	NA	NA	0%	992													
996		Cast 4th Floor	2 days	Thu 1/27/22	Fri 1/28/22	NA	NA	0%	994													
997		Cast Stair Pans	5 days	Mon 12/6/21	Fri 12/10/21	NA	NA	0%														
998		Stairwell Front	3 days	Mon 12/6/21	Wed 12/8/21	NA	NA	0%														
999		1st Through 2nd	1 day	Mon 12/6/21	Mon 12/6/21	NA	NA	0%	1008													
1000		2nd Thru 3rd	1 day	Tue 12/7/21	Tue 12/7/21	NA	NA	0%	999													



Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Gantt Chart												
										Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3					
1001	➔	3rd Thru 4th	1 day	Wed 12/8/21	Wed 12/8/21	NA	NA	0%	1000													
1002	➔	Stairwell Rear	3 days	Wed 12/8/21	Fri 12/10/21	NA	NA	0%														
1003	➔	1st Thru 2nd	1 day	Wed 12/8/21	Wed 12/8/21	NA	NA	0%	1000													
1004	➔	2nd Thru 3rd	1 day	Thu 12/9/21	Thu 12/9/21	NA	NA	0%	1003													
1005	➔	3rd Thru 4th	1 day	Fri 12/10/21	Fri 12/10/21	NA	NA	0%	1004													
1006	➔	Misc. Metals	56 days	Wed 11/17/21	Thu 2/3/22	NA	NA	0%														
1007	➔	Lead-Fabrication	0 days	Wed 11/17/21	Wed 11/17/21	NA	NA	0%	957													
1008	➔	Stairwell 1st thru 4th	12 days	Thu 11/18/21	Fri 12/3/21	NA	NA	0%	1007													
1009	➔	Railing 1st Thru 4th Stairwells	10 days	Tue 12/28/21	Mon 1/10/22	NA	NA	0%	1008,1022													
1010	➔	Railing Balconies 2nd floor	3 days	Fri 12/17/21	Tue 12/21/21	NA	NA	0%	1024													
1011	➔	Railing Balconies 3rd Floor	3 days	Thu 1/27/22	Mon 1/31/22	NA	NA	0%	1010,994													
1012	➔	Railing Balconies 4th Floor	3 days	Tue 2/1/22	Thu 2/3/22	NA	NA	0%	1011													
1013	➔	Exterior Finishes	35 days	Fri 11/12/21	Thu 12/30/21	NA	NA	0%														
1014	➔	Exterior Fascia	5 days	Fri 11/12/21	Thu 11/18/21	NA	NA	0%	955													
1015	➔	Set Exterior Stucco Band	4 days	Fri 11/19/21	Wed 11/24/21	NA	NA	0%	1014													
1016	➔	Roof	8 days	Thu 11/25/21	Mon 12/6/21	NA	NA	0%	1015													
1017	➔	Install Exterior Doors- Temp Lock	6 days	Fri 11/19/21	Fri 11/26/21	NA	NA	0%	1014													
1018	➔	Install Back Wall j-Molding	4 days	Fri 11/19/21	Wed 11/24/21	NA	NA	0%	1014													
1019	➔	Exterior Styrofoam Inserts	3 days	Thu 11/25/21	Mon 11/29/21	NA	NA	0%	1018													
1020	➔	Exterior Lathe -Stucco-	21 days	Fri 11/19/21	Fri 12/17/21	NA	NA	0%	1014													
1021	➔	Exterior Veneer	10 days	Fri 11/19/21	Thu 12/2/21	NA	NA	0%	1014													
1022	➔	Install Exterior Alum Soffit	6 days	Mon 12/20/21	Mon 12/27/21	NA	NA	0%	1020													
1023	➔	Prime and First Coat of Paint - Exterior	5 days	Fri 12/3/21	Thu 12/9/21	NA	NA	0%	1021													
1024	➔	Final Paint - Exterior	5 days	Fri 12/10/21	Thu 12/16/21	NA	NA	0%	1023													
1025	➔	Exterior Railing	2 days	Fri 12/17/21	Mon 12/20/21	NA	NA	0%	1024													
1026	➔	Temp Power	0 days	Thu 12/30/21	Thu 12/30/21	NA	NA	0%	826,1034													
1027	➔	Cast Exterior Sidewalks	8 days	Thu 11/25/21	Mon 12/6/21	NA	NA	0%	1020SS,1015													
1028	➔	Interior Finishes	100 days	Fri 11/19/21	Thu 4/7/22	NA	NA	0%														
1029	➔	Insulation and Inspection	35 days	Fri 11/19/21	Thu 1/6/22	NA	NA	0%														
1030	➔	1st Floor Insulation-Inspection	3 days	Fri 11/19/21	Tue 11/23/21	NA	NA	0%	968,1016SS-5 day													
1031	➔	2nd floor Insulation/ Inspection	3 days	Wed 12/1/21	Fri 12/3/21	NA	NA	0%	1030,969													
1032	➔	3rd Floor Insulation/ Inspection	3 days	Mon 12/13/21	Wed 12/15/21	NA	NA	0%	1031,971													
1033	➔	4th Floor Insulation/ Inspection	3 days	Thu 12/23/21	Mon 12/27/21	NA	NA	0%	1032,973													
1034	➔	Interior Zip-Hallway 1st thru 3rd	3 days	Tue 12/28/21	Thu 12/30/21	NA	NA	0%	1033													
1035	➔	Interior Stucco/Plaster over lathe- Hallway 1st Thru 3rd	5 days	Fri 12/31/21	Thu 1/6/22	NA	NA	0%	1034													
1036	➔	Drywall-GYP	46 days	Mon 11/22/21	Mon 1/24/22	NA	NA	0%														
1037	➔	1st Floor Hang- Finish Drywall	20 days	Mon 11/22/21	Fri 12/17/21	NA	NA	0%	1030SS+1 day													
1038	➔	Drywall Screw Inspection	0 days	Fri 12/17/21	Fri 12/17/21	NA	NA	0%	1037													
1039	➔	2nd Floor Hang- Finish Drywall	20 days	Thu 12/2/21	Wed 12/29/21	NA	NA	0%	1037SS+8 days													
1040	➔	Drywall Screw Inspection	0 days	Wed 12/29/21	Wed 12/29/21	NA	NA	0%	1039													
1041	➔	3rd Floor Hang- Finish Drywall	20 days	Tue 12/14/21	Mon 1/10/22	NA	NA	0%	1039SS+8 days													

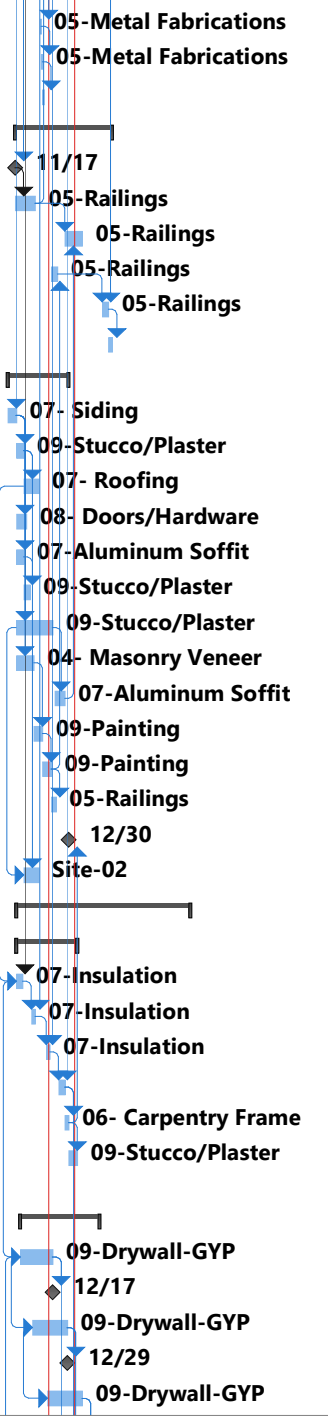

Project Update- 12-3-20
Project Start 1-4-21


Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Timeline													
										Q4	2021			2022			Q1	Q2	Q3				
1084	➔	Install Bath and Floor Tile	10 days	Tue 2/8/22	Mon 2/21/22	NA	NA	0%	1074														
1085	➔	Door Hardware Install	40 days	Thu 1/13/22	Wed 3/9/22	NA	NA	0%															
1086	➔	1st Floor	4 days	Thu 1/13/22	Tue 1/18/22	NA	NA	0%															
1087	➔	Install Door Hardware	4 days	Thu 1/13/22	Tue 1/18/22	NA	NA	0%	1061														
1088	➔	2nd Floor	4 days	Tue 2/22/22	Fri 2/25/22	NA	NA	0%															
1089	➔	Install Door Hardware	4 days	Tue 2/22/22	Fri 2/25/22	NA	NA	0%	1064														
1090	➔	3rd Floor	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%															
1091	➔	Install Door Hardware	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%	1067														
1092	➔	4th Floor	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%															
1093	➔	Install Door Hardware	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%	1091														
1094	➔	MEP Trim	40 days	Thu 1/13/22	Wed 3/9/22	NA	NA	0%															
1095	➔	1st Floor	4 days	Thu 1/13/22	Tue 1/18/22	NA	NA	0%															
1096	➔	MEP Trim	4 days	Thu 1/13/22	Tue 1/18/22	NA	NA	0%	1061														
1097	➔	2nd Floor	4 days	Tue 2/22/22	Fri 2/25/22	NA	NA	0%															
1098	➔	MEP Trim	4 days	Tue 2/22/22	Fri 2/25/22	NA	NA	0%	1064														
1099	➔	3rd Floor	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%															
1100	➔	MEP Trim	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%	1067														
1101	➔	4th Floor	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%															
1102	➔	MEP Trim	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%	1100														
1103	➔	MEPF Inspections	25 days	Fri 3/4/22	Thu 4/7/22	NA	NA	0%															
1104	➔	Final MEP Inspections	21 days	Fri 3/4/22	Fri 4/1/22	NA	NA	0%	1100,1096														
1105	➔	Equipment start up	4 days	Mon 4/4/22	Thu 4/7/22	NA	NA	0%	1104														
1106	➔	Install Flooring/Tile/LVT	40 days	Wed 1/19/22	Tue 3/15/22	NA	NA	0%															
1107	➔	1st Floor	4 days	Wed 1/19/22	Mon 1/24/22	NA	NA	0%															
1108	➔	Flooring	4 days	Wed 1/19/22	Mon 1/24/22	NA	NA	0%	1096														
1109	➔	2nd Floor	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%															
1110	➔	Flooring	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%	1098														
1111	➔	3rd Floor	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%															
1112	➔	Flooring	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%	1100														
1113	➔	4th Floor	4 days	Thu 3/10/22	Tue 3/15/22	NA	NA	0%															
1114	➔	Flooring	4 days	Thu 3/10/22	Tue 3/15/22	NA	NA	0%	1112														
1115	➔	Bath Accessories	40 days	Wed 1/19/22	Tue 3/15/22	NA	NA	0%															
1116	➔	1st Floor	4 days	Wed 1/19/22	Mon 1/24/22	NA	NA	0%															
1117	➔	Specialties-DIV 10	4 days	Wed 1/19/22	Mon 1/24/22	NA	NA	0%	1096														
1118	➔	2nd Floor	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%															
1119	➔	Specialties-DIV 10	4 days	Mon 2/28/22	Thu 3/3/22	NA	NA	0%	1098														
1120	➔	3rd Floor	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%															
1121	➔	Specialties-DIV 10	4 days	Fri 3/4/22	Wed 3/9/22	NA	NA	0%	1100														
1122	➔	4th Floor	4 days	Thu 3/10/22	Tue 3/15/22	NA	NA	0%															
1123	➔	Specialties-DIV 10	4 days	Thu 3/10/22	Tue 3/15/22	NA	NA	0%	1121														
1124	➔	Punch Walk Thru	5 days	Thu 3/10/22	Wed 3/16/22	NA	NA	0%															
1125	➔	Final Inspection-Building-Fire	3 days	Thu 3/10/22	Mon 3/14/22	NA	NA	0%	1121														

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3
1126	➔	Owner/A-E	2 days	Tue 3/15/22	Wed 3/16/22	NA	NA	0%	1125								
1127	➔	Inspections	0 days	Thu 3/3/22	Thu 3/3/22	NA	NA	0%									
1128	➔	Final Inspections	0 days	Thu 3/3/22	Thu 3/3/22	NA	NA	0%	1119								
1129	➔	Punch Out and Clean	23 days	Thu 3/17/22	Mon 4/18/22	NA	NA	0%									
1130	➔	1st Floor	5 days	Thu 3/17/22	Wed 3/23/22	NA	NA	0%									
1131	➔	Punch and Clean	5 days	Thu 3/17/22	Wed 3/23/22	NA	NA	0%	1126,1125								
1132	➔	2nd Floor	5 days	Thu 3/24/22	Wed 3/30/22	NA	NA	0%									
1133	➔	Punch and Clean	5 days	Thu 3/24/22	Wed 3/30/22	NA	NA	0%	1131								
1134	➔	3rd Floor	5 days	Thu 3/31/22	Wed 4/6/22	NA	NA	0%									
1135	➔	Punch and Clean	5 days	Thu 3/31/22	Wed 4/6/22	NA	NA	0%	1133								
1136	➔	4th Floor	8 days	Thu 4/7/22	Mon 4/18/22	NA	NA	0%									
1137	➔	Punch and Clean	8 days	Thu 4/7/22	Mon 4/18/22	NA	NA	0%	1135								
1138	➔	Apartment Building Three	193 days	Tue 7/27/21	Thu 4/21/22	NA	NA	0%									
1139	➔	Survey Pad	1 day	Tue 7/27/21	Tue 7/27/21	NA	NA	0%	659SS+30 days								
1140	➔	Concrete- SOG	20 days	Wed 7/28/21	Tue 8/24/21	NA	NA	0%									
1141	➔	Batter Boards	2 days	Wed 7/28/21	Thu 7/29/21	NA	NA	0%	1139								
1142	➔	Form SOG	5 days	Fri 7/30/21	Thu 8/5/21	NA	NA	0%	1141								
1143	➔	Final Grade +/- .10	1 day	Fri 8/6/21	Fri 8/6/21	NA	NA	0%	1142								
1144	➔	MEP Underground Rough	5 days	Mon 8/9/21	Fri 8/13/21	NA	NA	0%	1143								
1145	➔	Inspection mep Undgrd	0 days	Fri 8/13/21	Fri 8/13/21	NA	NA	0%	1144								
1146	➔	Treat, Reinforce, Inspect, and Pour SOG	5 days	Mon 8/16/21	Fri 8/20/21	NA	NA	0%	1145								
1147	➔	Curing Compound/Cut Slab	1 day	Mon 8/23/21	Mon 8/23/21	NA	NA	0%	1146								
1148	➔	Strip and Clean	1 day	Tue 8/24/21	Tue 8/24/21	NA	NA	0%	1147								
1149	➔	Elevator Pit	12 days	Wed 7/28/21	Thu 8/12/21	NA	NA	0%									
1150	➔	Excavate	1 day	Wed 7/28/21	Wed 7/28/21	NA	NA	0%	1139								
1151	➔	Set Sump Roughin	1 day	Thu 7/29/21	Thu 7/29/21	NA	NA	0%	1150								
1152	➔	Set Bar- Inspect- Cast Slab	2 days	Fri 7/30/21	Mon 8/2/21	NA	NA	0%	1151								
1153	➔	Set Form Walls	2 days	Tue 8/3/21	Wed 8/4/21	NA	NA	0%	1152								
1154	➔	Roughin E&P Walls	1 day	Thu 8/5/21	Thu 8/5/21	NA	NA	0%	1153								
1155	➔	Set Bar- Inspect-Pour	3 days	Fri 8/6/21	Tue 8/10/21	NA	NA	0%	1154								
1156	➔	Strip-Backfill-	2 days	Wed 8/11/21	Thu 8/12/21	NA	NA	0%	1155								
1157	➔	CMU Elevator Shaft	72 days	Wed 8/11/21	Thu 11/18/21	NA	NA	0%									
1158	➔	1st Floor	9 days	Wed 8/11/21	Mon 8/23/21	NA	NA	0%									
1159	➔	CMU through Bond Beam	3 days	Wed 8/11/21	Fri 8/13/21	NA	NA	0%	1155								
1160	➔	Bar and Inspect Pads	2 days	Mon 8/16/21	Tue 8/17/21	NA	NA	0%	1159								
1161	➔	Inspect	0 days	Tue 8/17/21	Tue 8/17/21	NA	NA	0%	1160								
1162	➔	Cast-Grout Mix 300psi	1 day	Wed 8/18/21	Wed 8/18/21	NA	NA	0%	1161								
1163	➔	Bond Beam Set-Bar-Inspect	2 days	Thu 8/19/21	Fri 8/20/21	NA	NA	0%	1162								
1164	➔	Cast Bond Beam	1 day	Mon 8/23/21	Mon 8/23/21	NA	NA	0%	1163								
1165	➔	2nd Floor	9 days	Fri 9/24/21	Wed 10/6/21	NA	NA	0%									
1166	➔	CMU through Bond Beam	3 days	Fri 9/24/21	Tue 9/28/21	NA	NA	0%	1164,1189								
1167	➔	Bar and Inspect Pads	2 days	Wed 9/29/21	Thu 9/30/21	NA	NA	0%	1166								

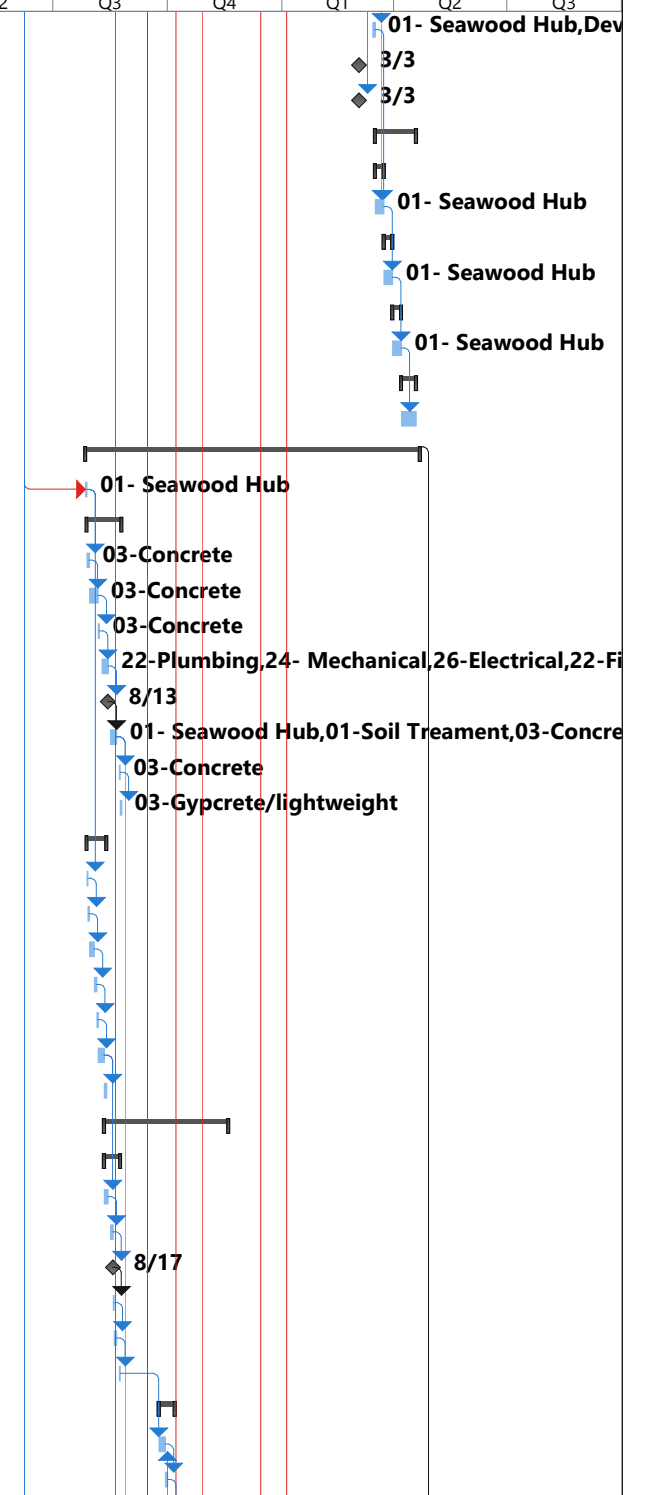


Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	2021				2022			
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
1209	→	Inspection	0 days	Tue 11/23/21	Tue 11/23/21	NA	NA	0%	1208					11/23			
1210	→	2nd FI MEP F/S Rough Walls & Ceilings	8 days	Wed 11/24/21	Fri 12/3/21	NA	NA	0%	1208					26-Electrical,24-Mechanical,22-Pl			
1211	→	Inspection	0 days	Fri 12/3/21	Fri 12/3/21	NA	NA	0%	1210					12/3			
1212	→	3rd FI MEP F/S Rough Walls & Ceilings	8 days	Mon 12/6/21	Wed 12/15/21	NA	NA	0%	1210					12/15			
1213	→	Inspect	0 days	Wed 12/15/21	Wed 12/15/21	NA	NA	0%	1212					26-Electrical,24-Mechanical,22			
1214	→	4th FI MEP F/S Rough Walls & Ceilings	8 days	Thu 12/16/21	Mon 12/27/21	NA	NA	0%	1212					12/27			
1215	→	Inspection	0 days	Mon 12/27/21	Mon 12/27/21	NA	NA	0%	1214					12/27			
1216	→	MEP F/S Rough Inspections	0 days	Mon 12/27/21	Mon 12/27/21	NA	NA	0%	1208,1210,1214								
1217	→	Gypcrete-Lightweight	30 days	Tue 12/28/21	Mon 2/7/22	NA	NA	0%									
1218	→	2nd floor prep	5 days	Tue 12/28/21	Mon 1/3/22	NA	NA	0%	1214					03-Gypcrete/lightweight			
1219	→	2nd floor place GYP-crete	5 days	Tue 1/4/22	Mon 1/10/22	NA	NA	0%	1218					03-Gypcrete/lightweight			
1220	→	3rd Floor Prep	5 days	Tue 1/11/22	Mon 1/17/22	NA	NA	0%	1219					03-Gypcrete/lightweight			
1221	→	3rd Place Gypcrete	5 days	Tue 1/18/22	Mon 1/24/22	NA	NA	0%	1220					03-Gypcrete/lightweight			
1222	→	4th Floor Prep	5 days	Tue 1/25/22	Mon 1/31/22	NA	NA	0%	1221								
1223	→	4th Floor Gypcrete	5 days	Tue 2/1/22	Mon 2/7/22	NA	NA	0%	1222								
1224	→	Lightweight Hallways 2nd & 3rd	9 days	Tue 1/25/22	Fri 2/4/22	NA	NA	0%									
1225	→	Prep 2nd Floor Hallway	2 days	Tue 1/25/22	Wed 1/26/22	NA	NA	0%	1221					03-Gypcrete/lightweight			
1226	→	Cast 2nd Floor Hallway	1 day	Thu 1/27/22	Thu 1/27/22	NA	NA	0%	1225					03-Gypcrete/lightweight			
1227	→	Prep 3rd Floor Hallway	2 days	Fri 1/28/22	Mon 1/31/22	NA	NA	0%	1226					03-Gypcrete/lightweight			
1228	→	Cast 3rd Floor Hallway	1 day	Tue 2/1/22	Tue 2/1/22	NA	NA	0%	1227					03-Gypcrete/lightweight			
1229	→	Prep 4th Floor Hallway	2 days	Wed 2/2/22	Thu 2/3/22	NA	NA	0%	1228								
1230	→	Cast 4th Floor Hallway	1 day	Fri 2/4/22	Fri 2/4/22	NA	NA	0%	1229								
1231	→	Lightweight Balconies	14 days	Fri 1/14/22	Wed 2/2/22	NA	NA	0%									
1232	→	Prep/Waterproof 2nd Floor	4 days	Fri 1/14/22	Wed 1/19/22	NA	NA	0%	1204					03-Gypcrete/lightweight			
1233	→	Prep/Waterproof 3rd Floor	4 days	Thu 1/20/22	Tue 1/25/22	NA	NA	0%	1232					03-Gypcrete/lightweight			
1234	→	Cast 2nd Floor	2 days	Wed 1/26/22	Thu 1/27/22	NA	NA	0%	1233					03-Gypcrete/lightweight			
1235	→	Cast 3rd Floor	2 days	Fri 1/28/22	Mon 1/31/22	NA	NA	0%	1234					03-Gypcrete/lightweight			
1236	→	Prep/Waterproof 4th Floor	4 days	Wed 1/26/22	Mon 1/31/22	NA	NA	0%	1233								
1237	→	Cast 4th Floor	2 days	Tue 2/1/22	Wed 2/2/22	NA	NA	0%	1235								
1238	→	Cast Stair Pans	5 days	Thu 12/9/21	Wed 12/15/21	NA	NA	0%									
1239	→	Stairwell Front	3 days	Thu 12/9/21	Mon 12/13/21	NA	NA	0%									
1240	→	1st Through 2nd	1 day	Thu 12/9/21	Thu 12/9/21	NA	NA	0%	1249					05-Metal Fabrications			
1241	→	2nd Thru 3rd	1 day	Fri 12/10/21	Fri 12/10/21	NA	NA	0%	1240					05-Metal Fabrications			
1242	→	3rd Thru 4th	1 day	Mon 12/13/21	Mon 12/13/21	NA	NA	0%	1241								
1243	→	Stairwell Rear	3 days	Mon 12/13/21	Wed 12/15/21	NA	NA	0%									
1244	→	1st Thru 2nd	1 day	Mon 12/13/21	Mon 12/13/21	NA	NA	0%	1241					05-Metal Fabrications			
1245	→	2nd Thru 3rd	1 day	Tue 12/14/21	Tue 12/14/21	NA	NA	0%	1244					05-Metal Fabrications			
1246	→	3rd Thru 4th	1 day	Wed 12/15/21	Wed 12/15/21	NA	NA	0%	1245								
1247	→	Misc. Metals	56 days	Mon 11/22/21	Tue 2/8/22	NA	NA	0%									
1248	→	Lead-Fabrication	0 days	Mon 11/22/21	Mon 11/22/21	NA	NA	0%	1198					11/22			
1249	→	Stairwell 1st thru 4th	12 days	Tue 11/23/21	Wed 12/8/21	NA	NA	0%	1248					05-Railings			
1250	→	Railing 1st Thru 4th Stairwells	10 days	Fri 12/31/21	Thu 1/13/22	NA	NA	0%	1249,1263					05-Railings			

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Timeline													
										Q4	2021			2022			Q1	Q2	Q3				
1334	➔	Install Door Hardware	4 days	Wed 3/9/22	Mon 3/14/22	NA	NA	0%	1332														
1335	➔	MEP Trim	40 days	Tue 1/18/22	Mon 3/14/22	NA	NA	0%															
1336	➔	1st Floor	4 days	Tue 1/18/22	Fri 1/21/22	NA	NA	0%															
1337	➔	MEP Trim	4 days	Tue 1/18/22	Fri 1/21/22	NA	NA	0%	1302														
1338	➔	2nd Floor	4 days	Fri 2/25/22	Wed 3/2/22	NA	NA	0%															
1339	➔	MEP Trim	4 days	Fri 2/25/22	Wed 3/2/22	NA	NA	0%	1305														
1340	➔	3rd Floor	4 days	Thu 3/3/22	Tue 3/8/22	NA	NA	0%															
1341	➔	MEP Trim	4 days	Thu 3/3/22	Tue 3/8/22	NA	NA	0%	1308														
1342	➔	4th Floor	4 days	Wed 3/9/22	Mon 3/14/22	NA	NA	0%															
1343	➔	MEP Trim	4 days	Wed 3/9/22	Mon 3/14/22	NA	NA	0%	1341														
1344	➔	MEPF Inspections	25 days	Wed 3/9/22	Tue 4/12/22	NA	NA	0%															
1345	➔	Final MEP Inspections	21 days	Wed 3/9/22	Wed 4/6/22	NA	NA	0%	1337,1341														
1346	➔	Equipment start up	4 days	Thu 4/7/22	Tue 4/12/22	NA	NA	0%	1345														
1347	➔	Install Flooring/Tile/LVT	40 days	Mon 1/24/22	Fri 3/18/22	NA	NA	0%															
1348	➔	1st Floor	4 days	Mon 1/24/22	Thu 1/27/22	NA	NA	0%															
1349	➔	Flooring	4 days	Mon 1/24/22	Thu 1/27/22	NA	NA	0%	1337														
1350	➔	2nd Floor	4 days	Thu 3/3/22	Tue 3/8/22	NA	NA	0%															
1351	➔	Flooring	4 days	Thu 3/3/22	Tue 3/8/22	NA	NA	0%	1339														
1352	➔	3rd Floor	4 days	Wed 3/9/22	Mon 3/14/22	NA	NA	0%															
1353	➔	Flooring	4 days	Wed 3/9/22	Mon 3/14/22	NA	NA	0%	1341														
1354	➔	4th Floor	4 days	Tue 3/15/22	Fri 3/18/22	NA	NA	0%															
1355	➔	Flooring	4 days	Tue 3/15/22	Fri 3/18/22	NA	NA	0%	1353														
1356	➔	Bath Accessories	40 days	Mon 1/24/22	Fri 3/18/22	NA	NA	0%															
1357	➔	1st Floor	4 days	Mon 1/24/22	Thu 1/27/22	NA	NA	0%															
1358	➔	Specialties-DIV 10	4 days	Mon 1/24/22	Thu 1/27/22	NA	NA	0%	1337														
1359	➔	2nd Floor	4 days	Thu 3/3/22	Tue 3/8/22	NA	NA	0%															
1360	➔	Specialties-DIV 10	4 days	Thu 3/3/22	Tue 3/8/22	NA	NA	0%	1339														
1361	➔	3rd Floor	4 days	Wed 3/9/22	Mon 3/14/22	NA	NA	0%															
1362	➔	Specialties-DIV 10	4 days	Wed 3/9/22	Mon 3/14/22	NA	NA	0%	1341														
1363	➔	4th Floor	4 days	Tue 3/15/22	Fri 3/18/22	NA	NA	0%															
1364	➔	Specialties-DIV 10	4 days	Tue 3/15/22	Fri 3/18/22	NA	NA	0%	1362														
1365	➔	Punch Walk Thru	5 days	Tue 3/15/22	Mon 3/21/22	NA	NA	0%															
1366	➔	Final Inspection-Building-Fire	3 days	Tue 3/15/22	Thu 3/17/22	NA	NA	0%	1362														
1367	➔	Owner/A-E	2 days	Fri 3/18/22	Mon 3/21/22	NA	NA	0%	1366														
1368	➔	Inspections	0 days	Tue 3/8/22	Tue 3/8/22	NA	NA	0%															
1369	➔	Final Inspections	0 days	Tue 3/8/22	Tue 3/8/22	NA	NA	0%	1360														
1370	➔	Punch Out and Clean	23 days	Tue 3/22/22	Thu 4/21/22	NA	NA	0%															
1371	➔	1st Floor	5 days	Tue 3/22/22	Mon 3/28/22	NA	NA	0%															
1372	➔	Punch and Clean	5 days	Tue 3/22/22	Mon 3/28/22	NA	NA	0%	1366,1367														
1373	➔	2nd Floor	5 days	Tue 3/29/22	Mon 4/4/22	NA	NA	0%															
1374	➔	Punch and Clean	5 days	Tue 3/29/22	Mon 4/4/22	NA	NA	0%	1372														
1375	➔	3rd Floor	5 days	Tue 4/5/22	Mon 4/11/22	NA	NA	0%															

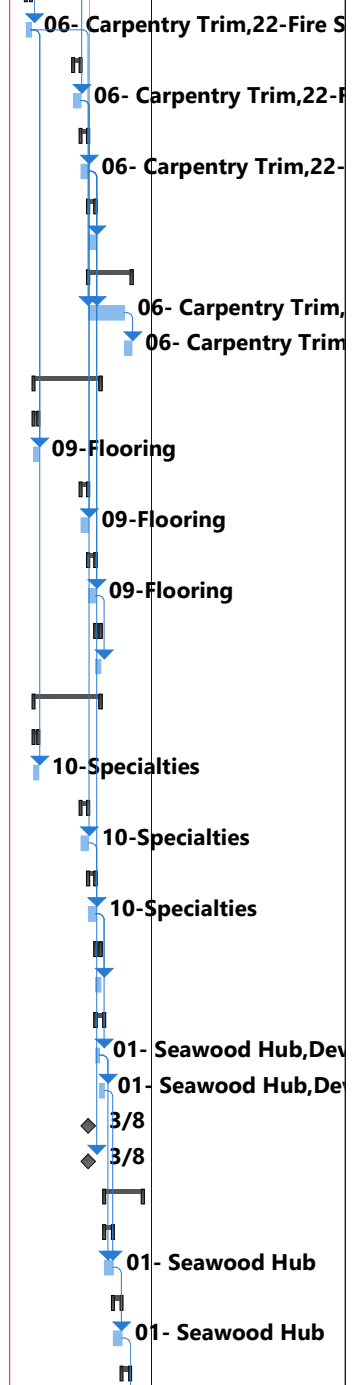

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	2021				2022					
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3		
1418	➔	Bond Beam Set-Bar-Inspect	2 days	Mon 1/3/22	Tue 1/4/22	NA	NA	0%	1417										
1419	➔	Cast Bond Beam	1 day	Wed 1/5/22	Wed 1/5/22	NA	NA	0%	1418										
1420	➔	4th Floor-Thru Rooftop	14 days	Thu 1/13/22	Tue 2/1/22	NA	NA	0%											
1421	➔	CMU through Bond Beam	3 days	Thu 1/13/22	Mon 1/17/22	NA	NA	0%	1419,1431,1432										
1422	➔	Bar and Inspect Pads	2 days	Tue 1/18/22	Wed 1/19/22	NA	NA	0%	1421										
1423	➔	Inspect	0 days	Wed 1/19/22	Wed 1/19/22	NA	NA	0%	1422										
1424	➔	Cast-Grout Mix 300psi	1 day	Thu 1/20/22	Thu 1/20/22	NA	NA	0%	1423										
1425	➔	Bond Beam Set-Bar-Inspect	2 days	Fri 1/21/22	Mon 1/24/22	NA	NA	0%	1424										
1426	➔	Cast Bond Beam	1 day	Tue 1/25/22	Tue 1/25/22	NA	NA	0%	1425										
1427	➔	Form Roof-Bar-Inspect-Cast- Reg. Mix 3000PSI	5 days	Wed 1/26/22	Tue 2/1/22	NA	NA	0%	1426										
1428	➔	Exterior Frame	50 days	Thu 11/4/21	Wed 1/12/22	NA	NA	0%											
1429	➔	1st Floor- Joist	12 days	Thu 11/4/21	Fri 11/19/21	NA	NA	0%	1387										
1430	➔	2nd Floor to Joist	12 days	Mon 11/22/21	Tue 12/7/21	NA	NA	0%	1429										
1431	➔	3rd floor to Joist	12 days	Wed 12/8/21	Thu 12/23/21	NA	NA	0%	1430										
1432	➔	4th floor to Joist	14 days	Fri 12/24/21	Wed 1/12/22	NA	NA	0%	1431										
1433	➔	Roof Frame-Ext Dry-in	16 days	Thu 1/13/22	Thu 2/3/22	NA	NA	0%											
1434	➔	Set Truss Package	2 days	Thu 1/13/22	Fri 1/14/22	NA	NA	0%	1432										
1435	➔	Frame Roof	4 days	Mon 1/17/22	Thu 1/20/22	NA	NA	0%	1434										
1436	➔	Sheath Roof	4 days	Fri 1/21/22	Wed 1/26/22	NA	NA	0%	1435										
1437	➔	Dry-In Roof	2 days	Thu 1/27/22	Fri 1/28/22	NA	NA	0%	1436										
1438	➔	Tape and Seal Zip	4 days	Mon 1/31/22	Thu 2/3/22	NA	NA	0%	1437										
1439	➔	Install Windows	4 days	Mon 1/31/22	Thu 2/3/22	NA	NA	0%	1437										
1440	➔	Inspect Engineering with Tie-down and Sheathing	0 days	Fri 1/28/22	Fri 1/28/22	NA	NA	0%	1437										
1441	➔	Interior Framing - Walls & Ceilings	48 days	Thu 1/20/22	Tue 3/29/22	NA	NA	0%	1435										
1442	➔	1st Floor	12 days	Fri 1/21/22	Mon 2/7/22	NA	NA	0%	1430										
1443	➔	2nd Floor	12 days	Tue 2/8/22	Wed 2/23/22	NA	NA	0%	1442										
1444	➔	3rd Floor	12 days	Thu 2/24/22	Fri 3/11/22	NA	NA	0%	1443										
1445	➔	4th Floor	12 days	Mon 3/14/22	Tue 3/29/22	NA	NA	0%	1444										
1446	➔	Framing Inspection	0 days	Thu 1/20/22	Thu 1/20/22	NA	NA	0%											
1447	➔	Framing Punch Out	2 days	Fri 1/21/22	Mon 1/24/22	NA	NA	0%	1446										
1448	➔	MEP Rough in	32 days	Wed 1/26/22	Thu 3/10/22	NA	NA	0%											
1449	➔	1st FI MEP F/S Rough Walls & Ceilings	8 days	Wed 1/26/22	Fri 2/4/22	NA	NA	0%	1442SS+3 days										
1450	➔	Inspection	0 days	Fri 2/4/22	Fri 2/4/22	NA	NA	0%	1449										
1451	➔	2nd FI MEP F/S Rough Walls & Ceilings	8 days	Mon 2/7/22	Wed 2/16/22	NA	NA	0%	1449										
1452	➔	Inspection	0 days	Wed 2/16/22	Wed 2/16/22	NA	NA	0%	1451										
1453	➔	3rd FI MEP F/S Rough Walls & Ceilings	8 days	Thu 2/17/22	Mon 2/28/22	NA	NA	0%	1451										
1454	➔	Inspect	0 days	Mon 2/28/22	Mon 2/28/22	NA	NA	0%	1453										
1455	➔	4th FI MEP F/S Rough Walls & Ceilings	8 days	Tue 3/1/22	Thu 3/10/22	NA	NA	0%	1453										
1456	➔	Inspection	0 days	Thu 3/10/22	Thu 3/10/22	NA	NA	0%	1455										
1457	➔	MEP F/S Rough Inspections	0 days	Thu 3/10/22	Thu 3/10/22	NA	NA	0%	1449,1451,1455										
1458	➔	Gypcrete-Lightweight	30 days	Fri 3/11/22	Thu 4/21/22	NA	NA	0%											

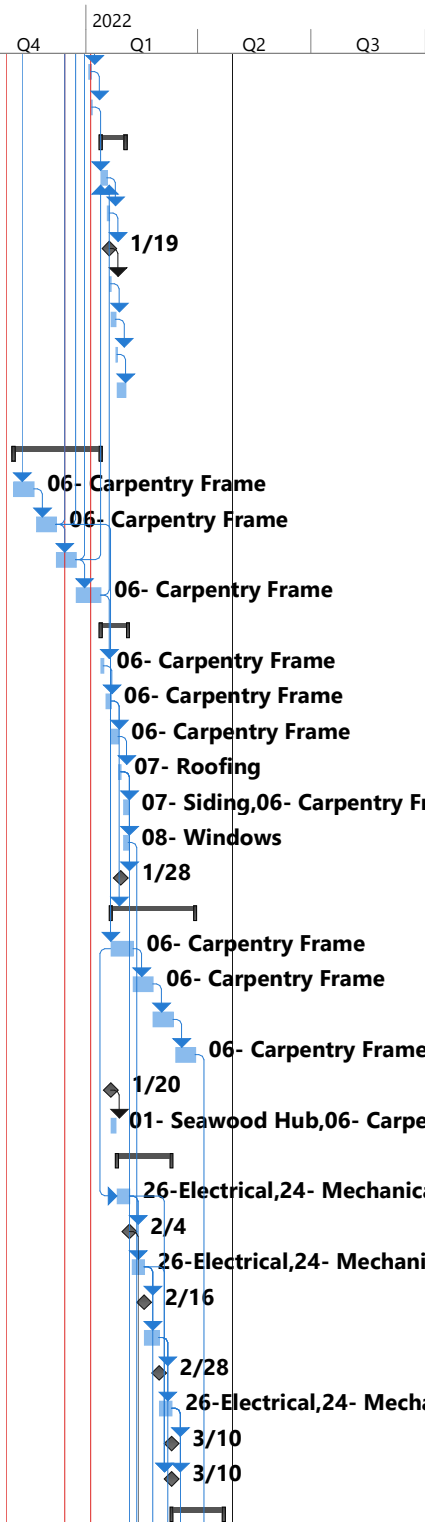

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Timeline											
										Q4	2021			2022							
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
1542	➔	Prime Paint - Interior	6 days	Wed 2/16/22	Wed 2/23/22	NA	NA	0%	1530SS+4 days												
1543	➔	Finish Paint	4 days	Mon 3/28/22	Thu 3/31/22	NA	NA	0%	1560												
1544	➔	2nd Floor	32 days	Mon 3/28/22	Tue 5/10/22	NA	NA	0%													
1545	➔	Prime Paint - Interior	6 days	Mon 3/28/22	Mon 4/4/22	NA	NA	0%	1533SS+4 days												
1546	➔	Finish Paint	4 days	Thu 5/5/22	Tue 5/10/22	NA	NA	0%	1562												
1547	➔	3rd Floor	28 days	Thu 4/7/22	Mon 5/16/22	NA	NA	0%													
1548	➔	Prime Paint - Interior	6 days	Thu 4/7/22	Thu 4/14/22	NA	NA	0%	1536SS+4 days												
1549	➔	Finish Paint	4 days	Wed 5/11/22	Mon 5/16/22	NA	NA	0%	1564												
1550	➔	4th Floor	26 days	Fri 4/15/22	Fri 5/20/22	NA	NA	0%													
1551	➔	Prime Paint - Interior	6 days	Fri 4/15/22	Fri 4/22/22	NA	NA	0%	1548												
1552	➔	Finish Paint	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%	1549												
1553	➔	Install Cabinets and Countertops	49 days	Thu 2/24/22	Tue 5/3/22	NA	NA	0%													
1554	➔	1st floor	12 days	Thu 2/24/22	Fri 3/11/22	NA	NA	0%	1542												
1555	➔	2nd Floor	12 days	Tue 4/5/22	Wed 4/20/22	NA	NA	0%	1545												
1556	➔	3rd Floor	12 days	Mon 4/11/22	Tue 4/26/22	NA	NA	0%	1548SS+2 days												
1557	➔	4th Floor	12 days	Mon 4/18/22	Tue 5/3/22	NA	NA	0%	1556SS+5 days												
1558	➔	Tile and Flooring	42 days	Mon 3/14/22	Tue 5/10/22	NA	NA	0%													
1559	➔	1st Floor	10 days	Mon 3/14/22	Fri 3/25/22	NA	NA	0%													
1560	➔	Install Bath and Floor Tile	10 days	Mon 3/14/22	Fri 3/25/22	NA	NA	0%	1554												
1561	➔	2nd Floor	10 days	Thu 4/21/22	Wed 5/4/22	NA	NA	0%													
1562	➔	Install Bath and Floor Tile	10 days	Thu 4/21/22	Wed 5/4/22	NA	NA	0%	1555												
1563	➔	3rd Floor	10 days	Wed 4/27/22	Tue 5/10/22	NA	NA	0%													
1564	➔	Install Bath and Floor Tile	10 days	Wed 4/27/22	Tue 5/10/22	NA	NA	0%	1556												
1565	➔	4th Floor	10 days	Wed 4/27/22	Tue 5/10/22	NA	NA	0%													
1566	➔	Install Bath and Floor Tile	10 days	Wed 4/27/22	Tue 5/10/22	NA	NA	0%	1556												
1567	➔	Door Hardware Install	40 days	Fri 4/1/22	Thu 5/26/22	NA	NA	0%													
1568	➔	1st Floor	4 days	Fri 4/1/22	Wed 4/6/22	NA	NA	0%													
1569	➔	Install Door Hardware	4 days	Fri 4/1/22	Wed 4/6/22	NA	NA	0%	1543												
1570	➔	2nd Floor	4 days	Wed 5/11/22	Mon 5/16/22	NA	NA	0%													
1571	➔	Install Door Hardware	4 days	Wed 5/11/22	Mon 5/16/22	NA	NA	0%	1546												
1572	➔	3rd Floor	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%													
1573	➔	Install Door Hardware	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%	1549												
1574	➔	4th Floor	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%													
1575	➔	Install Door Hardware	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%	1573												
1576	➔	MEP Trim	40 days	Fri 4/1/22	Thu 5/26/22	NA	NA	0%													
1577	➔	1st Floor	4 days	Fri 4/1/22	Wed 4/6/22	NA	NA	0%													
1578	➔	MEP Trim	4 days	Fri 4/1/22	Wed 4/6/22	NA	NA	0%	1543												
1579	➔	2nd Floor	4 days	Wed 5/11/22	Mon 5/16/22	NA	NA	0%													
1580	➔	MEP Trim	4 days	Wed 5/11/22	Mon 5/16/22	NA	NA	0%	1546												
1581	➔	3rd Floor	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%													
1582	➔	MEP Trim	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%	1549												
1583	➔	4th Floor	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%													

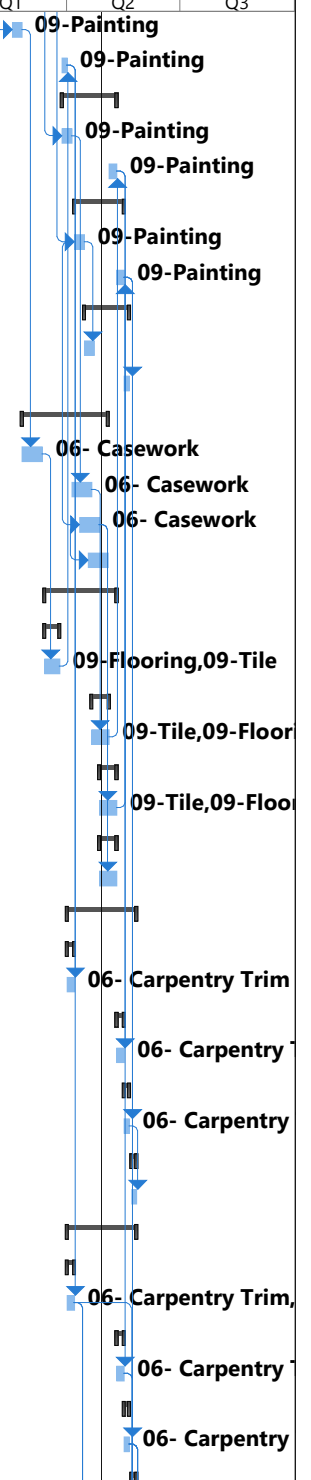

Project Update- 12-3-20
Project Start 1-4-21


Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3
1584	➔	MEP Trim	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%	1582								
1585	➔	MEPF Inspections	25 days	Mon 5/23/22	Fri 6/24/22	NA	NA	0%									
1586	➔	Final MEP Inspections	21 days	Mon 5/23/22	Mon 6/20/22	NA	NA	0%	1578,1582								
1587	➔	Equipment start up	4 days	Tue 6/21/22	Fri 6/24/22	NA	NA	0%	1586								
1588	➔	Install Flooring/Tile/LVT	40 days	Thu 4/7/22	Wed 6/1/22	NA	NA	0%									
1589	➔	1st Floor	4 days	Thu 4/7/22	Tue 4/12/22	NA	NA	0%									
1590	➔	Flooring	4 days	Thu 4/7/22	Tue 4/12/22	NA	NA	0%	1578								
1591	➔	2nd Floor	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%									
1592	➔	Flooring	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%	1580								
1593	➔	3rd Floor	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%									
1594	➔	Flooring	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%	1582								
1595	➔	4th Floor	4 days	Fri 5/27/22	Wed 6/1/22	NA	NA	0%									
1596	➔	Flooring	4 days	Fri 5/27/22	Wed 6/1/22	NA	NA	0%	1594								
1597	➔	Bath Accessories	40 days	Thu 4/7/22	Wed 6/1/22	NA	NA	0%									
1598	➔	1st Floor	4 days	Thu 4/7/22	Tue 4/12/22	NA	NA	0%									
1599	➔	Specialties-DIV 10	4 days	Thu 4/7/22	Tue 4/12/22	NA	NA	0%	1578								
1600	➔	2nd Floor	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%									
1601	➔	Specialties-DIV 10	4 days	Tue 5/17/22	Fri 5/20/22	NA	NA	0%	1580								
1602	➔	3rd Floor	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%									
1603	➔	Specialties-DIV 10	4 days	Mon 5/23/22	Thu 5/26/22	NA	NA	0%	1582								
1604	➔	4th Floor	4 days	Fri 5/27/22	Wed 6/1/22	NA	NA	0%									
1605	➔	Specialties-DIV 10	4 days	Fri 5/27/22	Wed 6/1/22	NA	NA	0%	1603								
1606	➔	Punch Walk Thru	5 days	Fri 5/27/22	Thu 6/2/22	NA	NA	0%									
1607	➔	Final Inspection-Building-Fire	3 days	Fri 5/27/22	Tue 5/31/22	NA	NA	0%	1603								
1608	➔	Owner/A-E	2 days	Wed 6/1/22	Thu 6/2/22	NA	NA	0%	1607								
1609	➔	Inspections	0 days	Fri 5/20/22	Fri 5/20/22	NA	NA	0%									
1610	➔	Final Inspections	0 days	Fri 5/20/22	Fri 5/20/22	NA	NA	0%	1601								
1611	➔	Punch Out and Clean	23 days	Fri 6/3/22	Tue 7/5/22	NA	NA	0%									
1612	➔	1st Floor	5 days	Fri 6/3/22	Thu 6/9/22	NA	NA	0%									
1613	➔	Punch and Clean	5 days	Fri 6/3/22	Thu 6/9/22	NA	NA	0%	1607,1608								
1614	➔	2nd Floor	5 days	Fri 6/10/22	Thu 6/16/22	NA	NA	0%									
1615	➔	Punch and Clean	5 days	Fri 6/10/22	Thu 6/16/22	NA	NA	0%	1613								
1616	➔	3rd Floor	5 days	Fri 6/17/22	Thu 6/23/22	NA	NA	0%									
1617	➔	Punch and Clean	5 days	Fri 6/17/22	Thu 6/23/22	NA	NA	0%	1615								
1618	➔	4th Floor	8 days	Fri 6/24/22	Tue 7/5/22	NA	NA	0%									
1619	➔	Punch and Clean	8 days	Fri 6/24/22	Tue 7/5/22	NA	NA	0%	1617								
1620	➔	Apartment Building One	193 days	Fri 10/29/21	Tue 7/26/22	NA	NA	0%									
1621	➔	Survey Pad	1 day	Fri 10/29/21	Fri 10/29/21	NA	NA	0%	659,661SS+45 day								
1622	➔	Concrete- SOG	20 days	Mon 11/1/21	Fri 11/26/21	NA	NA	0%									
1623	➔	Batter Boards	2 days	Mon 11/1/21	Tue 11/2/21	NA	NA	0%	1621								
1624	➔	Form SOG	5 days	Wed 11/3/21	Tue 11/9/21	NA	NA	0%	1623								
1625	➔	Final Grade +/- .10	1 day	Wed 11/10/21	Wed 11/10/21	NA	NA	0%	1624								

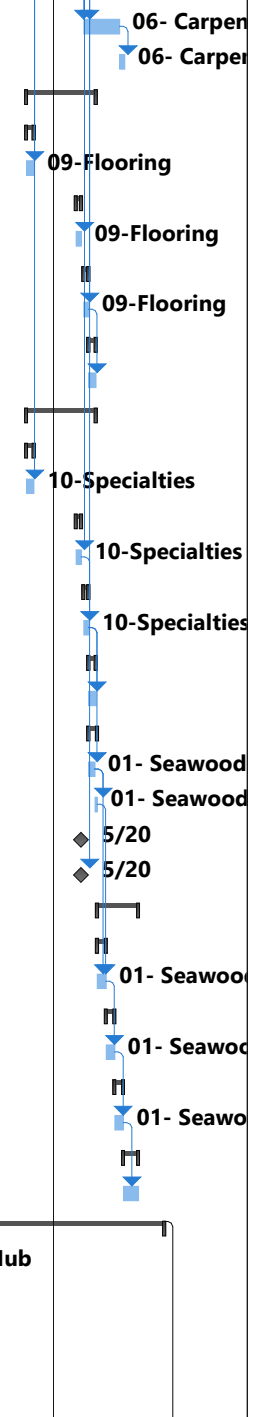

Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Timeline													
										Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3						
1626	➔	MEP Underground Rough	5 days	Thu 11/11/21	Wed 11/17/21	NA	NA	0%	1625														
1627	➔	Inspection mep Undgrd	0 days	Wed 11/17/21	Wed 11/17/21	NA	NA	0%	1626														
1628	➔	Treat, Reinforce, Inspect, and Pour SOG	5 days	Thu 11/18/21	Wed 11/24/21	NA	NA	0%	1627														
1629	➔	Curing Compound/Cut Slab	1 day	Thu 11/25/21	Thu 11/25/21	NA	NA	0%	1628														
1630	➔	Strip and Clean	1 day	Fri 11/26/21	Fri 11/26/21	NA	NA	0%	1629														
1631	➔	Elevator Pit	12 days	Mon 11/1/21	Tue 11/16/21	NA	NA	0%															
1632	➔	Excavate	1 day	Mon 11/1/21	Mon 11/1/21	NA	NA	0%	1621														
1633	➔	Set Sump Roughin	1 day	Tue 11/2/21	Tue 11/2/21	NA	NA	0%	1632														
1634	➔	Set Bar- Inspect- Cast Slab	2 days	Wed 11/3/21	Thu 11/4/21	NA	NA	0%	1633														
1635	➔	Set Form Walls	2 days	Fri 11/5/21	Mon 11/8/21	NA	NA	0%	1634														
1636	➔	Roughin E&P Walls	1 day	Tue 11/9/21	Tue 11/9/21	NA	NA	0%	1635														
1637	➔	Set Bar- Inspect-Pour	3 days	Wed 11/10/21	Fri 11/12/21	NA	NA	0%	1636														
1638	➔	Strip-Backfill-	2 days	Mon 11/15/21	Tue 11/16/21	NA	NA	0%	1637														
1639	➔	CMU Elevator Shaft	72 days	Mon 11/15/21	Tue 2/22/22	NA	NA	0%															
1640	➔	1st Floor	9 days	Mon 11/15/21	Thu 11/25/21	NA	NA	0%															
1641	➔	CMU through Bond Beam	3 days	Mon 11/15/21	Wed 11/17/21	NA	NA	0%	1637														
1642	➔	Bar and Inspect Pads	2 days	Thu 11/18/21	Fri 11/19/21	NA	NA	0%	1641														
1643	➔	Inspect	0 days	Fri 11/19/21	Fri 11/19/21	NA	NA	0%	1642														
1644	➔	Cast-Grout Mix 300psi	1 day	Mon 11/22/21	Mon 11/22/21	NA	NA	0%	1643														
1645	➔	Bond Beam Set-Bar-Inspect	2 days	Tue 11/23/21	Wed 11/24/21	NA	NA	0%	1644														
1646	➔	Cast Bond Beam	1 day	Thu 11/25/21	Thu 11/25/21	NA	NA	0%	1645														
1647	➔	2nd Floor	9 days	Wed 12/29/21	Mon 1/10/22	NA	NA	0%															
1648	➔	CMU through Bond Beam	3 days	Wed 12/29/21	Fri 12/31/21	NA	NA	0%	1646,1671														
1649	➔	Bar and Inspect Pads	2 days	Mon 1/3/22	Tue 1/4/22	NA	NA	0%	1648														
1650	➔	Inspect	0 days	Tue 1/4/22	Tue 1/4/22	NA	NA	0%	1649														
1651	➔	Cast-Grout Mix 300psi	1 day	Wed 1/5/22	Wed 1/5/22	NA	NA	0%	1650														
1652	➔	Bond Beam Set-Bar-Inspect	2 days	Thu 1/6/22	Fri 1/7/22	NA	NA	0%	1651														
1653	➔	Cast Bond Beam	1 day	Mon 1/10/22	Mon 1/10/22	NA	NA	0%	1652														
1654	➔	3rd Floor	9 days	Fri 1/14/22	Wed 1/26/22	NA	NA	0%															
1655	➔	CMU through Bond Beam	3 days	Fri 1/14/22	Tue 1/18/22	NA	NA	0%	1653,1671,1672														
1656	➔	Bar and Inspect Pads	2 days	Wed 1/19/22	Thu 1/20/22	NA	NA	0%	1655														
1657	➔	Inspect	0 days	Thu 1/20/22	Thu 1/20/22	NA	NA	0%	1656														
1658	➔	Cast-Grout Mix 300psi	1 day	Fri 1/21/22	Fri 1/21/22	NA	NA	0%	1657														
1659	➔	Bond Beam Set-Bar-Inspect	2 days	Mon 1/24/22	Tue 1/25/22	NA	NA	0%	1658														
1660	➔	Cast Bond Beam	1 day	Wed 1/26/22	Wed 1/26/22	NA	NA	0%	1659														
1661	➔	4th Floor-Thru Rooftop	14 days	Thu 2/3/22	Tue 2/22/22	NA	NA	0%															
1662	➔	CMU through Bond Beam	3 days	Thu 2/3/22	Mon 2/7/22	NA	NA	0%	1660,1672,1673														
1663	➔	Bar and Inspect Pads	2 days	Tue 2/8/22	Wed 2/9/22	NA	NA	0%	1662														
1664	➔	Inspect	0 days	Wed 2/9/22	Wed 2/9/22	NA	NA	0%	1663														
1665	➔	Cast-Grout Mix 300psi	1 day	Thu 2/10/22	Thu 2/10/22	NA	NA	0%	1664														
1666	➔	Bond Beam Set-Bar-Inspect	2 days	Fri 2/11/22	Mon 2/14/22	NA	NA	0%	1665														
1667	➔	Cast Bond Beam	1 day	Tue 2/15/22	Tue 2/15/22	NA	NA	0%	1666														

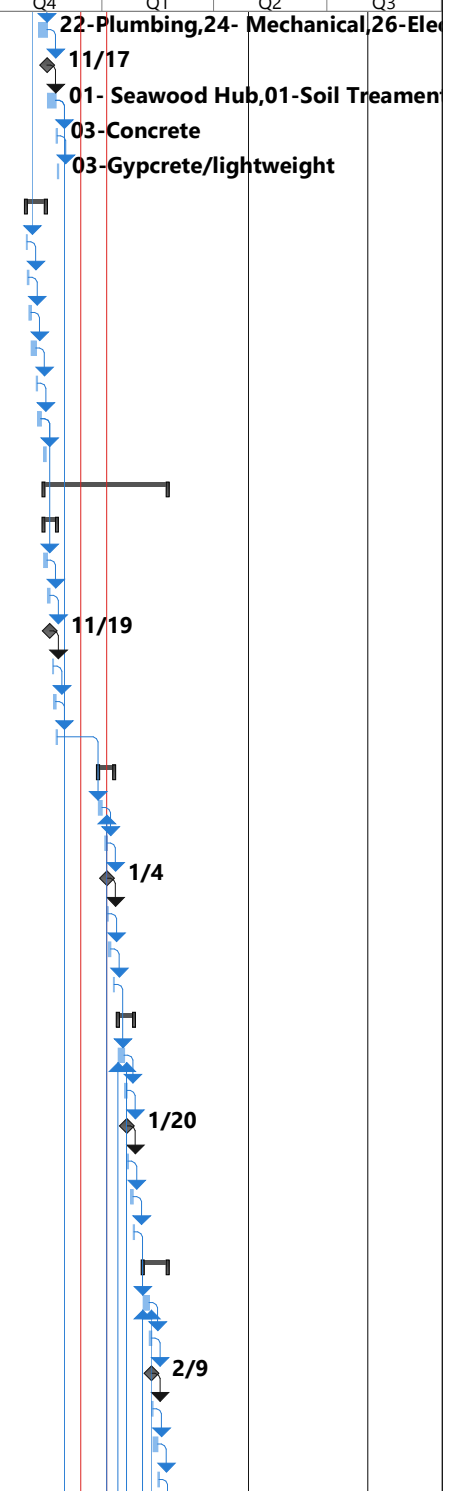

Project Update- 12-3-20
Project Start 1-4-21


Task	Inactive Task	Manual Summary Rollup	External Milestone	Critical
Split	Inactive Milestone	Manual Summary	Deadline	Critical Split
Milestone	Inactive Summary	Start-only	Path Driving Predecessor Milestone Task	Progress
Summary	Manual Task	Finish-only	Path Driving Predecessor Summary Task	Manual Progress
Project Summary	Duration-only	External Tasks	Path Driving Predecessor Normal Task	

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3
1668	➔	Form Roof-Bar-Inspect-Cast- Reg. Mix 3000PSI	5 days	Wed 2/16/22	Tue 2/22/22	NA	NA	0%	1667								
1669	➔	Exterior Frame	50 days	Thu 11/25/21	Wed 2/2/22	NA	NA	0%									
1670	➔	1st Floor- Joist	12 days	Thu 11/25/21	Fri 12/10/21	NA	NA	0%	1628								
1671	➔	2nd Floor to Joist	12 days	Mon 12/13/21	Tue 12/28/21	NA	NA	0%	1670								
1672	➔	3rd floor to Joist	12 days	Wed 12/29/21	Thu 1/13/22	NA	NA	0%	1671								
1673	➔	4th floor to Joist	14 days	Fri 1/14/22	Wed 2/2/22	NA	NA	0%	1672								
1674	➔	Roof Frame-Ext Dry-in	16 days	Thu 2/3/22	Thu 2/24/22	NA	NA	0%									
1675	➔	Set Truss Package	2 days	Thu 2/3/22	Fri 2/4/22	NA	NA	0%	1673								
1676	➔	Frame Roof	4 days	Mon 2/7/22	Thu 2/10/22	NA	NA	0%	1675								
1677	➔	Sheath Roof	4 days	Fri 2/11/22	Wed 2/16/22	NA	NA	0%	1676								
1678	➔	Dry-In Roof	2 days	Thu 2/17/22	Fri 2/18/22	NA	NA	0%	1677								
1679	➔	Tape and Seal Zip	4 days	Mon 2/21/22	Thu 2/24/22	NA	NA	0%	1678								
1680	➔	Install Windows	4 days	Mon 2/21/22	Thu 2/24/22	NA	NA	0%	1678								
1681	➔	Inspect Engineering with Tie-down and Sheathing	0 days	Fri 2/18/22	Fri 2/18/22	NA	NA	0%	1678								
1682	➔	Interior Framing - Walls & Ceilings	48 days	Thu 2/10/22	Tue 4/19/22	NA	NA	0%	1676								
1683	➔	1st Floor	12 days	Fri 2/11/22	Mon 2/28/22	NA	NA	0%	1671								
1684	➔	2nd Floor	12 days	Tue 3/1/22	Wed 3/16/22	NA	NA	0%	1683								
1685	➔	3rd Floor	12 days	Thu 3/17/22	Fri 4/1/22	NA	NA	0%	1684								
1686	➔	4th Floor	12 days	Mon 4/4/22	Tue 4/19/22	NA	NA	0%	1685								
1687	➔	Framing Inspection	0 days	Thu 2/10/22	Thu 2/10/22	NA	NA	0%									
1688	➔	Framing Punch Out	2 days	Fri 2/11/22	Mon 2/14/22	NA	NA	0%	1687								
1689	➔	MEP Rough in	32 days	Wed 2/16/22	Thu 3/31/22	NA	NA	0%									
1690	➔	1st FI MEP F/S Rough Walls & Ceilings	8 days	Wed 2/16/22	Fri 2/25/22	NA	NA	0%	1683SS+3 days								
1691	➔	Inspection	0 days	Fri 2/25/22	Fri 2/25/22	NA	NA	0%	1690								
1692	➔	2nd FI MEP F/S Rough Walls & Ceilings	8 days	Mon 2/28/22	Wed 3/9/22	NA	NA	0%	1690								
1693	➔	Inspection	0 days	Wed 3/9/22	Wed 3/9/22	NA	NA	0%	1692								
1694	➔	3rd FI MEP F/S Rough Walls & Ceilings	8 days	Thu 3/10/22	Mon 3/21/22	NA	NA	0%	1692								
1695	➔	Inspect	0 days	Mon 3/21/22	Mon 3/21/22	NA	NA	0%	1694								
1696	➔	4th FI MEP F/S Rough Walls & Ceilings	8 days	Tue 3/22/22	Thu 3/31/22	NA	NA	0%	1694								
1697	➔	Inspection	0 days	Thu 3/31/22	Thu 3/31/22	NA	NA	0%	1696								
1698	➔	MEP F/S Rough Inspections	0 days	Thu 3/31/22	Thu 3/31/22	NA	NA	0%	1690,1692,1696								
1699	➔	Gypcrete-Lightweight	30 days	Fri 4/1/22	Thu 5/12/22	NA	NA	0%									
1700	➔	2nd floor prep	5 days	Fri 4/1/22	Thu 4/7/22	NA	NA	0%	1696								
1701	➔	2nd floor place GYP-crete	5 days	Fri 4/8/22	Thu 4/14/22	NA	NA	0%	1700								
1702	➔	3rd Floor Prep	5 days	Fri 4/15/22	Thu 4/21/22	NA	NA	0%	1701								
1703	➔	3rd Place Gypcrete	5 days	Fri 4/22/22	Thu 4/28/22	NA	NA	0%	1702								
1704	➔	4th Floor Prep	5 days	Fri 4/29/22	Thu 5/5/22	NA	NA	0%	1703								
1705	➔	4th Floor Gypcrete	5 days	Fri 5/6/22	Thu 5/12/22	NA	NA	0%	1704								
1706	➔	Lightweight Hallways 2nd & 3rd	9 days	Fri 4/29/22	Wed 5/11/22	NA	NA	0%									
1707	➔	Prep 2nd Floor Hallway	2 days	Fri 4/29/22	Mon 5/2/22	NA	NA	0%	1703								
1708	➔	Cast 2nd Floor Hallway	1 day	Tue 5/3/22	Tue 5/3/22	NA	NA	0%	1707								

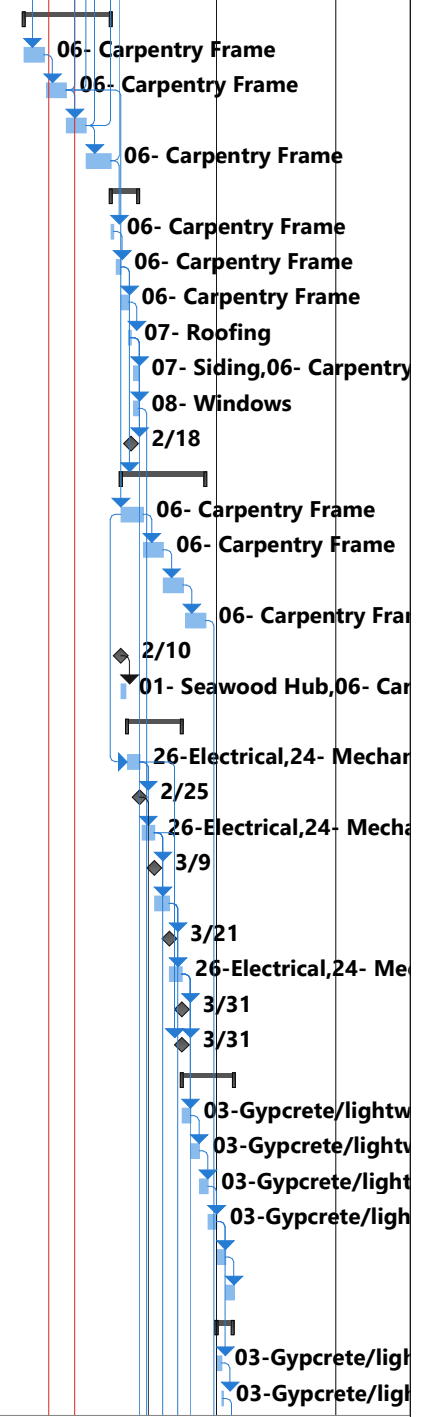


Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	2021				2022				
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
1751		Interior Finishes	100 days	Mon 2/28/22	Fri 7/15/22	NA	NA	0%										
1752		Insulation and Inspection	27 days	Mon 2/28/22	Tue 4/5/22	NA	NA	0%										
1753		1st Floor Insulation-Inspection	3 days	Mon 2/28/22	Wed 3/2/22	NA	NA	0%	1691,1739SS-5 da									
1754		2nd floor Insulation/ Inspection	3 days	Thu 3/10/22	Mon 3/14/22	NA	NA	0%	1692,1753									
1755		3rd Floor Insulation/ Inspection	3 days	Tue 3/22/22	Thu 3/24/22	NA	NA	0%	1694,1754									
1756		4th Floor Insulation/ Inspection	3 days	Fri 4/1/22	Tue 4/5/22	NA	NA	0%	1696,1755									
1757		Interior Zip-Hallway 1st thru 3rd	3 days	Wed 4/6/22	Fri 4/8/22	NA	NA	0%	1752									
1758		Interior Stucco/Plaster over lathe- Hallway 1st Thru 3rd	5 days	Mon 4/11/22	Fri 4/15/22	NA	NA	0%	1757									
1759		Drywall-GYP	46 days	Tue 3/1/22	Tue 5/3/22	NA	NA	0%										
1760		1st Floor Hang- Finish Drywall	20 days	Tue 3/1/22	Mon 3/28/22	NA	NA	0%	1753SS+1 day									
1761		Drywall Screw Inspection	0 days	Mon 3/28/22	Mon 3/28/22	NA	NA	0%	1760									
1762		2nd Floor Hang- Finish Drywall	20 days	Fri 3/11/22	Thu 4/7/22	NA	NA	0%	1760SS+8 days									
1763		Drywall Screw Inspection	0 days	Thu 4/7/22	Thu 4/7/22	NA	NA	0%	1762									
1764		3rd Floor Hang- Finish Drywall	20 days	Wed 3/23/22	Tue 4/19/22	NA	NA	0%	1762SS+8 days									
1765		Drywall Screw Inspection	0 days	Tue 4/19/22	Tue 4/19/22	NA	NA	0%	1764									
1766		4th Floor Hang- Finish Drywall	20 days	Wed 4/6/22	Tue 5/3/22	NA	NA	0%	1756									
1767		Drywall Screw Inspection	0 days	Tue 5/3/22	Tue 5/3/22	NA	NA	0%	1766									
1768		Doors and Trim	97 days	Thu 3/3/22	Fri 7/15/22	NA	NA	0%										
1769		1st Floor	23 days	Thu 3/3/22	Mon 4/4/22	NA	NA	0%										
1770		1st floor Install Doors	5 days	Tue 3/29/22	Mon 4/4/22	NA	NA	0%	1760									
1771		1st Running Trim	4 days	Thu 3/3/22	Tue 3/8/22	NA	NA	0%	1760SS+2 days									
1772		2nd Floor	6 days	Fri 4/8/22	Fri 4/15/22	NA	NA	0%										
1773		2nd floor Install Doors	5 days	Fri 4/8/22	Thu 4/14/22	NA	NA	0%	1762									
1774		2nd Running Trim	4 days	Tue 4/12/22	Fri 4/15/22	NA	NA	0%	1773SS+2 days									
1775		3rd Floor	6 days	Wed 4/20/22	Wed 4/27/22	NA	NA	0%										
1776		3rd floor Install Doors	5 days	Wed 4/20/22	Tue 4/26/22	NA	NA	0%	1764									
1777		3rd Floor Running Trim	4 days	Fri 4/22/22	Wed 4/27/22	NA	NA	0%	1776SS+2 days									
1778		4th Floor	5 days	Wed 4/27/22	Tue 5/3/22	NA	NA	0%										
1779		4th floor Install Doors	5 days	Wed 4/27/22	Tue 5/3/22	NA	NA	0%	1776									
1780		4th Floor Running Trim	4 days	Thu 4/28/22	Tue 5/3/22	NA	NA	0%	1777									
1781		Paint	68 days	Wed 3/9/22	Fri 6/10/22	NA	NA	0%										
1782		1st Floor	32 days	Wed 3/9/22	Thu 4/21/22	NA	NA	0%										
1783		Prime Paint - Interior	6 days	Wed 3/9/22	Wed 3/16/22	NA	NA	0%	1771SS+4 days									
1784		Finish Paint	4 days	Mon 4/18/22	Thu 4/21/22	NA	NA	0%	1801									
1785		2nd Floor	32 days	Mon 4/18/22	Tue 5/31/22	NA	NA	0%										
1786		Prime Paint - Interior	6 days	Mon 4/18/22	Mon 4/25/22	NA	NA	0%	1774SS+4 days									
1787		Finish Paint	4 days	Thu 5/26/22	Tue 5/31/22	NA	NA	0%	1803									
1788		3rd Floor	28 days	Thu 4/28/22	Mon 6/6/22	NA	NA	0%										
1789		Prime Paint - Interior	6 days	Thu 4/28/22	Thu 5/5/22	NA	NA	0%	1777SS+4 days									
1790		Finish Paint	4 days	Wed 6/1/22	Mon 6/6/22	NA	NA	0%	1805									
1791		4th Floor	26 days	Fri 5/6/22	Fri 6/10/22	NA	NA	0%										

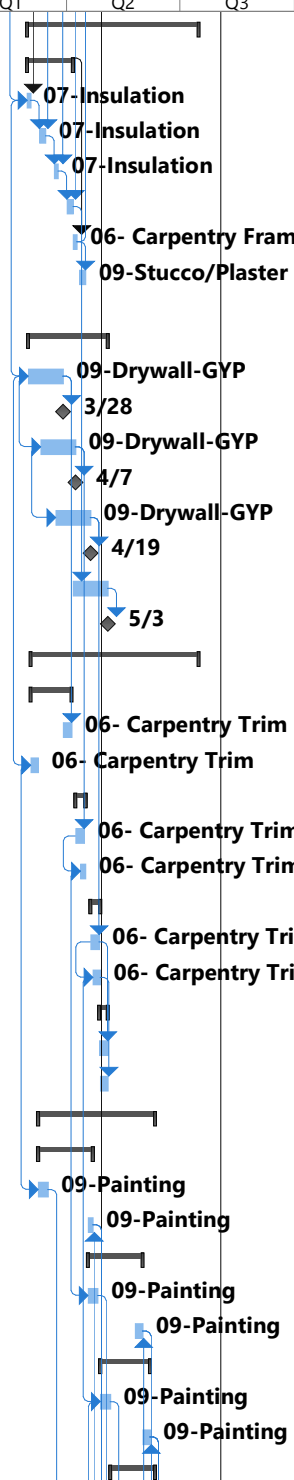

Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	2021			2022				
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
1792	➔	Prime Paint - Interior	6 days	Fri 5/6/22	Fri 5/13/22	NA	NA	0%	1789								
1793	➔	Finish Paint	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%	1790								
1794	➔	Install Cabinets and Countertops	49 days	Thu 3/17/22	Tue 5/24/22	NA	NA	0%									
1795	➔	1st floor	12 days	Thu 3/17/22	Fri 4/1/22	NA	NA	0%	1783								
1796	➔	2nd Floor	12 days	Tue 4/26/22	Wed 5/11/22	NA	NA	0%	1786								
1797	➔	3rd Floor	12 days	Mon 5/2/22	Tue 5/17/22	NA	NA	0%	1789SS+2 days								
1798	➔	4th Floor	12 days	Mon 5/9/22	Tue 5/24/22	NA	NA	0%	1797SS+5 days								
1799	➔	Tile and Flooring	42 days	Mon 4/4/22	Tue 5/31/22	NA	NA	0%									
1800	➔	1st Floor	10 days	Mon 4/4/22	Fri 4/15/22	NA	NA	0%									
1801	➔	Install Bath and Floor Tile	10 days	Mon 4/4/22	Fri 4/15/22	NA	NA	0%	1795								
1802	➔	2nd Floor	10 days	Thu 5/12/22	Wed 5/25/22	NA	NA	0%									
1803	➔	Install Bath and Floor Tile	10 days	Thu 5/12/22	Wed 5/25/22	NA	NA	0%	1796								
1804	➔	3rd Floor	10 days	Wed 5/18/22	Tue 5/31/22	NA	NA	0%									
1805	➔	Install Bath and Floor Tile	10 days	Wed 5/18/22	Tue 5/31/22	NA	NA	0%	1797								
1806	➔	4th Floor	10 days	Wed 5/18/22	Tue 5/31/22	NA	NA	0%									
1807	➔	Install Bath and Floor Tile	10 days	Wed 5/18/22	Tue 5/31/22	NA	NA	0%	1797								
1808	➔	Door Hardware Install	40 days	Fri 4/22/22	Thu 6/16/22	NA	NA	0%									
1809	➔	1st Floor	4 days	Fri 4/22/22	Wed 4/27/22	NA	NA	0%									
1810	➔	Install Door Hardware	4 days	Fri 4/22/22	Wed 4/27/22	NA	NA	0%	1784								
1811	➔	2nd Floor	4 days	Wed 6/1/22	Mon 6/6/22	NA	NA	0%									
1812	➔	Install Door Hardware	4 days	Wed 6/1/22	Mon 6/6/22	NA	NA	0%	1787								
1813	➔	3rd Floor	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%									
1814	➔	Install Door Hardware	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%	1790								
1815	➔	4th Floor	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%									
1816	➔	Install Door Hardware	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%	1814								
1817	➔	MEP Trim	40 days	Fri 4/22/22	Thu 6/16/22	NA	NA	0%									
1818	➔	1st Floor	4 days	Fri 4/22/22	Wed 4/27/22	NA	NA	0%									
1819	➔	MEP Trim	4 days	Fri 4/22/22	Wed 4/27/22	NA	NA	0%	1784								
1820	➔	2nd Floor	4 days	Wed 6/1/22	Mon 6/6/22	NA	NA	0%									
1821	➔	MEP Trim	4 days	Wed 6/1/22	Mon 6/6/22	NA	NA	0%	1787								
1822	➔	3rd Floor	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%									
1823	➔	MEP Trim	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%	1790								
1824	➔	4th Floor	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%									
1825	➔	MEP Trim	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%	1823								
1826	➔	MEPF Inspections	25 days	Mon 6/13/22	Fri 7/15/22	NA	NA	0%									
1827	➔	Final MEP Inspections	21 days	Mon 6/13/22	Mon 7/11/22	NA	NA	0%	1819,1823								
1828	➔	Equipment start up	4 days	Tue 7/12/22	Fri 7/15/22	NA	NA	0%	1827								
1829	➔	Install Flooring/Tile/LVT	40 days	Thu 4/28/22	Wed 6/22/22	NA	NA	0%									
1830	➔	1st Floor	4 days	Thu 4/28/22	Tue 5/3/22	NA	NA	0%									
1831	➔	Flooring	4 days	Thu 4/28/22	Tue 5/3/22	NA	NA	0%	1819								
1832	➔	2nd Floor	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%									
1833	➔	Flooring	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%	1821								

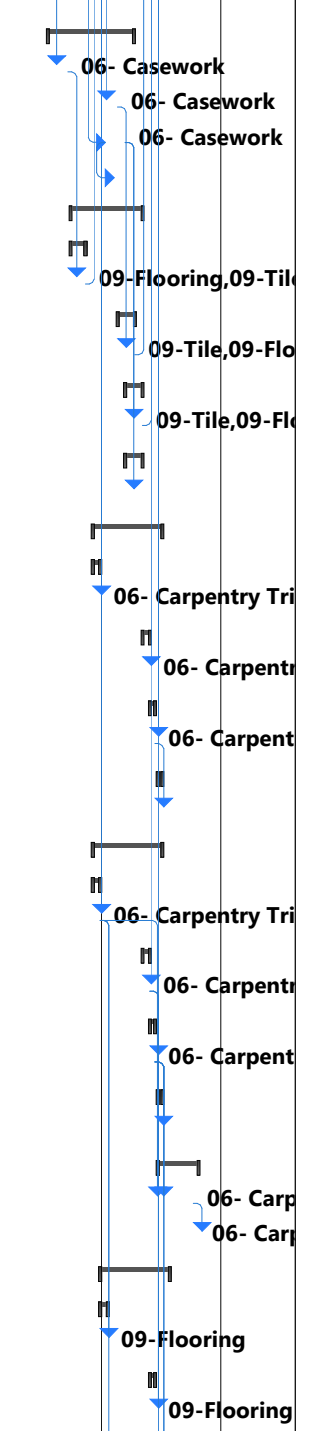

Project Update- 12-3-20
Project Start 1-4-21


Task	Inactive Task	Manual Summary Rollup	External Milestone	Critical
Split	Inactive Milestone	Manual Summary	Deadline	Critical Split
Milestone	Inactive Summary	Start-only	Path Driving Predecessor Milestone Task	Progress
Summary	Manual Task	Finish-only	Path Driving Predecessor Summary Task	Manual Progress
Project Summary	Duration-only	External Tasks	Path Driving Predecessor Normal Task	

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	2021				2022			
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
1834	➔	3rd Floor	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%									
1835	➔	Flooring	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%	1823								
1836	➔	4th Floor	4 days	Fri 6/17/22	Wed 6/22/22	NA	NA	0%									
1837	➔	Flooring	4 days	Fri 6/17/22	Wed 6/22/22	NA	NA	0%	1835								
1838	➔	Bath Accessories	40 days	Thu 4/28/22	Wed 6/22/22	NA	NA	0%									
1839	➔	1st Floor	4 days	Thu 4/28/22	Tue 5/3/22	NA	NA	0%									
1840	➔	Specialties-DIV 10	4 days	Thu 4/28/22	Tue 5/3/22	NA	NA	0%	1819								
1841	➔	2nd Floor	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%									
1842	➔	Specialties-DIV 10	4 days	Tue 6/7/22	Fri 6/10/22	NA	NA	0%	1821								
1843	➔	3rd Floor	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%									
1844	➔	Specialties-DIV 10	4 days	Mon 6/13/22	Thu 6/16/22	NA	NA	0%	1823								
1845	➔	4th Floor	4 days	Fri 6/17/22	Wed 6/22/22	NA	NA	0%									
1846	➔	Specialties-DIV 10	4 days	Fri 6/17/22	Wed 6/22/22	NA	NA	0%	1844								
1847	➔	Punch Walk Thru	5 days	Fri 6/17/22	Thu 6/23/22	NA	NA	0%									
1848	➔	Final Inspection-Building-Fire	3 days	Fri 6/17/22	Tue 6/21/22	NA	NA	0%	1844								
1849	➔	Owner/A-E	2 days	Wed 6/22/22	Thu 6/23/22	NA	NA	0%	1848								
1850	➔	Inspections	0 days	Fri 6/10/22	Fri 6/10/22	NA	NA	0%									
1851	➔	Final Inspections	0 days	Fri 6/10/22	Fri 6/10/22	NA	NA	0%	1842								
1852	➔	Punch Out and Clean	23 days	Fri 6/24/22	Tue 7/26/22	NA	NA	0%									
1853	➔	1st Floor	5 days	Fri 6/24/22	Thu 6/30/22	NA	NA	0%									
1854	➔	Punch and Clean	5 days	Fri 6/24/22	Thu 6/30/22	NA	NA	0%	1848,1849								
1855	➔	2nd Floor	5 days	Fri 7/1/22	Thu 7/7/22	NA	NA	0%									
1856	➔	Punch and Clean	5 days	Fri 7/1/22	Thu 7/7/22	NA	NA	0%	1854								
1857	➔	3rd Floor	5 days	Fri 7/8/22	Thu 7/14/22	NA	NA	0%									
1858	➔	Punch and Clean	5 days	Fri 7/8/22	Thu 7/14/22	NA	NA	0%	1856								
1859	➔	4th Floor	8 days	Fri 7/15/22	Tue 7/26/22	NA	NA	0%									
1860	➔	Punch and Clean	8 days	Fri 7/15/22	Tue 7/26/22	NA	NA	0%	1858								
1861	➔	Apartment Building Five	193 days	Wed 12/15/21	Fri 9/9/22	NA	NA	0%									
1862	➔	Survey Pad	1 day	Wed 12/15/21	Wed 12/15/21	NA	NA	0%	659,662SS+60 day								
1863	➔	Concrete- SOG	20 days	Thu 12/16/21	Wed 1/12/22	NA	NA	0%									
1864	➔	Batter Boards	2 days	Thu 12/16/21	Fri 12/17/21	NA	NA	0%	1862								
1865	➔	Form SOG	5 days	Mon 12/20/21	Fri 12/24/21	NA	NA	0%	1864								
1866	➔	Final Grade +/- .10	1 day	Mon 12/27/21	Mon 12/27/21	NA	NA	0%	1865								
1867	➔	MEP Underground Rough	5 days	Tue 12/28/21	Mon 1/3/22	NA	NA	0%	1866								
1868	➔	Inspection mep Undgrd	0 days	Mon 1/3/22	Mon 1/3/22	NA	NA	0%	1867								
1869	➔	Treat, Reinforce, Inspect, and Pour SOG	5 days	Tue 1/4/22	Mon 1/10/22	NA	NA	0%	1868								
1870	➔	Curing Compound/Cut Slab	1 day	Tue 1/11/22	Tue 1/11/22	NA	NA	0%	1869								
1871	➔	Strip and Clean	1 day	Wed 1/12/22	Wed 1/12/22	NA	NA	0%	1870								
1872	➔	Elevator Pit	12 days	Thu 12/16/21	Fri 12/31/21	NA	NA	0%									
1873	➔	Excavate	1 day	Thu 12/16/21	Thu 12/16/21	NA	NA	0%	1862								
1874	➔	Set Sump Roughin	1 day	Fri 12/17/21	Fri 12/17/21	NA	NA	0%	1873								
1875	➔	Set Bar- Inspect- Cast Slab	2 days	Mon 12/20/21	Tue 12/21/21	NA	NA	0%	1874								

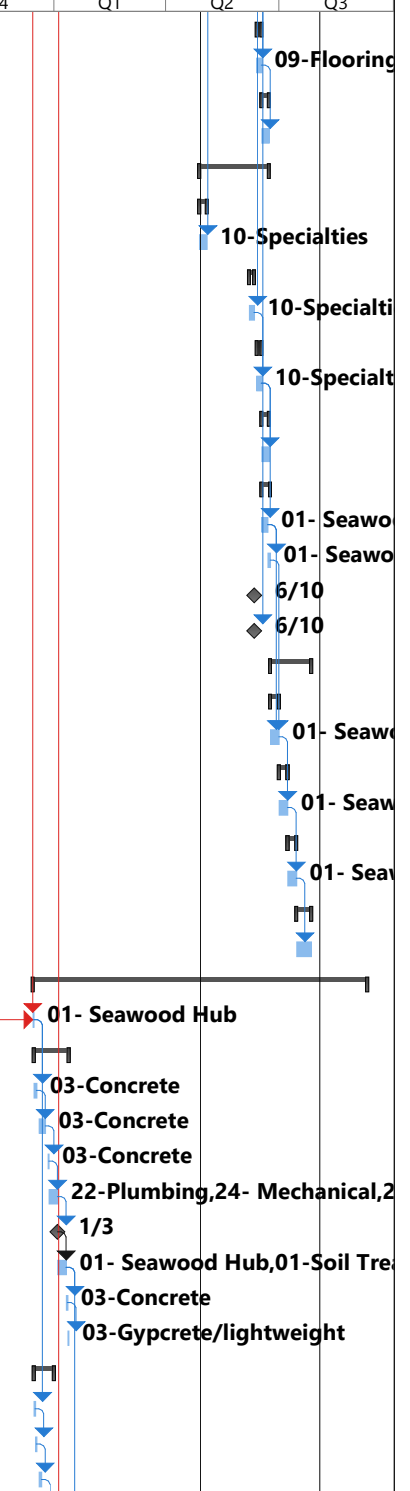

Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Gantt Chart												
										Q4	2021			2022			Q3					
1876	➔	Set Form Walls	2 days	Wed 12/22/21	Thu 12/23/21	NA	NA	0%	1875													
1877	➔	Roughin E&P Walls	1 day	Fri 12/24/21	Fri 12/24/21	NA	NA	0%	1876													
1878	➔	Set Bar- Inspect-Pour	3 days	Mon 12/27/21	Wed 12/29/21	NA	NA	0%	1877													
1879	➔	Strip-Backfill-	2 days	Thu 12/30/21	Fri 12/31/21	NA	NA	0%	1878													
1880	➔	CMU Elevator Shaft	72 days	Thu 12/30/21	Fri 4/8/22	NA	NA	0%														
1881	➔	1st Floor	9 days	Thu 12/30/21	Tue 1/11/22	NA	NA	0%														
1882	➔	CMU through Bond Beam	3 days	Thu 12/30/21	Mon 1/3/22	NA	NA	0%	1878													
1883	➔	Bar and Inspect Pads	2 days	Tue 1/4/22	Wed 1/5/22	NA	NA	0%	1882													
1884	➔	Inspect	0 days	Wed 1/5/22	Wed 1/5/22	NA	NA	0%	1883													
1885	➔	Cast-Grout Mix 300psi	1 day	Thu 1/6/22	Thu 1/6/22	NA	NA	0%	1884													
1886	➔	Bond Beam Set-Bar-Inspect	2 days	Fri 1/7/22	Mon 1/10/22	NA	NA	0%	1885													
1887	➔	Cast Bond Beam	1 day	Tue 1/11/22	Tue 1/11/22	NA	NA	0%	1886													
1888	➔	2nd Floor	9 days	Mon 2/14/22	Thu 2/24/22	NA	NA	0%														
1889	➔	CMU through Bond Beam	3 days	Mon 2/14/22	Wed 2/16/22	NA	NA	0%	1887,1912													
1890	➔	Bar and Inspect Pads	2 days	Thu 2/17/22	Fri 2/18/22	NA	NA	0%	1889													
1891	➔	Inspect	0 days	Fri 2/18/22	Fri 2/18/22	NA	NA	0%	1890													
1892	➔	Cast-Grout Mix 300psi	1 day	Mon 2/21/22	Mon 2/21/22	NA	NA	0%	1891													
1893	➔	Bond Beam Set-Bar-Inspect	2 days	Tue 2/22/22	Wed 2/23/22	NA	NA	0%	1892													
1894	➔	Cast Bond Beam	1 day	Thu 2/24/22	Thu 2/24/22	NA	NA	0%	1893													
1895	➔	3rd Floor	9 days	Wed 3/2/22	Mon 3/14/22	NA	NA	0%														
1896	➔	CMU through Bond Beam	3 days	Wed 3/2/22	Fri 3/4/22	NA	NA	0%	1894,1912,1913													
1897	➔	Bar and Inspect Pads	2 days	Mon 3/7/22	Tue 3/8/22	NA	NA	0%	1896													
1898	➔	Inspect	0 days	Tue 3/8/22	Tue 3/8/22	NA	NA	0%	1897													
1899	➔	Cast-Grout Mix 300psi	1 day	Wed 3/9/22	Wed 3/9/22	NA	NA	0%	1898													
1900	➔	Bond Beam Set-Bar-Inspect	2 days	Thu 3/10/22	Fri 3/11/22	NA	NA	0%	1899													
1901	➔	Cast Bond Beam	1 day	Mon 3/14/22	Mon 3/14/22	NA	NA	0%	1900													
1902	➔	4th Floor-Thru Rooftop	14 days	Tue 3/22/22	Fri 4/8/22	NA	NA	0%														
1903	➔	CMU through Bond Beam	3 days	Tue 3/22/22	Thu 3/24/22	NA	NA	0%	1901,1913,1914													
1904	➔	Bar and Inspect Pads	2 days	Fri 3/25/22	Mon 3/28/22	NA	NA	0%	1903													
1905	➔	Inspect	0 days	Mon 3/28/22	Mon 3/28/22	NA	NA	0%	1904													
1906	➔	Cast-Grout Mix 300psi	1 day	Tue 3/29/22	Tue 3/29/22	NA	NA	0%	1905													
1907	➔	Bond Beam Set-Bar-Inspect	2 days	Wed 3/30/22	Thu 3/31/22	NA	NA	0%	1906													
1908	➔	Cast Bond Beam	1 day	Fri 4/1/22	Fri 4/1/22	NA	NA	0%	1907													
1909	➔	Form Roof-Bar-Inspect-Cast- Reg. Mix 3000PSI	5 days	Mon 4/4/22	Fri 4/8/22	NA	NA	0%	1908													
1910	➔	Exterior Frame	50 days	Tue 1/11/22	Mon 3/21/22	NA	NA	0%														
1911	➔	1st Floor- Joist	12 days	Tue 1/11/22	Wed 1/26/22	NA	NA	0%	1869													
1912	➔	2nd Floor to Joist	12 days	Thu 1/27/22	Fri 2/11/22	NA	NA	0%	1911													
1913	➔	3rd floor to Joist	12 days	Mon 2/14/22	Tue 3/1/22	NA	NA	0%	1912													
1914	➔	4th floor to Joist	14 days	Wed 3/2/22	Mon 3/21/22	NA	NA	0%	1913													
1915	➔	Roof Frame-Ext Dry-in	16 days	Tue 3/22/22	Tue 4/12/22	NA	NA	0%														
1916	➔	Set Truss Package	2 days	Tue 3/22/22	Wed 3/23/22	NA	NA	0%	1914													

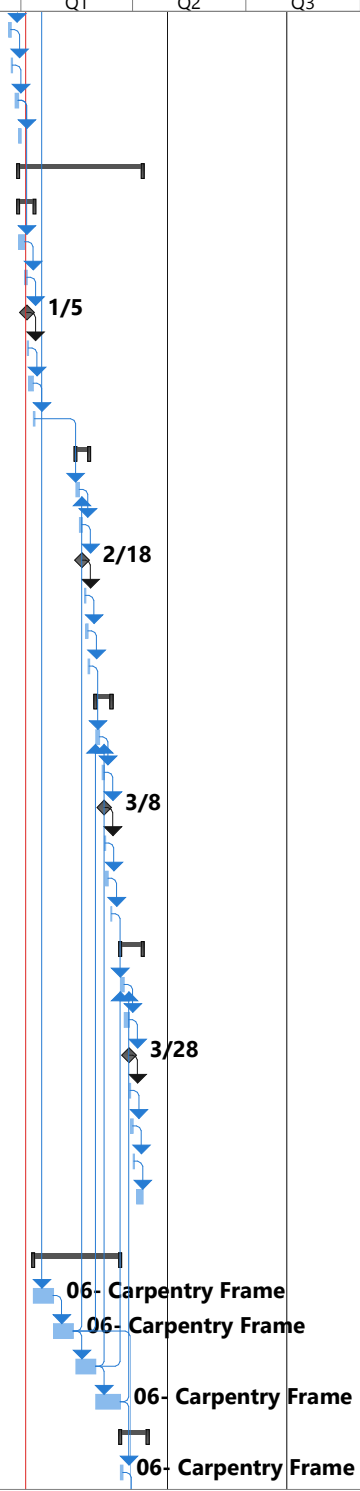


Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Gantt Chart												
										Q4	2021			2022			Q1	Q2	Q3			
1959	➔	Prep/Waterproof 4th Floor	4 days	Thu 6/16/22	Tue 6/21/22	NA	NA	0%	1956													
1960	➔	Cast 4th Floor	2 days	Wed 6/22/22	Thu 6/23/22	NA	NA	0%	1958													
1961	➔	Cast Stair Pans	5 days	Fri 4/29/22	Thu 5/5/22	NA	NA	0%														
1962	➔	Stairwell Front	3 days	Fri 4/29/22	Tue 5/3/22	NA	NA	0%														
1963	➔	1st Through 2nd	1 day	Fri 4/29/22	Fri 4/29/22	NA	NA	0%	1972													
1964	➔	2nd Thru 3rd	1 day	Mon 5/2/22	Mon 5/2/22	NA	NA	0%	1963													
1965	➔	3rd Thru 4th	1 day	Tue 5/3/22	Tue 5/3/22	NA	NA	0%	1964													
1966	➔	Stairwell Rear	3 days	Tue 5/3/22	Thu 5/5/22	NA	NA	0%														
1967	➔	1st Thru 2nd	1 day	Tue 5/3/22	Tue 5/3/22	NA	NA	0%	1964													
1968	➔	2nd Thru 3rd	1 day	Wed 5/4/22	Wed 5/4/22	NA	NA	0%	1967													
1969	➔	3rd Thru 4th	1 day	Thu 5/5/22	Thu 5/5/22	NA	NA	0%	1968													
1970	➔	Misc. Metals	56 days	Tue 4/12/22	Wed 6/29/22	NA	NA	0%														
1971	➔	Lead-Fabrication	0 days	Tue 4/12/22	Tue 4/12/22	NA	NA	0%	1921													
1972	➔	Stairwell 1st thru 4th	12 days	Wed 4/13/22	Thu 4/28/22	NA	NA	0%	1971													
1973	➔	Railing 1st Thru 4th Stairwells	10 days	Mon 5/23/22	Fri 6/3/22	NA	NA	0%	1972,1986													
1974	➔	Railing Balconies 2nd floor	3 days	Thu 5/12/22	Mon 5/16/22	NA	NA	0%	1988													
1975	➔	Railing Balconies 3rd Floor	3 days	Wed 6/22/22	Fri 6/24/22	NA	NA	0%	1958,1974													
1976	➔	Railing Balconies 4th Floor	3 days	Mon 6/27/22	Wed 6/29/22	NA	NA	0%	1975													
1977	➔	Exterior	35 days	Thu 4/7/22	Wed 5/25/22	NA	NA	0%														
1978	➔	Exterior Fascia	5 days	Thu 4/7/22	Wed 4/13/22	NA	NA	0%	1919													
1979	➔	Set Exterior Stucco Band	4 days	Thu 4/14/22	Tue 4/19/22	NA	NA	0%	1978													
1980	➔	Roof	8 days	Wed 4/20/22	Fri 4/29/22	NA	NA	0%	1979													
1981	➔	Install Exterior Doors- Temp Lock	6 days	Thu 4/14/22	Thu 4/21/22	NA	NA	0%	1978													
1982	➔	Install Back Wall j-Molding	4 days	Thu 4/14/22	Tue 4/19/22	NA	NA	0%	1978													
1983	➔	Exterior Styrofoam Inserts	3 days	Wed 4/20/22	Fri 4/22/22	NA	NA	0%	1982													
1984	➔	Exterior Lathe -Stucco-	21 days	Thu 4/14/22	Thu 5/12/22	NA	NA	0%	1978													
1985	➔	Exterior Veneer	10 days	Thu 4/14/22	Wed 4/27/22	NA	NA	0%	1978													
1986	➔	Install Exterior Alum Soffit	6 days	Fri 5/13/22	Fri 5/20/22	NA	NA	0%	1984													
1987	➔	Prime and First Coat of Paint - Exterior	5 days	Thu 4/28/22	Wed 5/4/22	NA	NA	0%	1985													
1988	➔	Final Paint - Exterior	5 days	Thu 5/5/22	Wed 5/11/22	NA	NA	0%	1987													
1989	➔	Exterior Railing	2 days	Thu 5/12/22	Fri 5/13/22	NA	NA	0%	1988													
1990	➔	Temp Power	0 days	Wed 5/25/22	Wed 5/25/22	NA	NA	0%	826,1998													
1991	➔	Cast Exterior Sidewalks	8 days	Wed 4/20/22	Fri 4/29/22	NA	NA	0%	1979,1984SS													
1992	➔	Interior Finishes	100 days	Thu 4/14/22	Wed 8/31/22	NA	NA	0%														
1993	➔	Insulation and Inspection	27 days	Thu 4/14/22	Fri 5/20/22	NA	NA	0%														
1994	➔	1st Floor Insulation-Inspection	3 days	Thu 4/14/22	Mon 4/18/22	NA	NA	0%	1932,1980SS-5 da													
1995	➔	2nd floor Insulation/ Inspection	3 days	Tue 4/26/22	Thu 4/28/22	NA	NA	0%	1933,1994													
1996	➔	3rd Floor Insulation/ Inspection	3 days	Fri 5/6/22	Tue 5/10/22	NA	NA	0%	1935,1995													
1997	➔	4th Floor Insulation/ Inspection	3 days	Wed 5/18/22	Fri 5/20/22	NA	NA	0%	1937,1996													
1998	➔	Interior Zip-Hallway 1st thru 3rd	3 days	Mon 5/23/22	Wed 5/25/22	NA	NA	0%	1993													
1999	➔	Interior Stucco/Plaster over lathe- Hallway 1st Thru 3rd	5 days	Thu 5/26/22	Wed 6/1/22	NA	NA	0%	1998													

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3
2084	➔	3rd Floor	4 days	Thu 7/28/22	Tue 8/2/22	NA	NA	0%									
2085	➔	Specialties-DIV 10	4 days	Thu 7/28/22	Tue 8/2/22	NA	NA	0%	2064								
2086	➔	4th Floor	4 days	Wed 8/3/22	Mon 8/8/22	NA	NA	0%									
2087	➔	Specialties-DIV 10	4 days	Wed 8/3/22	Mon 8/8/22	NA	NA	0%	2085								
2088	➔	Punch Walk Thru	5 days	Wed 8/3/22	Tue 8/9/22	NA	NA	0%									
2089	➔	Final Inspection-Building-Fire	3 days	Wed 8/3/22	Fri 8/5/22	NA	NA	0%	2085								
2090	➔	Owner/A-E	2 days	Mon 8/8/22	Tue 8/9/22	NA	NA	0%	2089								
2091	➔	Inspections	0 days	Wed 7/27/22	Wed 7/27/22	NA	NA	0%									
2092	➔	Final Inspections	0 days	Wed 7/27/22	Wed 7/27/22	NA	NA	0%	2083								
2093	➔	Punch Out and Clean	23 days	Wed 8/10/22	Fri 9/9/22	NA	NA	0%									
2094	➔	1st Floor	5 days	Wed 8/10/22	Tue 8/16/22	NA	NA	0%									
2095	➔	Punch and Clean	5 days	Wed 8/10/22	Tue 8/16/22	NA	NA	0%	2089,2090								
2096	➔	2nd Floor	5 days	Wed 8/17/22	Tue 8/23/22	NA	NA	0%									
2097	➔	Punch and Clean	5 days	Wed 8/17/22	Tue 8/23/22	NA	NA	0%	2095								
2098	➔	3rd Floor	5 days	Wed 8/24/22	Tue 8/30/22	NA	NA	0%									
2099	➔	Punch and Clean	5 days	Wed 8/24/22	Tue 8/30/22	NA	NA	0%	2097								
2100	➔	4th Floor	8 days	Wed 8/31/22	Fri 9/9/22	NA	NA	0%									
2101	➔	Punch and Clean	8 days	Wed 8/31/22	Fri 9/9/22	NA	NA	0%	2099								
2102	➔	Apartment Building Two	202 days	Wed 1/5/22	Thu 10/13/22	NA	NA	0%									
2103	➔	Survey Pad	1 day	Wed 1/5/22	Wed 1/5/22	NA	NA	0%	659,662SS+75 day								
2104	➔	Concrete- SOG	29 days	Thu 1/6/22	Tue 2/15/22	NA	NA	0%									
2105	➔	Batter Boards	2 days	Thu 1/6/22	Fri 1/7/22	NA	NA	0%	2103								
2106	➔	Form SOG	5 days	Mon 1/10/22	Fri 1/14/22	NA	NA	0%	2105								
2107	➔	Final Grade +/- .10	1 day	Mon 1/17/22	Mon 1/17/22	NA	NA	0%	2106								
2108	➔	MEP Underground Rough	14 days	Tue 1/18/22	Fri 2/4/22	NA	NA	0%	2107								
2109	➔	Inspection mep Undgrd	0 days	Fri 2/4/22	Fri 2/4/22	NA	NA	0%	2108								
2110	➔	Treat, Reinforce, Inspect, and Pour SOG	5 days	Mon 2/7/22	Fri 2/11/22	NA	NA	0%	2109								
2111	➔	Curing Compound/Cut Slab	1 day	Mon 2/14/22	Mon 2/14/22	NA	NA	0%	2110								
2112	➔	Strip and Clean	1 day	Tue 2/15/22	Tue 2/15/22	NA	NA	0%	2111								
2113	➔	Elevator Pit	12 days	Thu 1/6/22	Fri 1/21/22	NA	NA	0%									
2114	➔	Excavate	1 day	Thu 1/6/22	Thu 1/6/22	NA	NA	0%	2103								
2115	➔	Set Sump Roughin	1 day	Fri 1/7/22	Fri 1/7/22	NA	NA	0%	2114								
2116	➔	Set Bar- Inspect- Cast Slab	2 days	Mon 1/10/22	Tue 1/11/22	NA	NA	0%	2115								
2117	➔	Set Form Walls	2 days	Wed 1/12/22	Thu 1/13/22	NA	NA	0%	2116								
2118	➔	Roughin E&P Walls	1 day	Fri 1/14/22	Fri 1/14/22	NA	NA	0%	2117								
2119	➔	Set Bar- Inspect-Pour	3 days	Mon 1/17/22	Wed 1/19/22	NA	NA	0%	2118								
2120	➔	Strip-Backfill-	2 days	Thu 1/20/22	Fri 1/21/22	NA	NA	0%	2119								
2121	➔	CMU Elevator Shaft	81 days	Thu 1/20/22	Thu 5/12/22	NA	NA	0%									
2122	➔	1st Floor	9 days	Thu 1/20/22	Tue 2/1/22	NA	NA	0%									
2123	➔	CMU through Bond Beam	3 days	Thu 1/20/22	Mon 1/24/22	NA	NA	0%	2119								
2124	➔	Bar and Inspect Pads	2 days	Tue 1/25/22	Wed 1/26/22	NA	NA	0%	2123								
2125	➔	Inspect	0 days	Wed 1/26/22	Wed 1/26/22	NA	NA	0%	2124								

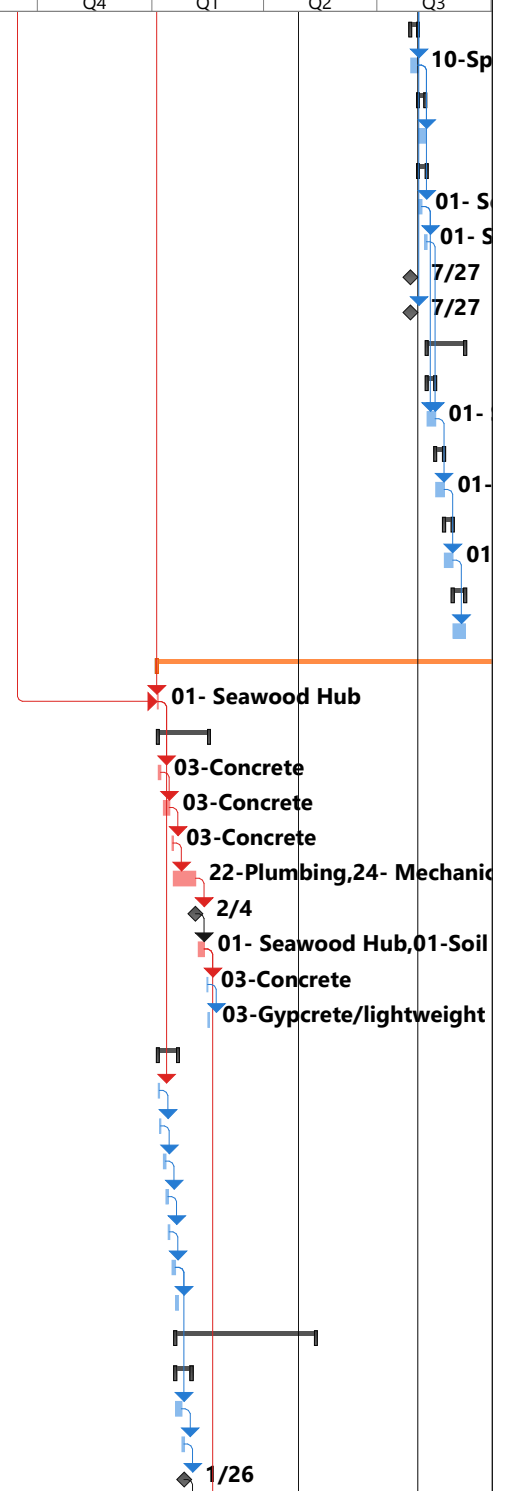

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			


ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Timeline													
										Q4	2021			2022				Q3					
2126	➔	Cast-Grout Mix 300psi	1 day	Thu 1/27/22	Thu 1/27/22	NA	NA	0%	2125														
2127	➔	Bond Beam Set-Bar-Inspect	2 days	Fri 1/28/22	Mon 1/31/22	NA	NA	0%	2126														
2128	➔	Cast Bond Beam	1 day	Tue 2/1/22	Tue 2/1/22	NA	NA	0%	2127														
2129	➔	2nd Floor	9 days	Fri 3/18/22	Wed 3/30/22	NA	NA	0%															
2130	➔	CMU through Bond Beam	3 days	Fri 3/18/22	Tue 3/22/22	NA	NA	0%	2128,2153														
2131	➔	Bar and Inspect Pads	2 days	Wed 3/23/22	Thu 3/24/22	NA	NA	0%	2130														
2132	➔	Inspect	0 days	Thu 3/24/22	Thu 3/24/22	NA	NA	0%	2131														
2133	➔	Cast-Grout Mix 300psi	1 day	Fri 3/25/22	Fri 3/25/22	NA	NA	0%	2132														
2134	➔	Bond Beam Set-Bar-Inspect	2 days	Mon 3/28/22	Tue 3/29/22	NA	NA	0%	2133														
2135	➔	Cast Bond Beam	1 day	Wed 3/30/22	Wed 3/30/22	NA	NA	0%	2134														
2136	➔	3rd Floor	9 days	Tue 4/5/22	Fri 4/15/22	NA	NA	0%															
2137	➔	CMU through Bond Beam	3 days	Tue 4/5/22	Thu 4/7/22	NA	NA	0%	2135,2153,2154														
2138	➔	Bar and Inspect Pads	2 days	Fri 4/8/22	Mon 4/11/22	NA	NA	0%	2137														
2139	➔	Inspect	0 days	Mon 4/11/22	Mon 4/11/22	NA	NA	0%	2138														
2140	➔	Cast-Grout Mix 300psi	1 day	Tue 4/12/22	Tue 4/12/22	NA	NA	0%	2139														
2141	➔	Bond Beam Set-Bar-Inspect	2 days	Wed 4/13/22	Thu 4/14/22	NA	NA	0%	2140														
2142	➔	Cast Bond Beam	1 day	Fri 4/15/22	Fri 4/15/22	NA	NA	0%	2141														
2143	➔	4th Floor-Thru Rooftop	14 days	Mon 4/25/22	Thu 5/12/22	NA	NA	0%															
2144	➔	CMU through Bond Beam	3 days	Mon 4/25/22	Wed 4/27/22	NA	NA	0%	2142,2154,2155														
2145	➔	Bar and Inspect Pads	2 days	Thu 4/28/22	Fri 4/29/22	NA	NA	0%	2144														
2146	➔	Inspect	0 days	Fri 4/29/22	Fri 4/29/22	NA	NA	0%	2145														
2147	➔	Cast-Grout Mix 300psi	1 day	Mon 5/2/22	Mon 5/2/22	NA	NA	0%	2146														
2148	➔	Bond Beam Set-Bar-Inspect	2 days	Tue 5/3/22	Wed 5/4/22	NA	NA	0%	2147														
2149	➔	Cast Bond Beam	1 day	Thu 5/5/22	Thu 5/5/22	NA	NA	0%	2148														
2150	➔	Form Roof-Bar-Inspect-Cast- Reg. Mix 3000PSI	5 days	Fri 5/6/22	Thu 5/12/22	NA	NA	0%	2149														
2151	➔	Exterior Frame	50 days	Mon 2/14/22	Fri 4/22/22	NA	NA	0%															
2152	➔	1st Floor- Joist	12 days	Mon 2/14/22	Tue 3/1/22	NA	NA	0%	2110														
2153	➔	2nd Floor to Joist	12 days	Wed 3/2/22	Thu 3/17/22	NA	NA	0%	2152														
2154	➔	3rd floor to Joist	12 days	Fri 3/18/22	Mon 4/4/22	NA	NA	0%	2153														
2155	➔	4th floor to Joist	14 days	Tue 4/5/22	Fri 4/22/22	NA	NA	0%	2154														
2156	➔	Roof Frame-Ext Dry-in	16 days	Mon 4/25/22	Mon 5/16/22	NA	NA	0%															
2157	➔	Set Truss Package	2 days	Mon 4/25/22	Tue 4/26/22	NA	NA	0%	2155														
2158	➔	Frame Roof	4 days	Wed 4/27/22	Mon 5/2/22	NA	NA	0%	2157														
2159	➔	Sheath Roof	4 days	Tue 5/3/22	Fri 5/6/22	NA	NA	0%	2158														
2160	➔	Dry-In Roof	2 days	Mon 5/9/22	Tue 5/10/22	NA	NA	0%	2159														
2161	➔	Tape and Seal Zip	4 days	Wed 5/11/22	Mon 5/16/22	NA	NA	0%	2160														
2162	➔	Install Windows	4 days	Wed 5/11/22	Mon 5/16/22	NA	NA	0%	2160														
2163	➔	Inspect Engineering with Tie-down and Sheathing	0 days	Tue 5/10/22	Tue 5/10/22	NA	NA	0%	2160														
2164	➔	Interior Framing - Walls & Ceilings	48 days	Mon 5/2/22	Thu 7/7/22	NA	NA	0%	2158														
2165	➔	1st Floor	12 days	Tue 5/3/22	Wed 5/18/22	NA	NA	0%	2153														
2166	➔	2nd Floor	12 days	Thu 5/19/22	Fri 6/3/22	NA	NA	0%	2165														

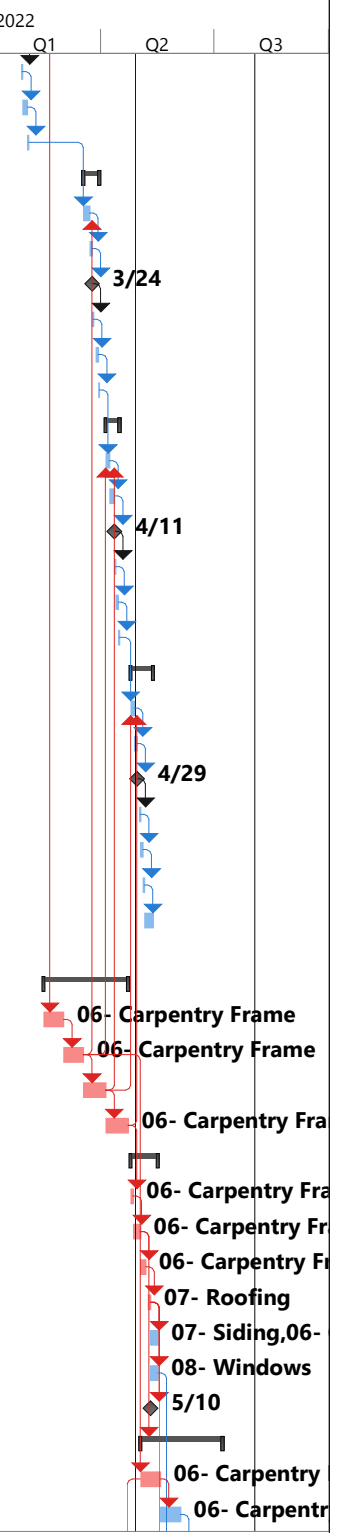

Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Q4	2021 Q1	Q2	Q3	Q4	2022 Q1	Q2	Q3
2292	➔	Install Door Hardware	4 days	Tue 7/12/22	Fri 7/15/22	NA	NA	0%	2266								
2293	➔	2nd Floor	4 days	Fri 8/19/22	Wed 8/24/22	NA	NA	0%									
2294	➔	Install Door Hardware	4 days	Fri 8/19/22	Wed 8/24/22	NA	NA	0%	2269								
2295	➔	3rd Floor	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%									
2296	➔	Install Door Hardware	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%	2272								
2297	➔	4th Floor	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%									
2298	➔	Install Door Hardware	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%	2296								
2299	➔	MEP Trim	40 days	Tue 7/12/22	Mon 9/5/22	NA	NA	0%									
2300	➔	1st Floor	4 days	Tue 7/12/22	Fri 7/15/22	NA	NA	0%									
2301	➔	MEP Trim	4 days	Tue 7/12/22	Fri 7/15/22	NA	NA	0%	2266								
2302	➔	2nd Floor	4 days	Fri 8/19/22	Wed 8/24/22	NA	NA	0%									
2303	➔	MEP Trim	4 days	Fri 8/19/22	Wed 8/24/22	NA	NA	0%	2269								
2304	➔	3rd Floor	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%									
2305	➔	MEP Trim	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%	2272								
2306	➔	4th Floor	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%									
2307	➔	MEP Trim	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%	2305								
2308	➔	MEPF Inspections	25 days	Wed 8/31/22	Tue 10/4/22	NA	NA	0%									
2309	➔	Final MEP Inspections	21 days	Wed 8/31/22	Wed 9/28/22	NA	NA	0%	2301,2305								
2310	➔	Equipment start up	4 days	Thu 9/29/22	Tue 10/4/22	NA	NA	0%	2309								
2311	➔	Install Flooring/Tile/LVT	40 days	Mon 7/18/22	Fri 9/9/22	NA	NA	0%									
2312	➔	1st Floor	4 days	Mon 7/18/22	Thu 7/21/22	NA	NA	0%									
2313	➔	Flooring	4 days	Mon 7/18/22	Thu 7/21/22	NA	NA	0%	2301								
2314	➔	2nd Floor	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%									
2315	➔	Flooring	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%	2303								
2316	➔	3rd Floor	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%									
2317	➔	Flooring	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%	2305								
2318	➔	4th Floor	4 days	Tue 9/6/22	Fri 9/9/22	NA	NA	0%									
2319	➔	Flooring	4 days	Tue 9/6/22	Fri 9/9/22	NA	NA	0%	2317								
2320	➔	Bath Accessories	40 days	Mon 7/18/22	Fri 9/9/22	NA	NA	0%									
2321	➔	1st Floor	4 days	Mon 7/18/22	Thu 7/21/22	NA	NA	0%									
2322	➔	Specialties-DIV 10	4 days	Mon 7/18/22	Thu 7/21/22	NA	NA	0%	2301								
2323	➔	2nd Floor	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%									
2324	➔	Specialties-DIV 10	4 days	Thu 8/25/22	Tue 8/30/22	NA	NA	0%	2303								
2325	➔	3rd Floor	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%									
2326	➔	Specialties-DIV 10	4 days	Wed 8/31/22	Mon 9/5/22	NA	NA	0%	2305								
2327	➔	4th Floor	4 days	Tue 9/6/22	Fri 9/9/22	NA	NA	0%									
2328	➔	Specialties-DIV 10	4 days	Tue 9/6/22	Fri 9/9/22	NA	NA	0%	2326								
2329	➔	Punch Walk Thru	5 days	Tue 9/6/22	Mon 9/12/22	NA	NA	0%									
2330	➔	Final Inspection-Building-Fire	3 days	Tue 9/6/22	Thu 9/8/22	NA	NA	0%	2326								
2331	➔	Owner/A-E	2 days	Fri 9/9/22	Mon 9/12/22	NA	NA	0%	2330								
2332	➔	Inspections	0 days	Tue 8/30/22	Tue 8/30/22	NA	NA	0%									
2333	➔	Final Inspections	0 days	Tue 8/30/22	Tue 8/30/22	NA	NA	0%	2324								



Project Update- 12-3-20
Project Start 1-4-21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	% Work Complete	Predecessors	Gantt Chart											
										Q4	2021			2022			Q3				
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
2334	➔	Punch Out and Clean	23 days	Tue 9/13/22	Thu 10/13/22	NA	NA	0%													
2335	➔	1st Floor	5 days	Tue 9/13/22	Mon 9/19/22	NA	NA	0%													
2336	➔	Punch and Clean	5 days	Tue 9/13/22	Mon 9/19/22	NA	NA	0%	2330,2331												
2337	➔	2nd Floor	5 days	Tue 9/20/22	Mon 9/26/22	NA	NA	0%													
2338	➔	Punch and Clean	5 days	Tue 9/20/22	Mon 9/26/22	NA	NA	0%	2336												
2339	➔	3rd Floor	5 days	Tue 9/27/22	Mon 10/3/22	NA	NA	0%													
2340	➔	Punch and Clean	5 days	Tue 9/27/22	Mon 10/3/22	NA	NA	0%	2338												
2341	➔	4th Floor	8 days	Tue 10/4/22	Thu 10/13/22	NA	NA	0%													
2342	➔	Punch and Clean	8 days	Tue 10/4/22	Thu 10/13/22	NA	NA	0%	2340												
2343	➔	FF&E	140 days	Fri 4/22/22	Thu 11/3/22	NA	NA	0%													
2344	➔	Appliance Package Set Bldg. 6-3	15 days	Fri 4/22/22	Thu 5/12/22	NA	NA	0%	1138												
2345	➔	Appliance Package Set Bldg. 4-1	15 days	Wed 7/27/22	Tue 8/16/22	NA	NA	0%	1620												
2346	➔	Appliance Package Set Bldg. 2-5	15 days	Fri 10/14/22	Thu 11/3/22	NA	NA	0%	2102												
2347	➔	Project Close	0 days	Thu 11/3/22	Thu 11/3/22	NA	NA	0%													
2348	➔	Final Site-Building JHA	0 days	Thu 11/3/22	Thu 11/3/22	NA	NA	0%	2102,2346												
2349	➔	Project Completion	0 days	Thu 11/3/22	Thu 11/3/22	NA	NA	0%	2348												

01- Seawood H

Project Update- 12-3-20 Project Start 1-4-21	Task		Inactive Task		Manual Summary Rollup		External Milestone		Critical	
	Split		Inactive Milestone		Manual Summary		Deadline		Critical Split	
	Milestone		Inactive Summary		Start-only		Path Driving Predecessor Milestone Task		Progress	
	Summary		Manual Task		Finish-only		Path Driving Predecessor Summary Task		Manual Progress	
	Project Summary		Duration-only		External Tasks		Path Driving Predecessor Normal Task			
